

Status of Bond Projects

8/14/2018 Governing Board Meeting

President Day, Vice President Cox Golder, Board Members and Superintendent Jaeger it is my pleasure to provide you with an update of the projects being completed with bond funding.

Amphitheater High:

**Switchgear damaged during shipping being repaired, no schedule
\$119,717**

**Panther Hall Renovations, sheet rock completed, hanging decorative
“Cloud” ceiling grid, HVAC replacement completed, lighting in
progress and flooring started Aug 6th \$973,122**



Canyon Del Oro:

ADA compliance and drainage issue at bldg. G continues, all concrete has been installed, final grade in progress \$22,643

Buildings T & M - HVAC restoration is completed \$186,185

Parking Lot ADA striping is completed

Slurry seal of Administration driveway scheduled for Aug 7th \$6,143



Ironwood Ridge:


Painting of light poles, fixtures, gates, rails, stair railings and risers being scheduled for quotes

Intercom & PA systems upgrade – complete \$60,000

**New signs and directions for parent drop-off to be installed Aug 6th
Parent drop-off being moved to outside lanes of west parking lot \$6,374**

AMS

**HVAC replacement - Bldgs 400, 500, 600, 700 wings are completed
\$258, 068**

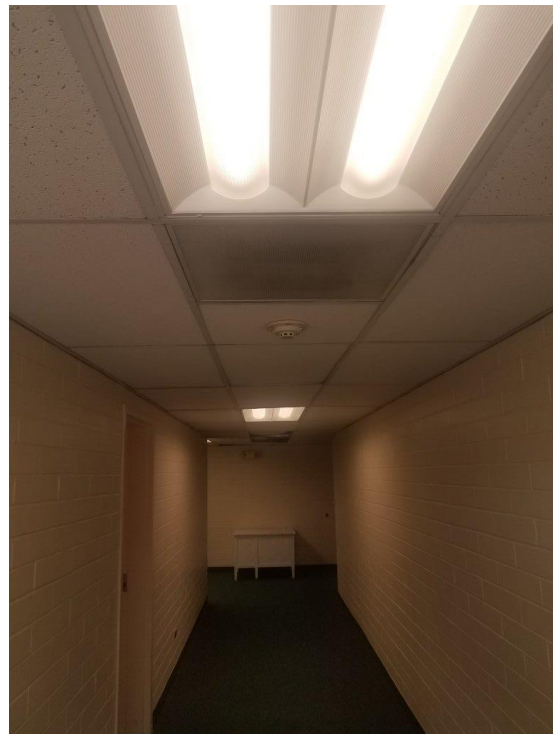

Copper Creek

Boiler replacement and mech. room upgrades, pre-con meeting held July 3rd, waiting on ship date to schedule \$100,281

K-3 playground equipment installation completed \$34,000



Coronado

Campus weatherproofing - painting MPR, Elementary wing, gym and cafeteria completed on Aug 3rd

Cross

HVAC Renovations for wrestling gym in design phase, roof repairs to be done at the same time as removal of swamp coolers

MPR flooring demo and abatement complete, flooring installation complete, new operable wall in MPR await delivery \$64,662



Donaldson

MPR HVAC has been completed \$68,884

Harelson

Redesign of bus loop and parent drop-off area postponed

Holaway

New clocks, bells and P.A. system installed \$74,000

La Cima

Renovate MPR - replace daylighting assembly, paint walls and replace VCT flooring – complete \$82,649

Mesa Verde

Site improvements to include adding 2 panic gates between Buildings A & F, aluminum awning between office and room 13, replace water fountain and other improvements awarded, awaiting scheduling \$67,646

Nash

Replace clocks, bells and P.A. system – completed Aug 3rd \$72,000

Painted Sky

Create 3 Pre-K classrooms: new playground equipment, curb, sidewalk, gate and awning – completed \$41,680



Prince

HVAC Bldgs CN, CW, CE scheduling delayed due to completion risk - rescheduled for winter/summer break \$258,068

Rillito

Interior renovations in Bldg. D 600 classrooms awarded and awaits scheduling \$57,312

Rio Vista

Lighting materials survey and budget received, project out for bid

Site requests to include: outdoor basketball court repair under review, removal of 4 dead trees being scheduled for summer

Walker

Electrostatic painting of railings and fencing completed, exterior painting of cafeteria, Administration building, and pre-school building completed \$23,007



Wilson

HVAC updates are complete \$62,598

Bus Loop construction is complete

Bond Funds \$47,876.32

Adjacent Ways \$49,996



**** SOMETHING NEW AT EVERY SCHOOL, EVERY YEAR! ****
