

DUNCANVILLE ISD

BOND
2023



Bond Updates

July 21, 2025



Huckabee
MORE THAN ARCHITECTS






Agenda

- **Welcome and Leadership Message**
- **Project Packages**
- **Bond Program Schedule**
- **Project Updates**
 - WRA
 - Huckabee
- **Closing**

Project Packages



WRA Architects

\$43M (approximate)

Package 1

Daniel ES, Hardin ES, Byrd MS, Kennemer MS,
& Reed MS **(Construction)**

Package 2

Alexander ES, Bilhartz ES, Fairmeadows ES,
Hyman ES, & Merrifield ES **(Construction)**

Package 3

Alexander ES & Fairmeadows ES (HVAC
Package) **(100% Complete)**

Package 4

Central **(Bidding)**

Package 5


Brandenburg **(Design)**

Packages 6

Idea Hub, Nutrition, PACE, Plaza, Summit,
Trans/Maint, Warehouse **(Design)**



Project Packages



Huckabee

\$61M (approximate)

Package 7

Smith (Bidding)

Package 8

Duncanville High School

CTE Addition & Area "M" Renovations (Construction)


Area "J" Renovations (Bidding)



Huckabee
MORE THAN ARCHITECTS



Bond Program Schedule

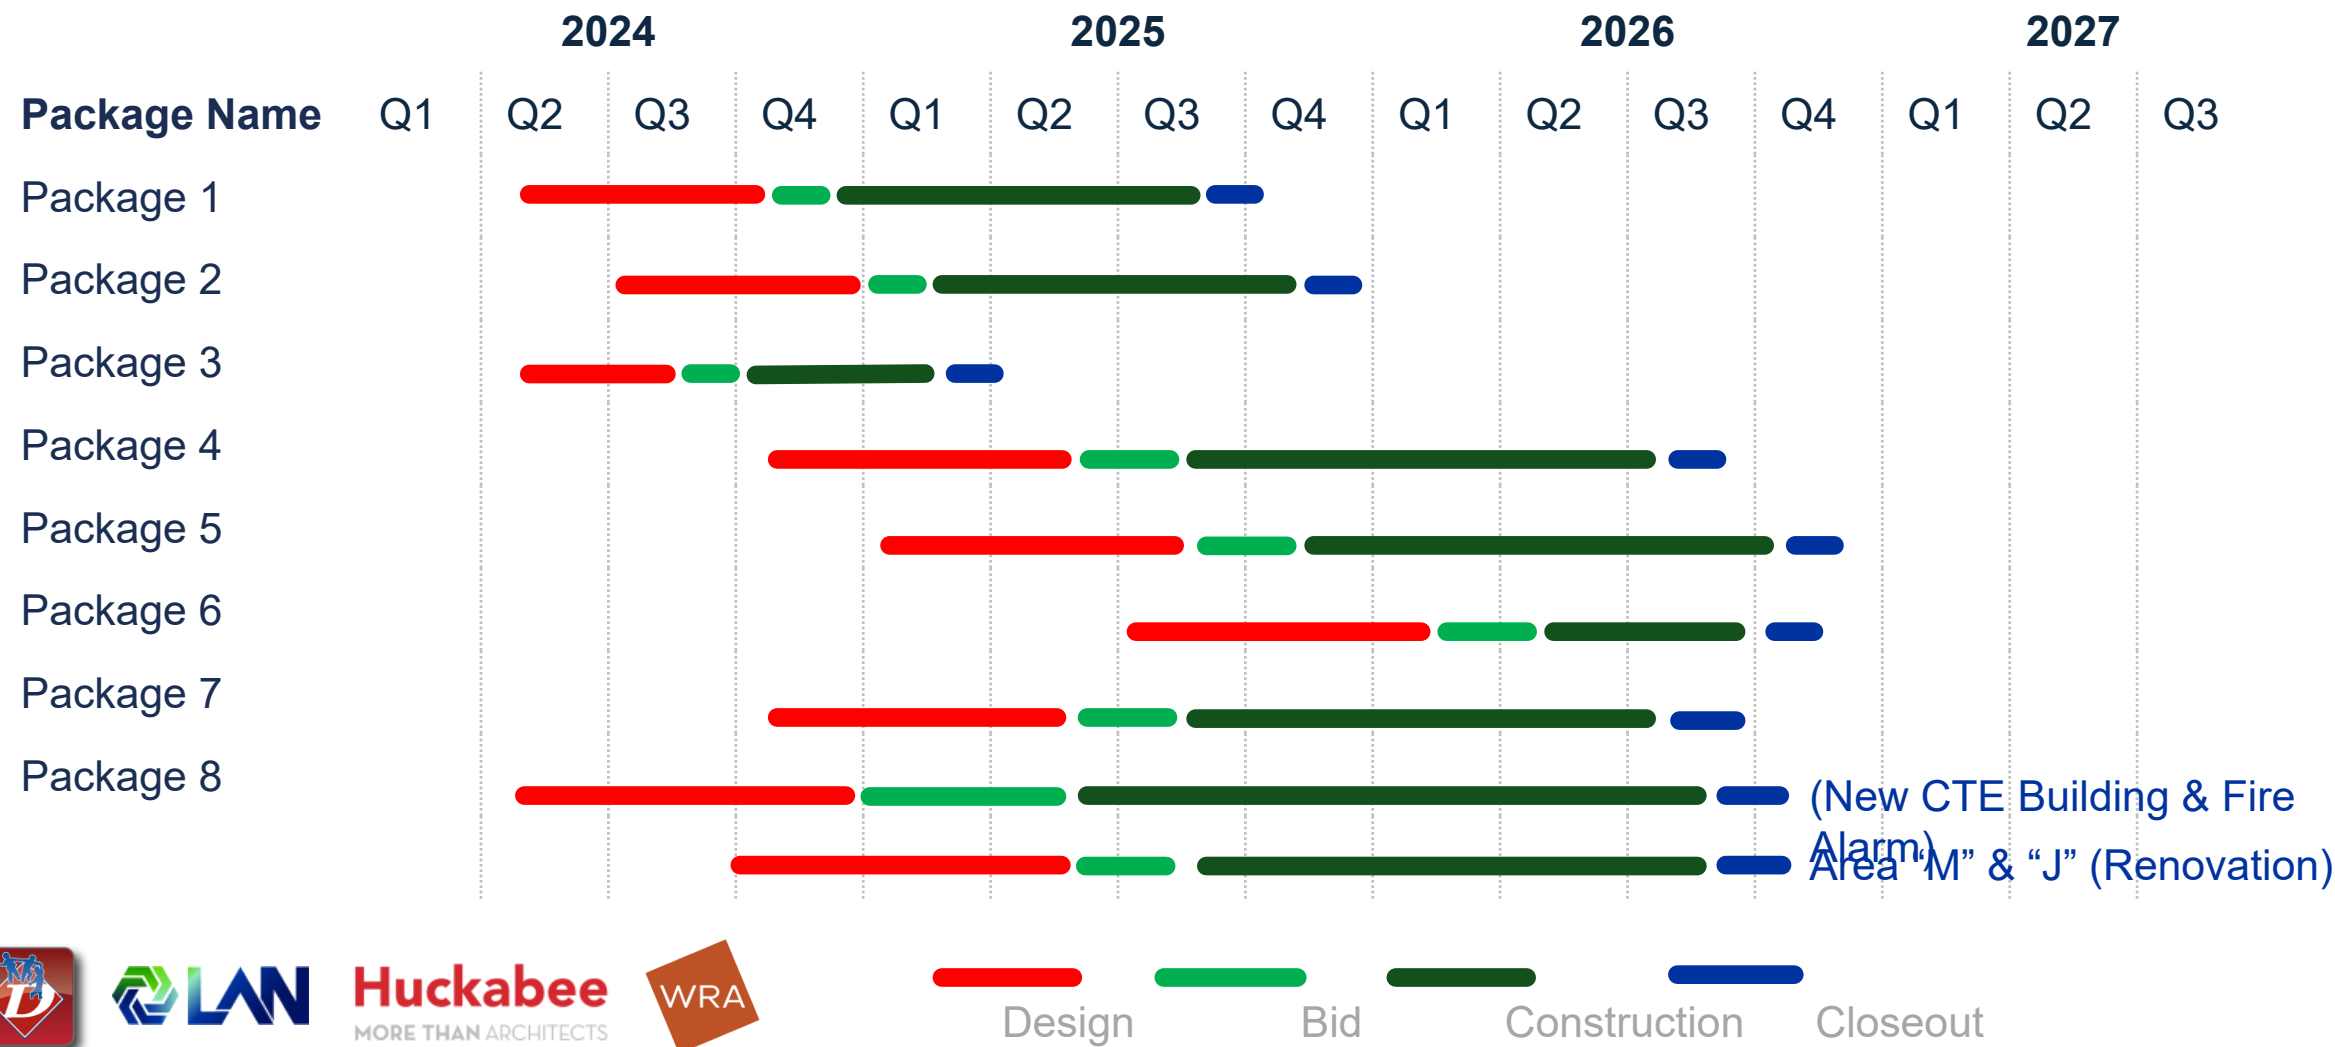

H. BOB DANIEL ELEMENTARY SCHOOL

- Exterior door renovations



- Corridor renovations



GLENN C. HARDIN ELEMENTARY SCHOOL

- Exterior door renovations



- Corridor renovations



BYRD MIDDLE SCHOOL



- Restroom renovations



- Library renovations



REED MIDDLE SCHOOL

- Restroom renovations




- Classroom renovations



KENNEMER MIDDLE SCHOOL



- Restroom renovations

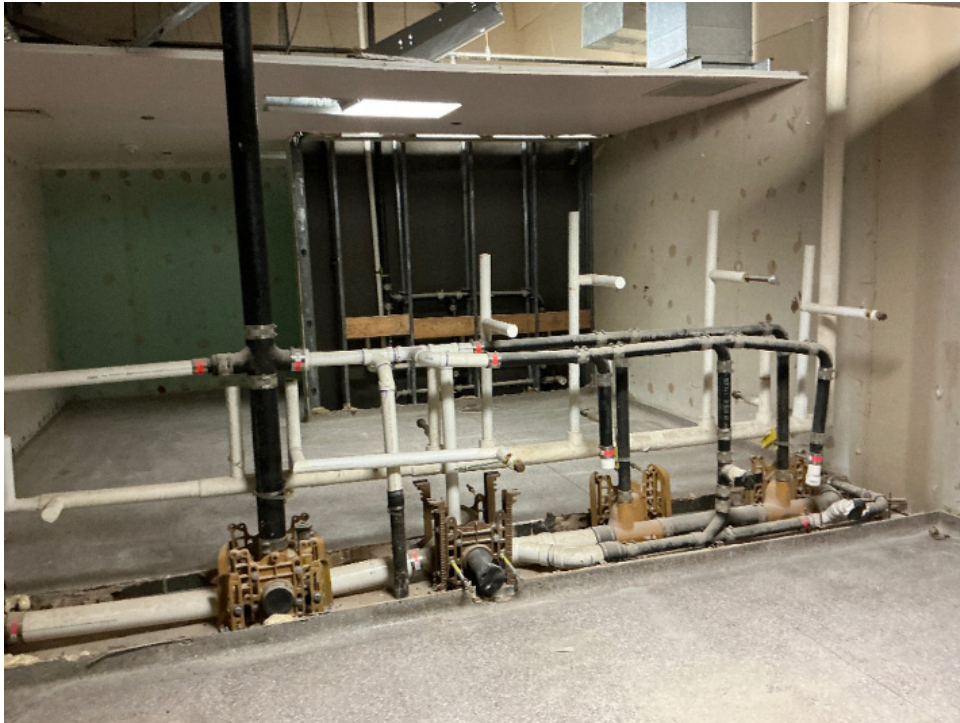

- Exterior renovations



ALEXANDER ELEMENTARY SCHOOL


- Classroom renovations



- Restroom renovations



BILHARTZ ELEMENTARY SCHOOL



- Music Room renovations



- Classroom renovations



FAIRMEADOWS ELEMENTARY SCHOOL

- Administration renovations



- Restroom renovations



HYMAN ELEMENTARY SCHOOL

- Exterior renovations



- Classroom renovations



MERRIFIELD ELEMENTARY SCHOOL


- Administration renovations



- Restroom renovations




DUNCANVILLE HIGH SCHOOL CTE ADDITION



Huckabee
MORE THAN ARCHITECTS

DUNCANVILLE HIGH SCHOOL CTE ADDITION



Huckabee
MORE THAN ARCHITECTS

DUNCANVILLE HIGH SCHOOL AREA "M" RENOVATIONS




Huckabee
MORE THAN ARCHITECTS


DUNCANVILLE HIGH SCHOOL AREA "M" RENOVATIONS



Huckabee
MORE THAN ARCHITECTS

DUNCANVILLE HIGH SCHOOL PORTABLE COMPLEX






Other Updates:

- **Duncanville HS – Portable Complex**
 - Relocation of existing portables in Duncanville ISD in progress and scheduled to be completed in August 2025
- **Central Elementary Fine Arts Academy**
 - Construction scheduled to start August 2025
- **Clint Q. Smith Early Learning Academy**
 - Bid Opening July 2025
 - Construction scheduled to start September 2025





Questions & Comments

