

Status of Bond Projects  
6/19/12 Governing Board Meeting


President Boros, Board Members, Dr. Balentine,  
Current Project Update:

**I. HEALTH, SAFETY, AND SECURITY**

**A. Transportation Offices:**

Construction is 95% complete.

The new transportation and food service offices are complete and occupied. The realignment of the bus yard is underway with trenching for electrical and new light poles being installed. The lot will be slurry sealed and restriped July 2 through July 5. This project is ahead of schedule and on budget.

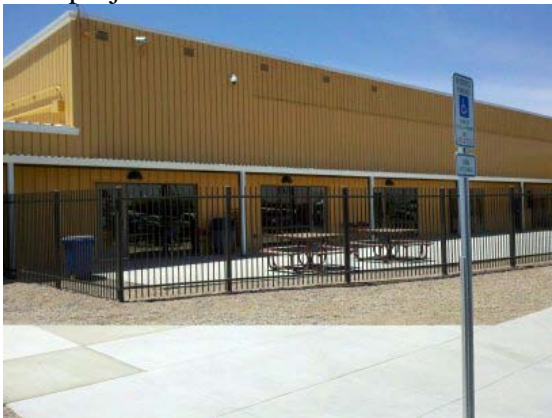

Transportation Front Elevation



Transportation Main Lobby



Transportation Driver's Lounge



Transportation Driver's Training Room

B. Wetmore Parking Re-capture:  
Construction is complete.



Wetmore New Sign, Flagpole, and Parking Spaces

## **II. INSTRUCTIONAL SPACE / PORTABLE REPLACEMENT**

### A. Amphitheater Middle School Addition / Remodel:

Programming is continuing with the AMS staff, Architects, General Contractor, and the Bond Dept. Construction Documents are 90% complete and being reviewed by Amphi Bond Dept, Amphi Tech Dept, and Amphi FSS Staff for accuracy as well as being priced by the contractor for preparation of a GMP (guaranteed maximum price).

### B. Canyon Del Oro High School Addition / Remodel:

Construction is 12% complete.

The MPR and kitchen are demo'd and being renovated for use in the fall semester.

Framing, rough electric and rough HVAC are complete in both areas. Rough plumbing is in process and the kitchen roof is currently being replaced.

The administration building is also demo'd and being renovated for use in the fall semester. Framing is complete and rough electric and rough HVAC are in process.

Restrooms campus wide are being renovated for ADA compliance as well as new restroom installation at building J-3 and the south gym.

Building C (culinary arts classroom and IDP program) has started. Footers are dug and underground MP&E has started.

Campus re-cabling is in process with trenching going on throughout inner campus for installation of IT and electrical conduit as well as re-cabling in classrooms in buildings K, T, R, N, F, A, and MPR.

Inner campus security fence is being manufactured while posts are being installed on site. CDO project is on schedule and on budget.



CDO MPR Renovation – West Wall



CDO MPR Renovation – North Wall



CDO Kitchen Roof Replacement



CDO Kitchen Renovation - framing




CDO Admin Renovation – framing



CDO New South Gym Restroom Site Prep



CDO "C" Building Site Prep

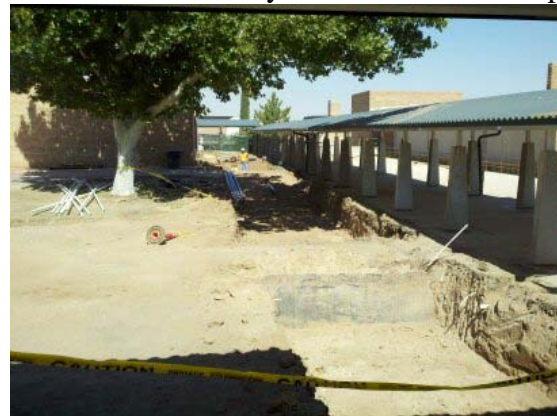

CDO Inner Campus Trenching for Re-Cabling



C. Canyon Del Oro Stadium Renovation: The stadium renovation work is 25% complete. The track has been removed, the field has been re-crowned, new soil amendments are in place, irrigation head replacement is complete, the light poles and home bleachers are repainted, and the inner and outer curbs around the track have been replaced. Sod is scheduled to be installed the last week of June and the track replacement will begin once sod is installed.

The stadium repair project is on schedule and on budget.



CDO Track Demolition



CDO Track Replacement and Field Re-crown

D. Copper Creek Classroom Renovation / IT Re-cabling: Construction is 80% complete. The renovation of classrooms 14 & 15 into computer labs and IDF #1 will be complete this week. All classroom accordion walls have been replaced. All above ceiling backbone cabling is complete. Surface mount raceway installation in classrooms, IDF's #2, #3, and #5 racking, relocation of the phone PBX, and admin re-cabling are in process.

Copper Creek re-cabling project is ahead of schedule and on budget.



Copper Creek Accordion Wall Replacement



Copper Creek IDF Rack Installation



Copper Creek Electrical Upgrades and PBX Relocation

E. Amphitheater High Renovations:

Programming is continuing with the AHS staff, Architects, General Contractor, and the Bond Dept.

F. Holaway Elementary Classroom Addition:

Programming has started with the Holaway staff, Architects, General Contractor, Amphi Tech Dept, and the Bond Dept.

G. Rio Vista Elementary Classroom Addition:

Programming has started with the Rio Vista staff, Architects, General Contractor, and the Bond Dept.

H. Nash Elementary Library Renovation:

Procurement of A&E services is under way.

**III. TRANSPORTATION**

4 full size and 16 smaller size busses are on order and are expected to ship to the district this month.
