

STATUS OF BUILDING PROJECTS SUMMER 2017 and GENERAL MAINTENANCE ITEMS



*Lead Water testing will take place the 3rd week of August for all sites. *

SUMMER 2017 PROJECTS – HIGH SCHOOL

Gym Flooring



SUMMER 2017 PROJECTS – HIGH SCHOOL

Tuff Shed



SUMMER 2017 PROJECTS – HIGH SCHOOL

Crow's Nest



SUMMER 2017 PROJECTS – HIGH SCHOOL

Crow's Nest



SUMMER 2017 PROJECTS – HIGH SCHOOL



VTC east in front of C-Region



C/D Hallway VTC



C-Region Common



D-Region Common

SUMMER 2017 PROJECTS – HIGH SCHOOL



SUMMER 2017 PROJECTS – HIGH SCHOOL

- Lightning control panel parts in scheduling Brian from Team Electric aiming for mid-August.
- All concrete poured and completed
- Exterior signs installation date toward the end of August
- Rooftop motor replacement installation date August 1st.
- Grounds crew will be there first week of August (trimming bushes, trees, spreading bark chips, clearing fence lines, etc.)
- Pool scoreboard is being delivered and should be here next week.

SUMMER 2017 PROJECTS – MIDDLE SCHOOL

- Grounds crew will be there mid August to do flower beds, trimming bushes, adding bark chips).
- Paint crew will be mid August to do the list per the principal.

SUMMER 2017 PROJECTS – PRESCOTT

Concrete completed east side walk in front of school.



SUMMER 2017 PROJECTS – PRESCOTT

Roof replacement
wrapping up by
second week of
August.



SUMMER 2017 PROJECTS – PRESCOTT

- Playground chips installation date August 4th lower playground.
- Electronic Messenger Board toward the end of August.
- Grounds crew finished fence lines, trimming bushes.
- Paint crew will be there next week to do list per principal.
- Gym mini blinds will be here next week and will schedule.
- East gate along 105th will be repaired on the week of the 14th.

SUMMER 2017 PROJECTS – RUSSELL

Playground chips



SUMMER 2017 PROJECTS – RUSSELL

1. Roof replacement is completed (doing a walk through with Dell for a punch list)



SUMMER 2017 PROJECTS – RUSSELL


- Boy's restroom flooring start date will be the week of the 7th.
- Concrete sanding sidewalks scheduled Wednesday of next week.
- Electronic Messenger Board toward the end of August.
- Grounds crew will be there end of July (front entrance clean up, fence lines, and building edges, etc.).
- Paint crew will be at Russell on August 7th to do the list per the principal.

SUMMER 2017 PROJECTS – SACRAMENTO

- Concrete sanding sidewalk scheduled next week on Thursday.
- Playground chips start August 3rd on both playgrounds.
- Electronic Messenger Board toward the end of August.
- Grounds crew there now and working on flower beds, fence lines, edges of building.
- Paint crew will be at Sacramento July 31st to do list per the principal.

SUMMER 2017 PROJECTS – SHAVER

Playground chips installation

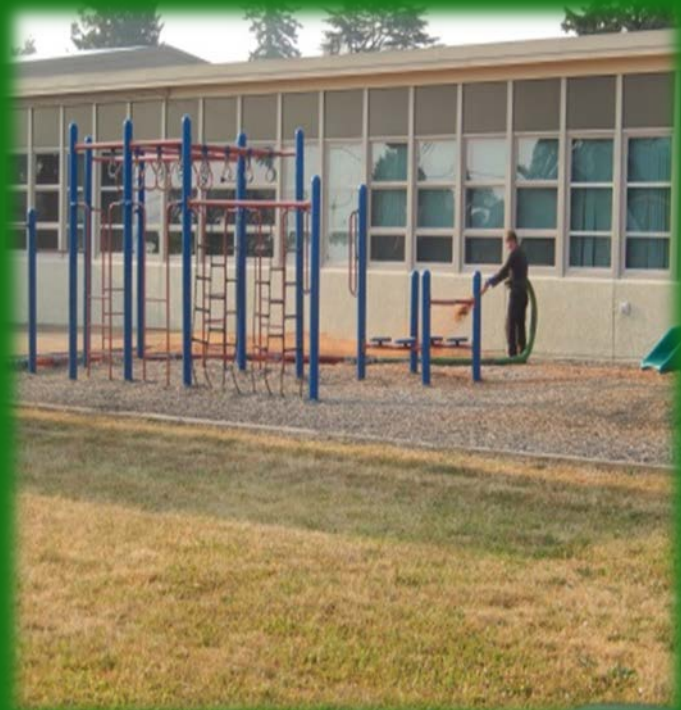

SUMMER 2017 PROJECTS – SHAVER

- Property fence is completed (Due to new park).
- Electronic Messenger Board toward the end of August.
- Grounds crew will be there end of July working on (fence lines, flower beds, trimming roses front entrance).
- Paint crew will be there on August 14th to do the list per the principal.

SUMMER 2017 PROJECTS – DISTRICT OFFICE

- Painting & shampooing Michelle Markle's office next week.
- Painted & Shampooed Mary's office.
- Grounds crew toward the end of August to do flower beds.
- Paint crew will be there to paint lots and touch up buildings.
Looking at the schedule, looking at mid August.
- Cleared out warehouse for Michael Lopes, working with Jayson on getting him some shelves.
- Waxing of DO floors August 10th thru the weekend, along with painting.
- Order signs for district office that mount on the walls. Once they arrive I will install and switch the ones that we have to match where staff is located.

SUMMER 2017 PROJECTS – RENTALS

WHEATLEY (THOMPSON)

1. Window units ordering Monday and it will take 7 days to be delivered. Will install when it arrives.
2. Grounds crew will be there August 1st to do fence lines, trimming rose bushes and all other bushes along with building edges.
3. Paint crew will be there August 18th to paint the lots.

HELENSVIEW (SUMNER)

1. Sewer line replacement completed (waiting on Lovett for asphalt) will be completed mid-next week.
2. Grounds crew will be there August 3rd to do fence lines, trimming bushes and building edges.
3. Paint crew will there August 18th to paint the lots.

KNOTT

1. Asbestos abatement completed.
2. VTC & Walk off mat completed & waxed.
3. Painting completed.
4. Grounds cleared and re-seeding west back area.
5. Steam traps & motors start Monday by maintenance.
6. Concrete poured today completed (Side-walks).

