

Town of Horizon City Capital Improvement Program

October 14, 2025
Council Meeting

Municipal Facilities Phase 1

- Site work
 - Landscape and irrigation pending
 - Sidewalk at the front of building 90% complete
 - Antenna relocation — coordination ongoing, scheduled for week of October 13.

Municipal Facilities Phase 1

- Vertical Construction
 - Work continuing
- Project currently on schedule

Municipal Facilities Phase 1





Oct 8, 2025 at 13:43:30 MDT



Oct 8, 2025 at 07:56:04 MDT



Oct 8, 2025 at 07:58:45 MDT

Municipal Facilities Phase 1



Picture taken September 30, 2025

Municipal Facilities Phase 1



Images taken on October 9, 2025

Federally- & State-Funded Project Updates

N. Darrington/Horizon Blvd. Reconstruction


- Horizon to Highweed - curb, colored concrete and paving
- Highweed to Roslyn - Base and water and wastewater lines installations
- Roslyn to Pete LaRue – wastewater line conflict with storm drain

N. Darrington/Horizon Blvd. Reconstruction

- **Pond Treatment**
 - Geotechnical recommendations due on October 14, 2025. Will be shared with TXDOT and contractor.

Rodman Shared Use Path (SUP)

- Phase 2 from Horizon to tire shop scheduled to begin week of October 13, 2025
- Forming curbs along phase 2.

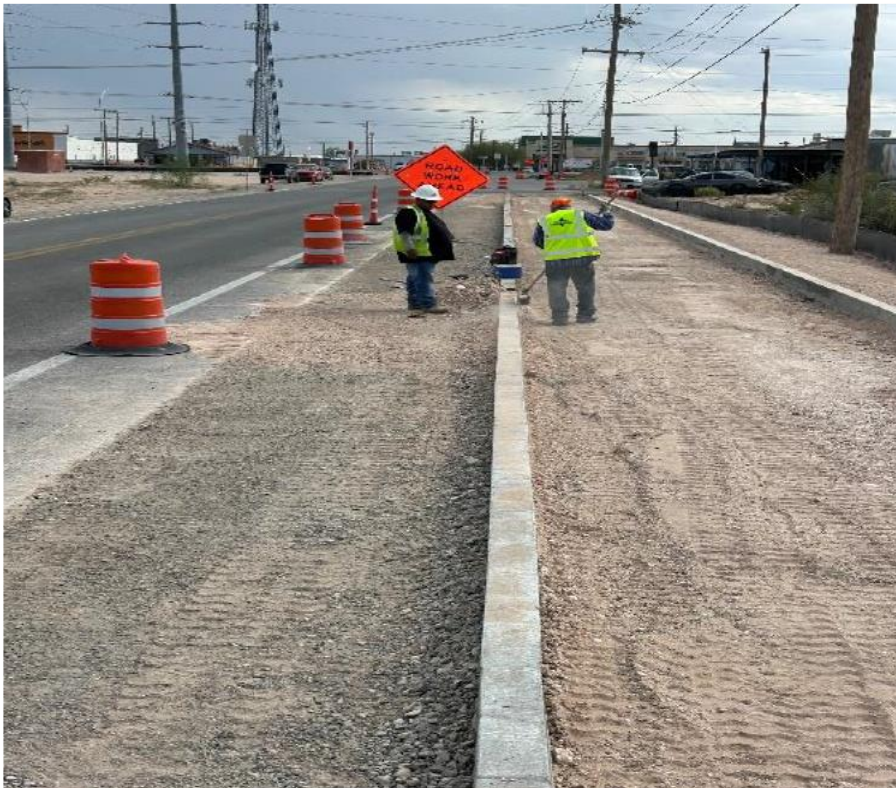

TIRZ/TOD Update

Dilley, Delake and Transit Plaza

- Design has begun - design budget from HUD \$1.7 million
- Coordination with Stakeholders
 - Met with ETA for transit plaza programming
 - City and ETA personnel visited two Sun Metro transit plazas: Airport and RC Poe

Town of Horizon City Capital Improvement Program

October 14, 2025
Council Meeting
