

Minidoka County School District  
**Monthly Maintenance Report**  
September 8, 2017

Aug. 8th - 126 New Requests  
116 Work in Progress  
22 Complete  
10069 Closed Work Orders


Sept. 8th - 101 New Requests  
113 Work in Progress  
91 Complete  
10156 Closed Work Orders

**Maintenance Department Updates**

**Current Projects:**


**DSC Roofing Project**

- 1) Roofing project to replace 3 areas of sloped roofing is designed and ready for bidding. Bidding to take place late spring. Advertise for bid April 19 & 26. Bid opening was May 4<sup>th</sup>. Replace and construct cat walk for servicing HVAC equipment on roof. Contracts being issued. Pre-construction meeting was held on July 7<sup>th</sup>. Work to begin on July 17<sup>th</sup>. Project under construction. Completion Mid- October.




**Minico**

- 1) Irrigation Pump Project Relocation- Advanced Irrigation Solutions is designing the relocation of Minico's turbine pump. This is being relocated because MID is dropping the water level in the ditch. In design. Plans complete and under review. Specs reviewing making ready to bid.

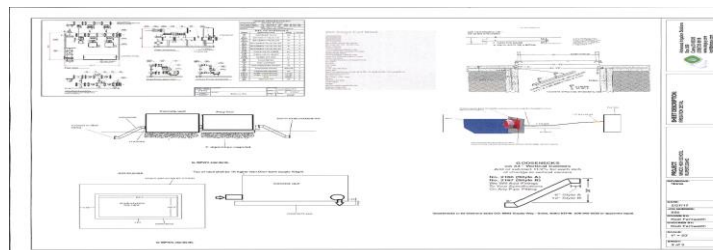

Minidoka County School District  
**Monthly Maintenance Report**  
September 8, 2017

2) New Computer Lab – Finishing up.

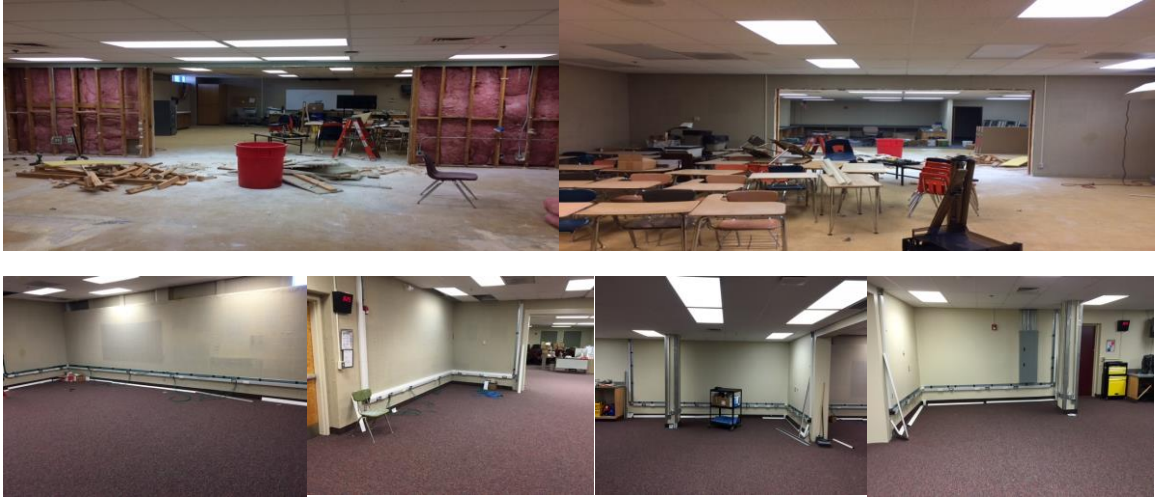


3) Ag Teachers Offices – Complete



**Maintenance Building**

Before. Project taken a backseat to construction in schools. Project on hold until summer work is complete.

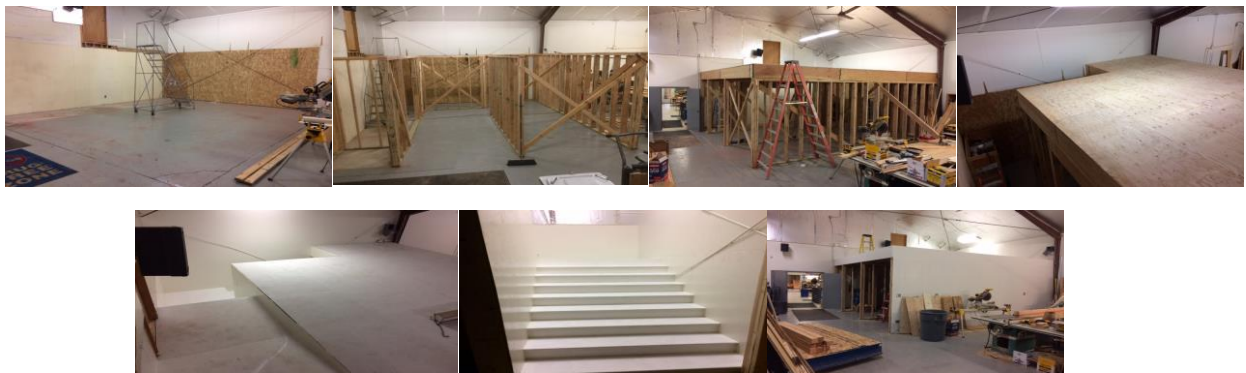

Minidoka County School District  
**Monthly Maintenance Report**  
September 8, 2017

**Food Service Building**

Project on hold until summer work is complete.



**Heyburn**

- 1) Flooring Before



After - 100% of carpet installed in classrooms. Tiled floors to follow after school starts. It will be done after hours & weekends. A classroom or two at a time. Hallways to follow.



**Paul**

- 1) Restroom sinks installed.

Before in Girl's Restroom

After

Before in Boy's Restroom

After



**East**

- 1) Modular - Fiber internet project complete.
