



A Professional Project Management Firm



NAVARRO ISD

Bond Projects Status Update

PRESENTED BY:

AG|CM, INC.

March 23, 2026

2024 BOND UPDATE

PROJECTS

Athletics Complex

Baseball & Softball

Football

Elementary and Intermediate Drives, Parking & Playground Improvements

Jr. High Remodel/Refresh

Existing High School Chiller Replacement

Existing Elementary and Intermediate Refreshes

Navarro South Elementary

Anticipated Start

Anticipated Completion

April 2025

April 2026

April 2025

September 2026

May 2025

Completed

January 2026

August 2026

January 2026

August 2026

~~May 2027~~ Jan 2026

August 2027

January 2026

May 2027



CONSTRUCTION UPDATES SINCE LAST MEETING

Athletics Complex



CONSTRUCTION UPDATES SINCE LAST MEETING

Athletics Complex




CONSTRUCTION UPDATES SINCE LAST MEETING

Chiller Replacement / Jr HS Refresh



CONSTRUCTION UPDATES SINCE LAST MEETING

Chiller Replacement / Jr HS Refresh

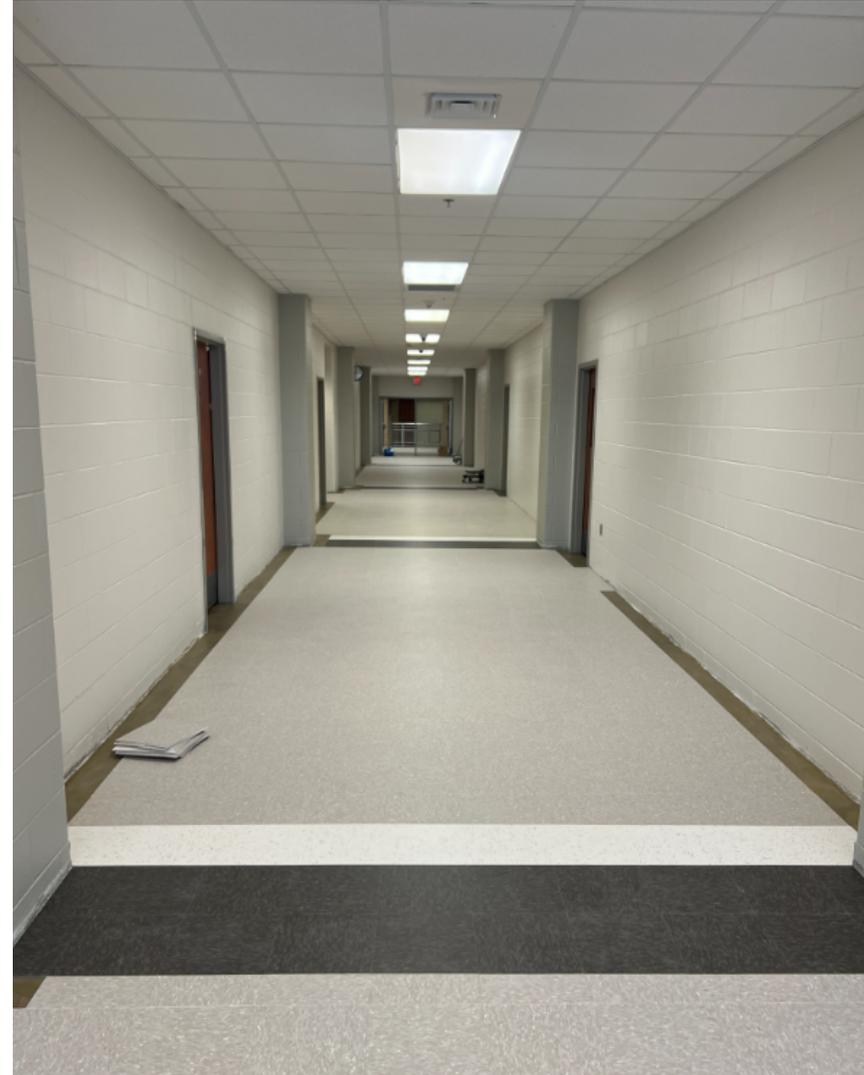

CONSTRUCTION UPDATES SINCE LAST MEETING

Navarro South Elementary



CONSTRUCTION UPDATES SINCE LAST MEETING

Navarro South Elementary



Discussion
