# Town of Horizon City Capital Improvement Program

January 14, 2025 Council Meeting


# Municipal Facilities Phase 1

- Site work continues
- Vertical Construction
  - Steel frames for sally port, buildings and plaza canopies
  - Continued work on electrical, plumbing and mechanical rough-in
- Change Order #2 for additional bullet proof doors on today's agenda for Council consideration

# Municipal Facilities Phase 1

- Coordinating with utilities:
  - EPEC Easement agreement on today's Council agenda
  - TGS
  - HRMUD
  - Conterra
- Contractor is coordinating with Darrington Reconstruction project manager
- Project currently on schedule


# Municipal Facilities Phase 1

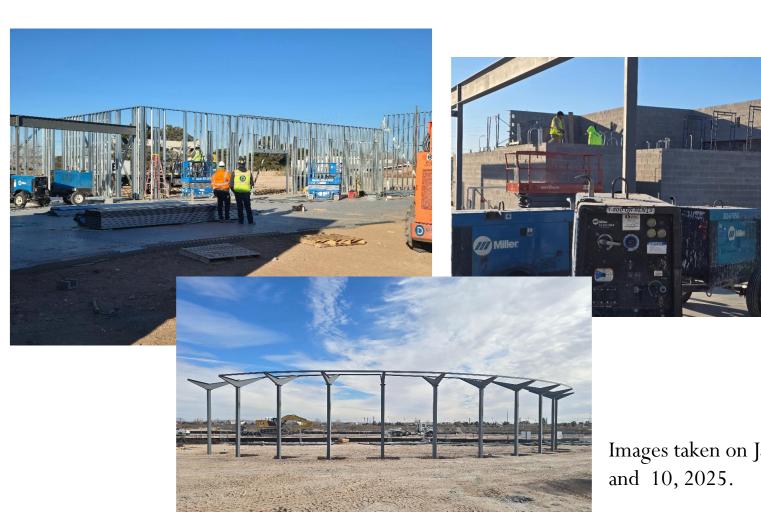

Images taken on January 6

# **New Regional Park**

 Coordinating for appraisal of property

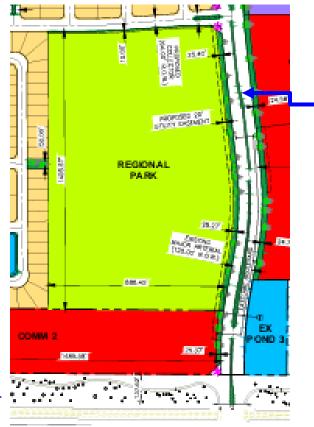

Eastlake Blvd.

Horizon Blvd.

From Preliminary Conceptual Plans, subject to change provided by Hunt Communities. June 2024

# Federally- & State-Funded Project Updates

# N. Darrington Reconstruction - Funding

- Staff working on necessary steps to apply for SIB loan.
- Revised 3-party agreement under review by partners
- Once amendment is approved, will work on ordinance amendments

# N. Darrington/Horizon Blvd. Reconstruction

- Storm drainage installation to being at Homestead – working through utility conflicts – pending TGS relocation dates
- Waterline installation at Oxbow
- Pond excavation continues
- Horizon Blvd. Phase 2
  - Temperatures during January 6 -10 affected paving

### Rodman Shared Use Path (SUP)

- Project under design 100% complete and under review
- Programmed for bidding and award in Spring 2025



# TIRZ/TOD Update

### Dilley, Delake and Transit Plaza

- Funding agreement has been executed
- Pending grant compliance manager selection

# Town of Horizon City Capital Improvement Program

January 14, 2025 Council Meeting
