


Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	D	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32				
EAST AURORA SCHOOL DISTRICT 131 - CAREER TECHNICAL CENTER																																										
MILESTONES																																										
MLSTN-1000	Core & Shell Design Complete	0	0	28-Jan-25																																						
MLSTN-1010	Design Complete	0	0	11-Mar-25																																						
MLSTN-1020	Commence Construction	0	0	15-Apr-25																																						
MLSTN-1030	Trade Contractor Scope Reviews Complete	0	0	21-Apr-25																																						
MLSTN-1040	Structure Complete	0	0	20-Nov-25																																						
MLSTN-1050	Enclosure Complete	0	0	20-Jan-26																																						
MLSTN-1060	Interior Buildout Complete	0	0	06-Aug-26																																						
MLSTN-1070	Substantial Completion	0	0	20-Aug-26																																						
PRECONSTRUCTION																																										
DESIGN																																										
DESIGN - BID RELEASE #1 - SITE WORK + CORE & SHELL																																										
DES-BR1-1000	Corlogan Clark Produce 50% Core & Shell Progress Set	0	0	18-Dec-24 A																																						
DES-BR1-1010	Corlogan Clark Produce 75% Core & Shell Progress Set	20	20	19-Dec-24																																						
DES-BR1-1020	Corlogan Clark Produce 100% Core & Shell Set	7	7	20-Jan-25																																						
DESIGN - BID RELEASE #2 - REMAINING TRADES																																										
DES-BR2-1000	Corlogan Clark Produce 50% Progress Set	26	26	18-Dec-24																																						
DES-BR2-1010	Corlogan Clark Produce 75% Progress Set	9	9	28-Jan-25																																						
DES-BR2-1020	Corlogan Clark Produce 90% Progress Set	15	15	10-Feb-25																																						
DES-BR2-1030	Corlogan Clark Produce 100% Set	7	7	03-Mar-25																																						
BID & AWARD																																										
BID RELEASE #1 - SITE WORK + CORE & SHELL																																										
BID-BR1-1000	FHP Develop Bid Packages	8	8	20-Jan-25																																						
BID-BR1-1010	Bid Release #1 Out to Bid	0	0	30-Jan-25																																						
BID-BR1-1020	Bid Release #1 Bid Period	15	15	30-Jan-25																																						
BID-BR1-1030	Bid Release #1 Bids Due	0	0	19-Feb-25																																						
BID-BR1-1040	FHP Conduct Trade Contractor Scope Reviews	5	5	20-Feb-25																																						
BID-BR1-1050	FHP Issue IGMP to Client	0	0	26-Feb-25																																						
BID-BR1-1060	Client Review IGMP	3	3	27-Feb-25																																						
BID-BR1-1070	Client Approve IGMP	0	0	03-Mar-25																																						
BID RELEASE #2 - REMAINING TRADES																																										
BID-BR2-1000	FHP Develop Bid Packages	9	9	03-Mar-25																																						
BID-BR2-1010	Bid Release #2 Out to Bid	0	0	14-Mar-25																																						
BID-BR2-1020	Bid Release #2 Bid Period	16	16	14-Mar-25																																						
BID-BR2-1030	Bid Release #2 Bids Due	0	0	04-Apr-25																																						
BID-BR2-1040	FHP Conduct Trade Contractor Scope Reviews	8	8	07-Apr-25																																						
BID-BR2-1050	FHP Issue GMP to Client	0	0	16-Apr-25																																						
BID-BR2-1060	Client Review GMP	3	3	17-Apr-25																																						
BID-BR2-1070	Client Approve GMP	0	0	21-Apr-25																																						
SUBMITTALS & MATERIAL PROCUREMENT																																										
SUB-1070	Precast - Submittals/Fabrication/Delivery	150	150	04-Mar-25																																						

Actual Work
 Remaining Work
 Critical Remaining Work

EAST AURORA SCHOOL DISTRICT 131 - CAREER TECHNICAL CENTER

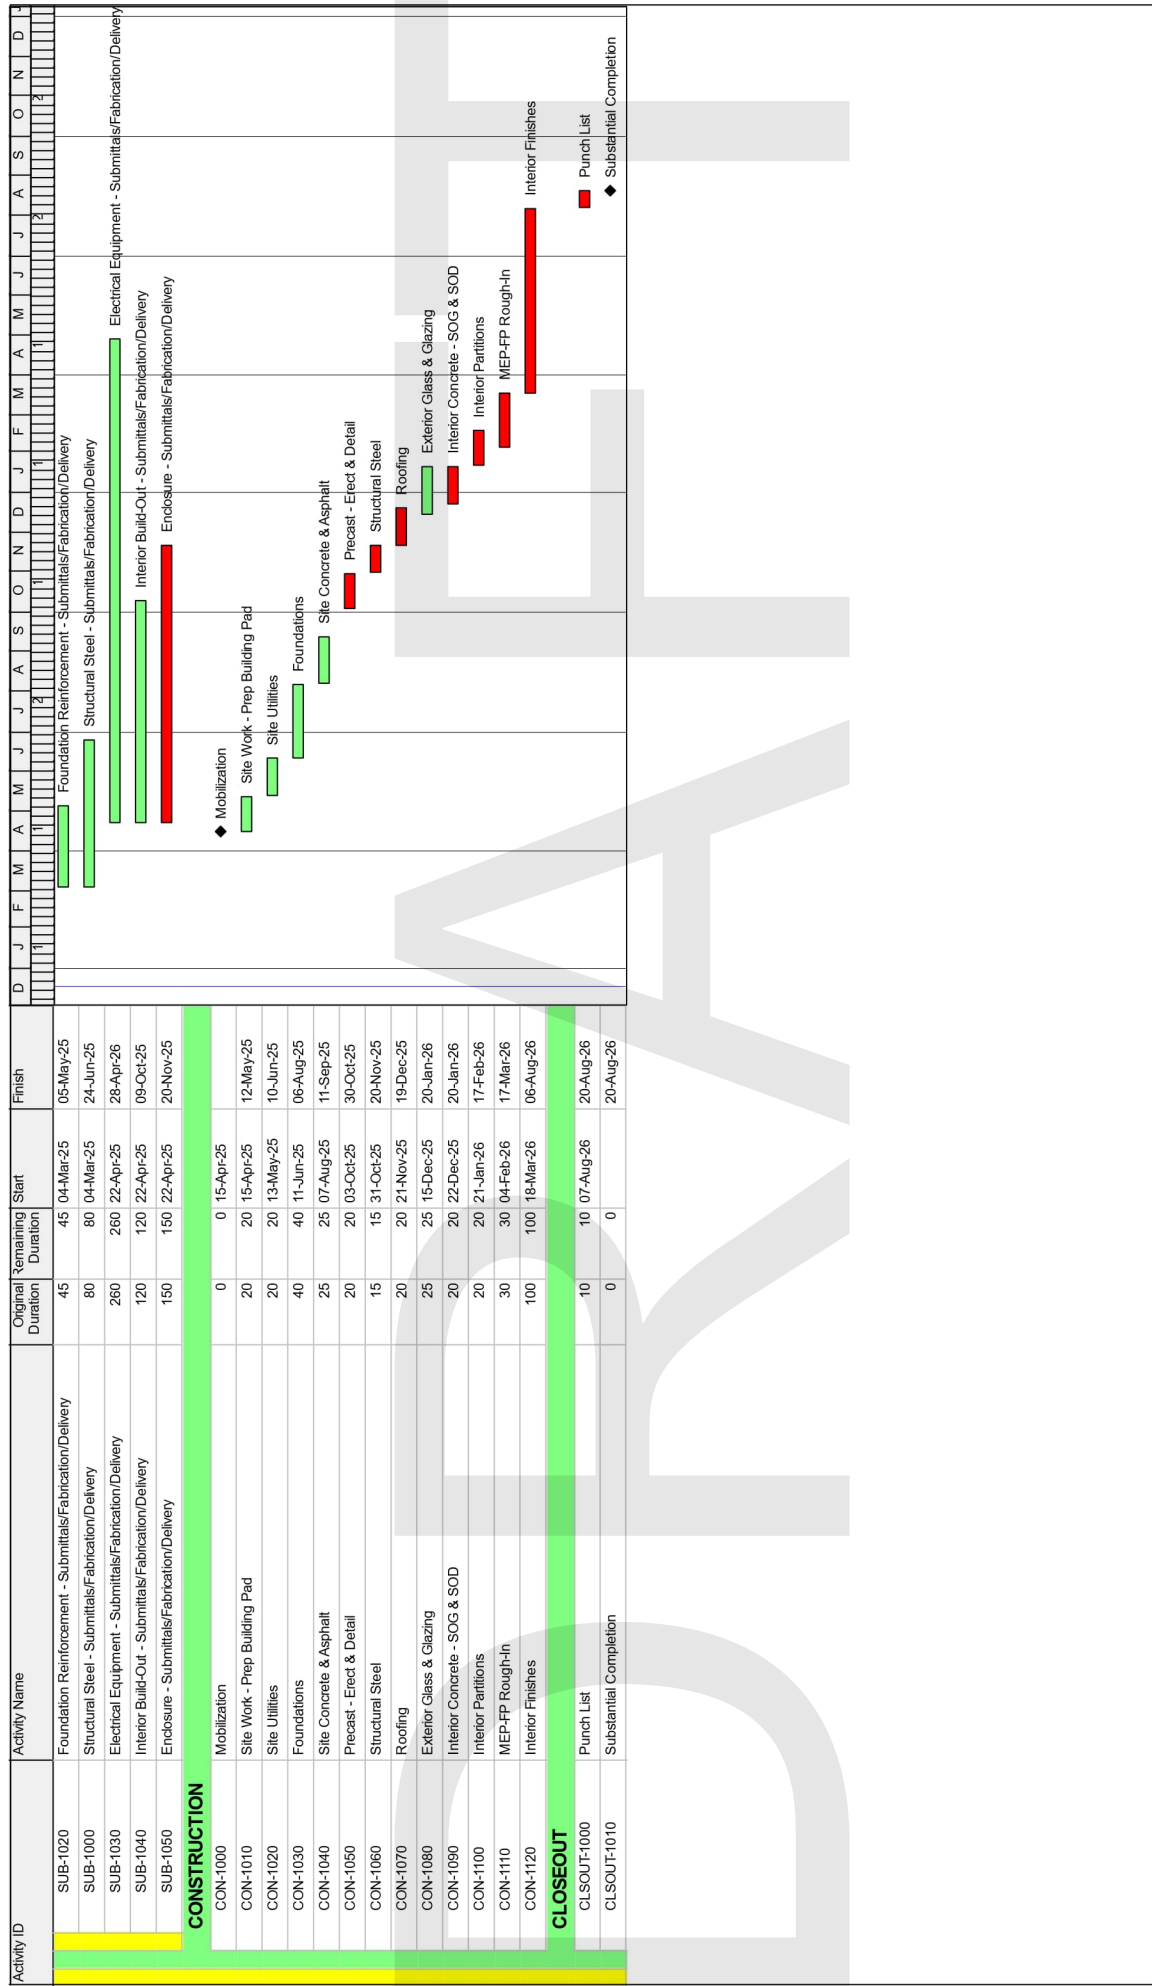

EAST AURORA SCHOOL DISTRICT 131 - CAREER TECHNICAL CENTER

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone
