


Bond Program Status Report To the Business Office

Through February 2016


2014 Bond Construction Program

Overall Performance February 2016 Report

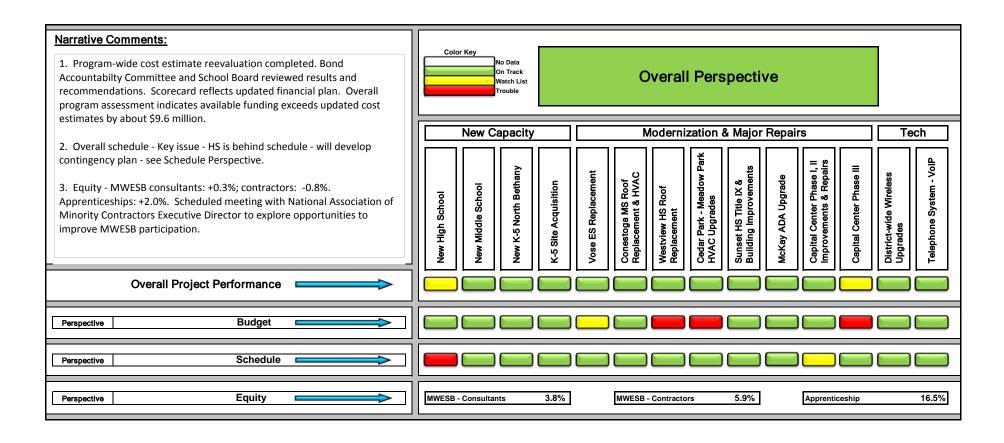

2014 Bond Construction Program

Budget Perspective February 2016 Report

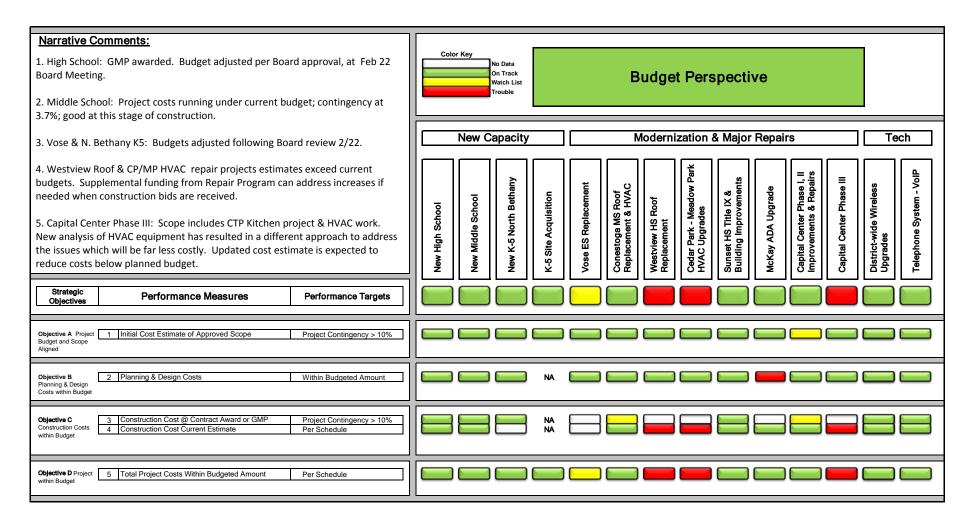


2014 Bond Construction Program


Schedule Perspective February 2016 Report

Narrative Comments: Color Kev 1. High school: behind schedule - will develop plan to complete sections of the building, if No Data needed, to allow opening for students on time while finishing work in areas not used by On Track **Schedule Perspective** students the first year. Student enrollment in 2017-18 likely to be at no more than 50% Watch List of capacity. HS boundary adjustment decisions will determine. 2. Middle school: Overall project schedule remains on track. 3. New K-5 @ N. Bethany: Land Use Permit hearing completed; permit being issued. **New Capacity Modernization & Major Repairs** Tech GMP contract awarded to Skanska. Resolved issue with County regarding realigning Kaiser Rd to allow 45mph speed limit; 35mph will be approved. -VolP Sunset HS Title IX & Building Improvements K-5 North Bethany Capital Center Phase III Capital Center Phase I, Improvements & Repai 4. Vose Replacement. Five contractors pregualified for bidding; ITB March 23. r Park - Meadow F S Upgrades Vose ES Replacement District-wide Wireless Upgrades Conestoga MS Roof Replacement & HVAC McKay ADA Upgrade K-5 Site Acquisition Westview HS Roof Replacement System · Middle School 5. SHS Title IX Project (includes Theater safety work). Phase I complete. Phase II, building New High School addition construction contract has been awarded. 6. Capital Center Phase II: IT Data Center substantially complete. Punch list only. Telephone 7. Capital Center Phase III: HVAC work and CTP (SPED) Kitchen; summer 2016 Cedar I HVAC I Strategic Performance Measures Performance Targets Objectives Occupancy / Completion Goal Established Green = Approved Objective A Project Execution Strategy Developed NA schedule. Establish Schedu Yellow = 0 - 4 weeks behind 3 Detailed Project Schedule Approved Target & Strategy Red > 4 weeks behind 4 Project Programming / Scope Completed 5 Design Contract Awarded NA Schematic Design (SD) Completed NA NA NA Objective B Design Development (DD) Completed NA Same as Objective A Land Use Permit Approved NA Permitting & Design Phases or Construction Documents (CD) Completd NA 10 Building Permit Approved Prime Contract Notice to Proceed Objective C Construction Started Same as Objective A NA Construction or Certificate of Occupancy Received 14 FF&E Ordered NA NA NA NA NA NA NA Same as Objective A FF&E Delivered and Installed NA NA NA NA NA NA Objective D Meet Occupancy Completion Schedule Target Occupancy / Completion on Schedule Same as Objective A Projected Occupancy / Completion Dates (month 9-2015 8-2017 8-2016 8-2017 2016 8-2016 8-2017 8-2016 8-2016 8-2016 5-2016 5-2016 9-2015 Phased

2014 Construction Bond Program

Equity Performance February 2016 Report

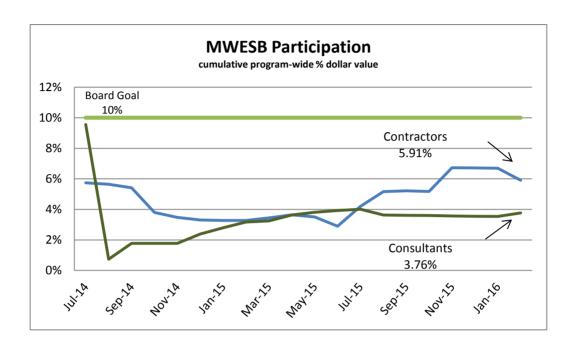

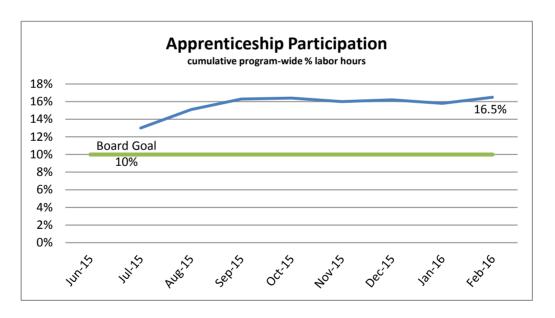



2014 Bond

Financial Summary Overall Program Cost Forecast and Available Funding

Project List	Original Funding Allocations	Funding Increases Available to Bond Program	Co	onstruction Cost Updates & Escalated for Inflation			
ACMA Replacement	\$ 28,300,000		\$	39,048,849	(RLB 1/16 + soft co	osts)	
AHS Title IX Compliance	\$ 2,000,000		\$	2,406,800		Color Key	_
Capital Center Improvements & Data Center	\$ 5,000,000		\$	14,357,208	(eB 2/29/16 EAC)	Final Cost Estimate	
District-Wide ADA Compliance	\$ 2,000,000		\$	2,000,000		Fixed Cost	
District-Wide Communication System	\$ 7,200,000		\$	5,517,170	(eB 2/29/16 EAC)	Estimate Update	
District-Wide Facility Repairs	\$ 98,000,000		\$	94,773,013		Inflation Projection	
District-Wide HVAC Controls	\$ 800,000		\$	800,000		Abbreviations:	RLB = Rider Levett Bucknall
Domestic / Fire Line Separation	\$ 800,000		\$	977,120			eB = eBuilder proj. mgmt info system
Five Oaks MS Renovation & Expansion	\$ 21,100,000		\$	32,401,576	(RLB 1/16 + soft co	osts)	EAC = \$ Estimate at proj. completion
Green Energy Technology	\$ 5,000,000		\$	3,010,000			HCC = Hoffman Construction Co.
Hazeldale K-5 Replacement	\$ 24,600,000		\$	35,765,354	(Vose estimate + ir	nflation)	GMP = Guaranteed Max. Price
IT Data Center @ Capital Center	\$ 2,900,000		((Costs Moved to CC Proiect)			
Kitchen Improvements	\$ 800,000		\$	977,120			
Land for new K-5 @ So. Cooper Mountain	\$ 3,000,000		\$	4,367,000			
Maintenance Facility Improvements	\$ 10,000,000		\$	12,383,615	(RLB 1/16 + soft co	osts + \$675K property	+ \$ parking lot work)
McKay ADA Improvements	\$ 400,000		\$	640,000			
New HS @ South Cooper Mountain	\$ 109,000,000		\$	184,508,541	(HCC GMP + soft of	costs)	
New K-5 @ North Bethany	\$ 25,000,000		\$	37,975,000	(GMP + soft costs)		
New MS @ Timberland	\$ 51,600,000		\$	60,711,652	(eB 2/29/16 EAC)		
Raleigh Hills K-8 Improvements	\$ 9,700,000		\$	12,295,720			
Security Upgrades	\$ 10,000,000		\$	10,000,000			
Seismic Upgrades	\$ 4,200,000		\$	5,206,740			
SHS Title IX Compliance	\$ 2,000,000		\$	4,324,288	(eB 2/29/16 EAC)		
Springville K-8 Improvements	\$ 2,000,000		\$	510,016	Completed		



2014 Bond

Financial Summary Overall Program Cost Forecast and Available Funding

Project List	ginal Funding Allocations		nding Increases ailable to Bond Program	C	Construction Cost Updates & Escalated for Inflation	
Vose K-5 Replacement	\$ 24,800,000			\$	33,794,951	(eB 2/29/16 EAC)
William Walker K-5 Replacement	\$ 24,600,000			\$	35,484,698	(Vose estimate + inflation)
Added Projects	\$ -			\$	1,980,066	
Program Contingency	\$ 45,400,000				Funding available	
Program Inflation	\$ 52,800,000				(not a cost)	
Pre-Bond Expenditure Reimbursements	\$ 1,000,000			\$	998,828	
Bond Management Costs	\$ 20,000,000			\$	28,000,000	
Bond Issuance Costs	\$ 6,000,000			\$	6,000,000	
construction	\$ 600,000,000			\$	671,215,325	
Learning Technology	\$ 56,000,000			\$	56,000,000	
Critical Equipment	\$ 24,000,000			\$	1 1	
ech & Equip Subtotal	\$ 80,000,000			\$	80,000,000	
otal Original Funding	\$ 680,000,000					
otal Cost Projection				\$	751,215,325	
2006 Bond Remaining Balance		\$	576,615			
Capital Center Rent Revenue		\$	433,385			
Construction Excise Tax Revenue		\$	1,000,000			
Interest Earnings 1st Bond Sale		\$	5,156,948			
Bond Premium 1st Bond Sale		\$	63,295,961			
Construction Excise Tax Rev Thru 2021		\$	5,401,000			
Other (estimated) *		\$	5,000,000			
Total Funding Available		\$	760,863,909			
Total Cost Updates				9	751,215,325	
Funding Balance Vs. Cost Updates	•					\$ 9,648,584
		S E F	otential other rev THPRD reimb. ** SB 1149 reimb. TO reimb. Facility grants Geismic grants	/enu	\$545,000 \$2,500,000 \$9,000 \$2,500,000 \$1,000,000 \$6,554,000	

7



2014 Bond Financial Summary

Project List		ginal Budget	Added Funding to		ised Approved		Jan-16		Feb-16	Net Continge	ncy Balance
	4	Allocations	Bond Program	Cu	rrent Budget	E	Est @ Comp.	Est @ Comp.		\$	%
ACMA Replacement	\$	28,300,000		\$	39,048,849	\$	39,048,849	\$	39,048,849		
AHS Title IX Compliance	\$	2,000,000		\$	2,406,800	\$	2,406,800	\$	2,406,800		
Capital Center Improvements & Data Center	\$	5,000,000		\$	13,508,130	\$	13,258,000	\$	14,357,208	\$ (849,078)	-5.9%
District-Wide ADA Compliance	\$	2,000,000		\$	2,000,000	\$	2,000,000	\$	2,000,000		
District-Wide Communication System	\$	7,200,000		\$	5,600,000	\$	5,600,000	\$	5,517,170	\$159,177	2.9%
District-Wide Facility Repairs	\$	98,000,000		\$	94,773,013	\$	94,773,013	\$	94,773,013		
District-Wide HVAC Controls	\$	800,000		\$	800,000	\$	800,000	\$	800,000		
Domestic / Fire Line Separation	\$	800,000		\$	977,120	\$	977,120	\$	977,120		
Five Oaks MS Renovation & Expansion	\$	21,100,000		\$	32,401,576	\$	32,401,576	\$	32,401,576		
Green Energy Technology	\$	5,000,000		\$	3,010,000	\$	3,010,000	\$	3,010,000		
Hazeldale K-5 Replacement	\$	24,600,000		\$	35,765,354	\$	35,765,354	\$	35,765,354		
IT Data Center @ Capital Center	\$	2,900,000			idget Moved to CC Project)						
Kitchen Improvements	\$	800,000		\$	977,120	\$	977,120	\$	977,120		
Land for new K-5 @ So. Cooper Mountain	\$	3,000,000		\$	4,367,000	\$	4,367,000	\$	4,367,000		
Maintenance Facility Improvements	\$	10,000,000		\$	12,383,615	\$	12,383,615	\$	12,383,615		
McKay ADA Improvements	\$	400,000		\$	640,000	\$	640,000	\$	640,000	\$ 51,061	8.7%
New HS @ South Cooper Mountain	\$	109,000,000		\$	184,654,450	\$	185,000,000	\$	184,508,541	\$ 9,659,372	5.5%
New K-5 @ North Bethany	\$	25,000,000		\$	37,975,000	\$	37,272,969	\$	37,975,000	\$ 3,089,259	8.9%
New MS @ Timberland	\$	51,600,000		\$	60,711,652	\$	60,711,652	\$	60,711,652	\$ 2,162,918	3.7%
Raleigh Hills K-8 Improvements	\$	9,700,000		\$	12,295,720	\$	12,295,720	\$	12,295,720		
Security Upgrades	\$	10,000,000		\$	10,000,000	\$	10,000,000	\$	10,000,000		



2014 Bond Financial Summary

Project List		iginal Budget		ded Funding to		vised Approved		Jan-16	Feb-16	Net Continge	ncy Balance
		Allocations	В	ond Program	C	urrent Budget	E	Est @ Comp.	Est @ Comp.	\$	%
Seismic Upgrades	\$	4,200,000			\$	5,206,740	\$	5,206,740	\$ 5,206,740		
SHS Title IX Compliance	\$	2,000,000			\$	4,324,288	\$	4,324,288	\$ 4,324,288	\$ 55,992	1.3%
Springville K-8 Improvements	\$	2,000,000			\$	510,016	\$	692,591	\$ 510,016	Completed;	Final Cost
Vose K-5 Replacement	\$	24,800,000			\$	33,794,951	\$	33,794,951	\$ 33,794,951	\$ 2,236,257	7.1%
William Walker K-5 Replacement	\$	24,600,000			\$	35,484,698	\$	35,484,698	\$ 35,484,698		
Added Projects					\$	1,980,066	\$	2,023,657	\$ 1,980,066		
Program Contingency	\$	45,400,000								,	
Program Inflation	\$	52,800,000									
Pre-Bond Expenditure Reimbursements	\$	1,000,000			\$	998,828	\$	998,828	\$ 998,828	Completed;	Final Cost
Bond Management Costs	\$	20,000,000			\$	28,000,000	\$	28,000,000	\$ 28,000,000		
Bond Issuance Costs	\$	6,000,000			\$	6,000,000	\$	6,000,000	\$ 6,000,000		
Construction	\$	600,000,000			\$	670,594,986			\$ 671,215,325		
Learning Technology	\$	56,000,000			\$	56,000,000			\$ 56,000,000		
Critical Equipment	\$	24,000,000			\$	24,000,000			\$ 24,000,000		
Tech & Equip Subtotal	\$	80,000,000			\$	80,000,000			\$ 80,000,000		
Grand Totals	\$	680,000,000			\$	750,594,986			\$ 751,215,325		
Interest Earnings			\$	5,156,948							
Bond Premium			\$	63,295,961							
Other Additional Funding (see Tab)			\$	12,411,000							
Total Added Funding			\$	80,863,909							
GRAND TOTAL 2014 BOND FUNDING			\$	760,863,909							
Funding Balance vs. Approved Budgets				\$10,26	68,9	23					
Funding Balance vs. Current Cost Estima	ites								\$ 9,648,584		

2014 Bond Program Financial Status Report Additional Funding Allocations

Additional Funding Allocation Program	ons	to Bond
Source		Funding
Remaining 2006 Bond Savings Capital Center Rent Revenue Balance Construction Excise Tax Revenue Forecasted Construction Excise Tax Estimated Other Grants & Reimbursements	\$ \$ \$ \$	576,615 433,385 1,000,000 5,401,000 5,000,000
TOTAL		\$12,411,000

2014 Bond Program Financial Status Report Green Energy Technology Fund Transfers

F	unding Allocations fron	ding Allocations from Green Energy Technology											
Project	Transfers into Projects		Bond Budget Balance	Comments									
		\$	5,000,000										
New High School	\$ 1,990,000	\$	3,010,000	288 kW solar PV panels									
New Middle School				Preliminary estimate: \$850,000									
TOTAL	\$1,990,000	\$	3,010,000										



2014 Bond Program Financial Status Report Added Projects

Added Projects	Approved by	Original Budget		ed Approved	Jan-16		Feb-16	Net Con Bala	tingency ince
	& Date	0	Curi	rent Budget	Est @ Comp.	Es	st @ Comp.	\$	%
Seclusion Rooms Alterations	Safety Comm 5/19/14		\$	99,368	\$ 99,368	\$	99,368	Com	peted
Portable Relocations 2014	Sr LT 5/20/14		\$	591,685	\$ 592,111	\$	592,111	Com	peted
Portable Relocations 2015	Sr LT 3/2015		\$	337,848	\$ 337,848	\$	294,257	Com	peted
Title IX Projects - Group II	Sr LT 3/2015		\$	990,000	\$ 994,330	\$	994,330	\$ 51,916	5.5%
									-
(Projects Financially Complete)									
Alle IBer's de Tatel			•	0.040.004	A 0.000.055	•	4 000 000	F4 040	
Added Projects Total		\$ -	\$	2,018,901	\$ 2,023,657	\$	1,980,066	\$ 51,916	



2014 Bond Program Financial Status Report

District-Wide Repair Projects - Budget = \$98,000,000

Project	In	itial Budget		vised Approved		Jan-16	Feb-16		Net Contingency Ba	alance
Tioject		om BCA List)	C	urrent Budget		Est @ Comp.	Est @ Comp.		\$	%
AHS Turf Replacement	\$	653,017	\$	814,543	\$	814,543	\$ 814,543		Completed	
SHS Roof Replacement	\$	2,181,226	\$	5,126,133	\$	5,126,133	\$ 5,126,133		Completed	
SHS Chiller	\$	188,549	\$	63,997	\$	63,997	\$ 63,997		Completed	
Five Oaks Phase I: Chiller Replacement	\$	167,734	\$	213,802	\$	92,397	\$ 92,397		Completed	
SHS Stadium Turf Replacement	\$	1,000,000	\$	1,331,077	\$	1,331,077	\$ 1,331,077		Completed	
JW/SM Fire Alarm Systems	\$	231,727	\$	481,389		481,383	481,389		Completed	
WHS Roof Replacement	\$	2,055,558	\$	2,055,558	\$	2,055,558	\$ 3,081,673	\$	(820,560)	-28.5%
Conestoga Roof Replacement	\$	2,157,350	\$	3,273,481		3,273,481	3,273,481	\$	900,270	37.9%
Capital Center - HVAC System, West side	\$	2,280,000	\$	-				М	oved to CC project	
SHS Repairs	\$	1,881,416	\$	-				М	oved to SHS Title IX pro	oject
SHS Repairs - Emergency Elec \$ Transferred	\$	(745,833)	\$	-						
SHS Auditorium Upgrades Phase I - Emerg Elec	\$	745,833	\$	807,355	\$	807,404	\$ 807,404	\$	31,721	4.1%
CP/MP HVAC Upgrades	\$	2,874,409	\$	4,857,183	\$	5,097,895	\$ 5,210,565	\$	6,671	0.1%
Conestoga Plumbing Repair (A/E only)	\$	160,000	\$	160,000		160,000	177,800	\$	(17,800)	-10.0%
Repair & Improvement Projects	\$	3,751,992	\$	3,592,647	\$	3,592,647	\$ 3,592,647			
(Projects Financially Complete)										
Repair Projects Total	\$	19,582,978	\$	22,777,164	\$	22,896,515	\$ 24,053,106	\$	100,302	
Repair Program Balance Available	\$	78,417,022	\$	71,995,849	\$	71,876,498	\$ 70,719,907			
Repair Program Less Transfers	\$	94,773,013								

2014 Bond Program Financial Status Report Security Upgrades

Security Upgrades	Approved by	Ir	nitial Budget	Revi	sed Approved		Jan-16	Feb-16		Ne	t Contingend	y Balance
Security Opgrades	& Date			Cu	rrent Budget	Es	st @ Comp.		Est @ Comp.		\$	%
Greenway ES Interior Door Locks, etc.	Dep Sup; 10/14/14	\$	2,000	\$	1,693	\$	1,693	\$	1,693			
Phase 1 & 1A: Building Perimeter Secuity	Safety Comm	\$	5,600,000	\$	5,000,000	\$	5,341,296	\$	5,341,296	\$	(289,207)	-5.5%
Security Projects Total		\$	5,602,000	\$	5,001,693	\$	5,342,989	\$	5,342,989	\$	(289,207)	
Security Program Balance Available		\$	4,398,000	\$	4,998,307	\$	4,657,011	\$	4,657,011			



2014 Bond Learning Technology/Classroom Systems and Critical Equipment Purchases February 29, 2016 Report

		Lear	ning Technology	/Classroom Systems - \$56 Million
	Project To Date Expenditures	2015-16 Budget	2015-16 Expenditures as of 2/29/16	Quarterly Description of Expenditures
Student Computer Replacement	\$ 2,554,035	\$ -	\$ -	Purchased 1,957 computers for student use in 2014-15. All machines were ready for students on the first day of school. Purchased 350 laptops for new teachers and for loan while laptops are in for repair in 2014-15. No computer replacement anticipated in 2015-16.
Digital Conversion - Innovation Grants	\$ 2,617,669	\$ 1,212,015	\$ 919,134	Student computing devices have been purchased and deployed with 17 Teacher teams at all levels across the district.
Technology Infrastructure	\$ 4,493,642	\$ 3,274,027	\$ 1,573,195	District Firewall, filters, core routers, and other critical networking equipment has been replaced. Enterprise wireless project in process to upgrade all schools wireless capacity.
Future Ready Schools	\$ 3,442,809	\$ 4,702,453	\$ 3,442,809	15 schools will begin planning for full school implementation of technology device integration with instructional practices. An additional 11 schools will be added in 2016-17. The devices for these schools will be purchased in the spring of 2016 in preparation for the 2016-17 school year.
Digital Curriculum	\$ 2,058,794	\$ 2,100,000	\$ 1,288,382	Salary for eight curriculum developers (4.2 FTE); Textbook purchases to support the ELA adoption; Payment for TeacherSource Enhancements on the professional development module and Lesson Plan design. High School Science Curriculum & Technology is also included in this amount.
Total Total Bond Funds Remaining	\$ 15,166,949	\$ 11,288,495	\$ 7,223,520 \$ 40,833,051	




2014 Bond Learning Technology/Classroom Systems and Critical Equipment Purchases February 29, 2016 Report

			Critical Eq	uipment - \$24 Million
	Project To Date Expenditures	2015-16 Budget	2015-16 Expenditures as of 2/29/16	Quarterly Description of Expenditures
Musical Instruments \$250,000	\$ 201,659	\$ 79,858 \$	31,517	One time expense of \$250,000.
Buses \$16,000,000	\$ 6,104,189	\$ 3,391,578 \$	3,250,709	Approximately \$2 million/year over eight years. In first year, \$4.25 million will be spent and \$2million/year will be spent in years two through seven. \$0 will be spent in the eighth year. Approximately \$1.4 million will be added to 2015-16 budget to pay for 13 buses ordered but not received as of June 30, 2015.
Copiers \$3,906,079	\$ 605,314	\$ 299,000 \$	269,615	Approximately \$250,000/year over eight years.
Scoreboard Replacements \$335,202	\$ 70,370	\$ 335,202 \$	70,370	\$67,000/high school to replace scoreboards. Beaverton High School to be completed in year 2. Remaining high schools are scheduled to be completed in 2016-17 (year 3).
FF&E for FD Kindy/ Additional Teachers \$2,336,297	\$ 1,369,984	\$ 1,376,450 \$	1,369,984	Furniture, fixtures & equipment, including technology, for full day kindergarten and additional teachers K-5.
Cafeteria Tables Replacement \$184,105	\$ 184,105	\$ 184,105 \$	184,105	Replace cafeteria tables district-wide.
Athletic Equipment \$232,000	\$ -	\$ 32,000 \$; -	Approximately \$100,000/year over three years beginning in year 2. \$68,000 was transferred in year 2 to the Scoreboard Replacements Project for the 4 remaining high schools (\$17,000/remaining high school).
Maintenance Equipment \$600,000	\$ 174,003	\$ 185,000 \$	174,003	Approximately \$120,000/year over five years beginning in year 2. Year 2 will have \$185,000. Year 6 will only have \$55,000.
Other Equipment Purchases \$15,000	\$ 15,000	\$ - \$	-	Other critical equipment purchases as needed Purchase of \$15,000 towards new locker banks at Stoller in 14-15.
Total Total Bond Funds Remaining	\$ 8,724,624	\$ 5,883,193 \$		

2014 Bond Learning Technology/Classroom Systems and Critical Equipment Purchases GL to JL Reconciliation February 29, 2016

Project #	Description	GL Key	20:	15-16 Budget	Encumbered	YTD Actuals	Balance
0102	Positive Change Grants	415.689.4189-xxxx	\$	1,212,015	\$ 230	\$ 919,134	\$ 292,651
0103	District Wireless Infrastructure	415.689.4182-xxxx		3,274,027	618,636	1,573,195	1,082,196
0104	Curriculum	415.551.4110-xxxx		464,023	183,570	280,453	-
0104	Curriculum	415.551.4182-xxxx		135,977	-	99,583	36,394
				600,000	183,570	380,036	36,394
0109	High School Science Curriculum	415.689.4181-xxxx		1,500,000	1,078	908,346	590,576
0110	Future Ready	415.689.4185-xxxx		4,702,453	1,258,950	3,442,809	694
Total Learni	ng Technology/Classroom Systems (\$56	M)	\$	11,288,495	\$ 2,062,464	\$ 7,223,520	\$ 2,002,511
Project #	Description	GL Key	20:	15-16 Budget	Encumbered	YTD Actuals	Balance
0105	Musical Instruments	415.499.4181-0460	\$	79,858	\$ 750	\$ 31,517	\$ 47,591
0106	Buses	415.625.2552-0564		3,391,578	133,501	3,250,709	7,368
0107	Copiers	415.651.4189-0541		299,000	18,355	269,615	11,030
0108	Scoreboard Replacement	415.420.4150-0541		67,000	9,122	800	57,078
		415.430.4150-0541		67,000	9,096	800	57,104
		415.450.4150-0541		67,202	543	66,710	(51)
		415.460.4150-0541		67,000	17,270	780	48,950
		415.480.4150-0541		67,000	9,142	1,280	56,578
				335,202	45,173	70,370	219,659
0111	Classroom Furniture & Equipment	415.499.4184-0461		494,661	4,611	488,679	1,371
0111	Classroom Furniture & Equipment	415.689.4184-0480		881,789	485	881,304	-
				1,376,450	5,096	1,369,983	1,371
0112	Cafeteria Table Replacement	415.499.4189-0461		184,105	-	184,105	-
0113	Athletic Equipment	415.555.4189-0460		32,000	-	-	32,000
0114	Maintenance Equipment	415.641.4189-0541		185,000	9,997	174,003	1,000

^{**} Encumbered amount is remaining salary budget.

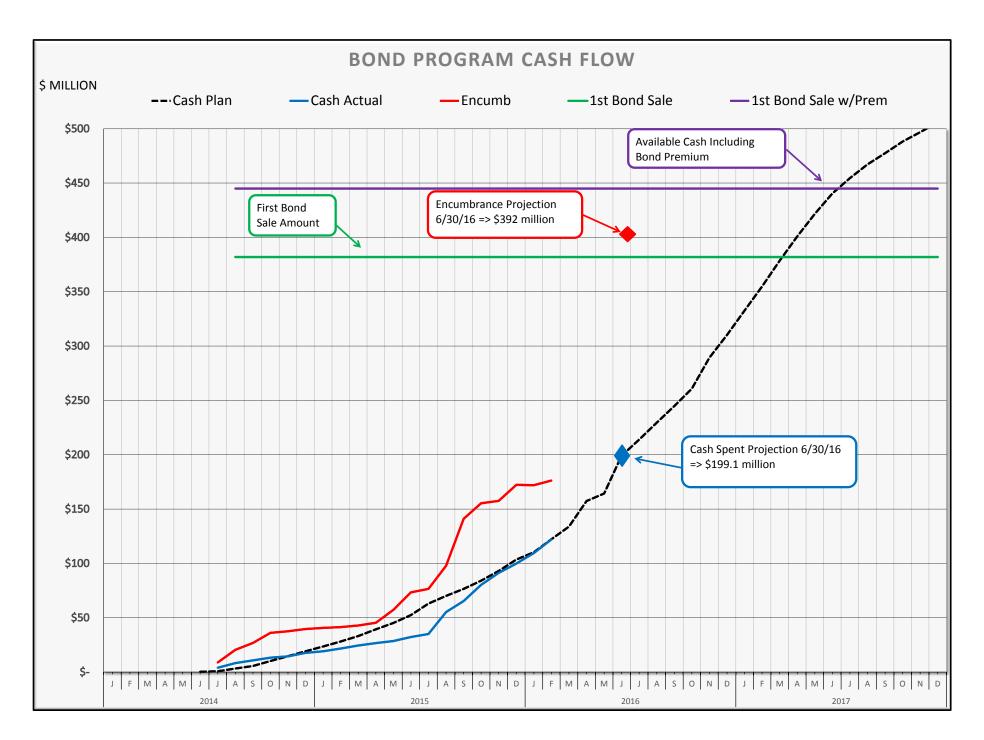

2014 Bond Program Monthly e-Builder/IFAS Reconciliation as of February 29, 2016

	IFAS GL	IFAS JL	e-Builder
Total Spent	122,051,585.82	\$ 96,479,387.50	\$ 87,345,545.96
Reconciling Items	576,615.33	\$ 2,077,911.50	\$ 11,211,753.04
Revenue Not In GL/JL	(176,720.43)	\$ -	
IT/Equipment Total		\$ 23,889,971.72	\$ 23,889,971.72
Adjustments:	(525.00)	\$ 70.00	\$ 70.00
Balance Total	122,450,955.72	\$ 122,447,340.72	\$ 122,447,340.72

Reconciling Items			Non JL	Non e-B
Bond Planning	7901		\$ -	\$ 998,828.50
Bond Issuance	7922			\$ 2,025,634.63
Payroll Expenses			\$ 2,077,911.50	\$ 3,843,975.40
Assurances				\$ 3,870,017.00
Non JL Items			\$ -	\$ 473,297.51
Non Bond Funds		576,615.33	\$ -	
		576,615.33	\$ 2,077,911.50	\$ 11,211,753.04

IT/Equipment Totals	
Aloha HS	\$ 800.00
Southridge HS	\$ 800.00
Beaverton HS	\$ 66,709.70
Westview HS	\$ 780.00
Sunset HS	\$ 1,280.00
Stoller Middle School	\$ 15,000.00
All Schools	\$ 874,443.30
Quality Curriculum	\$ 1,086,865.33
Transportation	\$ 6,104,189.06
Maintenance	\$ 174,003.00
Purchasing	\$ 605,314.03
IT	\$ 14,961,387.30
Trans to GF	\$ -
	\$ 23,889,971.72
