




A Professional Project Management Firm

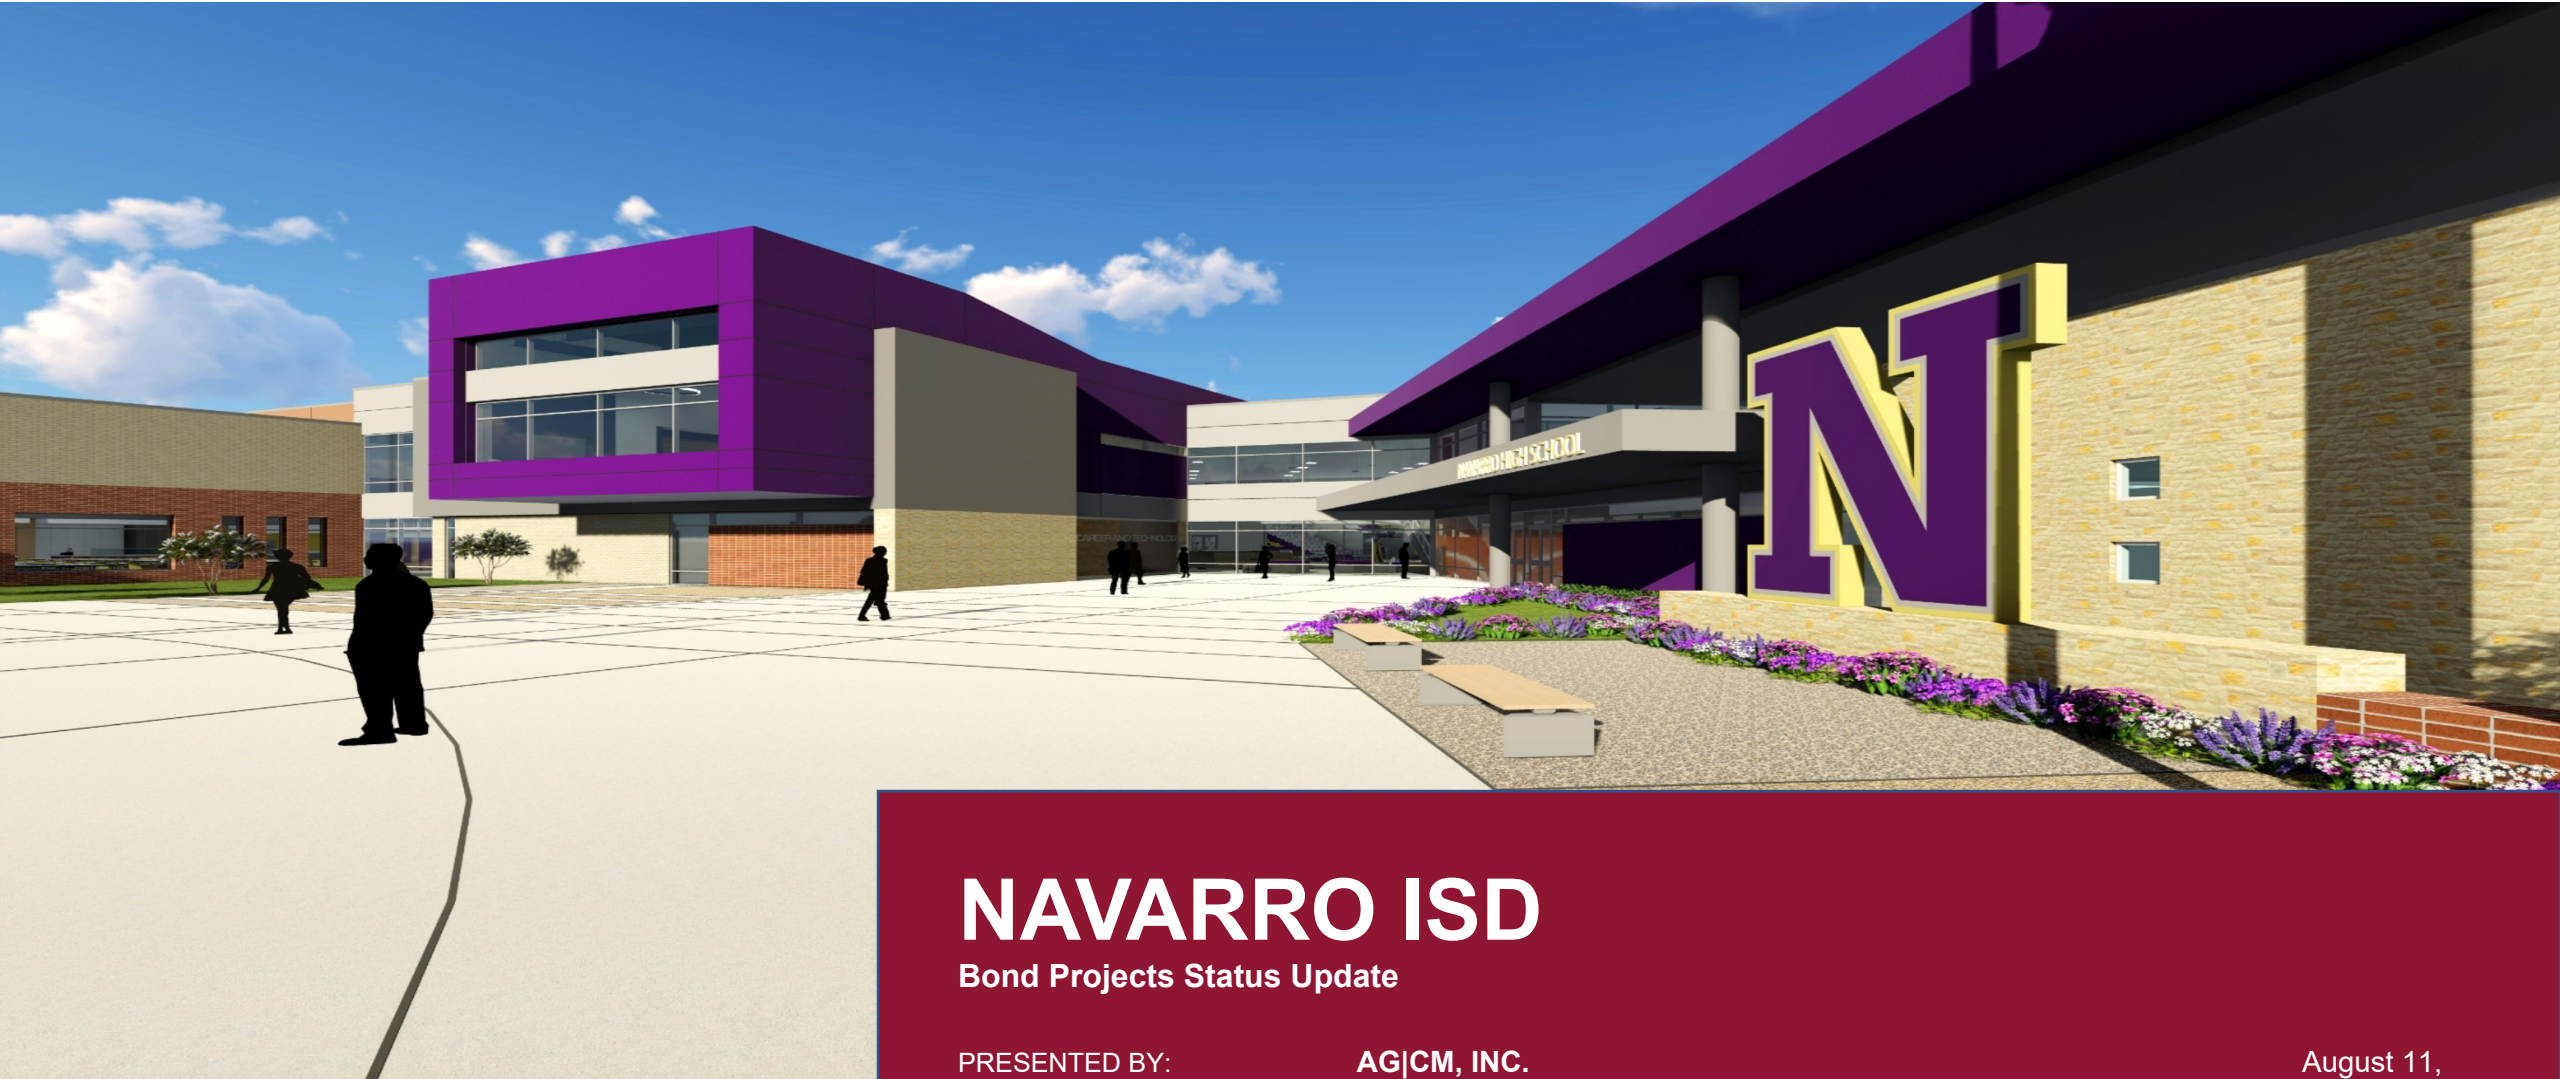

# NAVARRO ISD

Bond Projects Status Update

PRESENTED BY:  
2025

AG|CM, INC.

August 11,

# 2024 BOND UPDATE

## PROJECTS

- Athletics Complex
  - Baseball & Softball
  - Football
- Elementary and Intermediate Drives, Parking & Playground Improvements
- Jr. High Remodel/Refresh
- Existing High School Chiller Replacement
- Existing Elementary and Intermediate Refreshes
- Navarro South Elementary

Anticipated Start

Anticipated Completion

- |              |                |
|--------------|----------------|
| April 2025   | April 2026     |
| April 2025   | September 2026 |
| May 2025     | September 2025 |
| January 2026 | August 2026    |
| January 2026 | August 2026    |
| May 2027     | August 2027    |
| January 2026 | May 2027       |





# CONSTRUCTION UPDATES SINCE LAST MEETING

## Elementary and Intermediate Drives, Parking & Playground Improvements - August 2025

- Started: May 2025
- Completion: September 2025





# CONSTRUCTION UPDATES SINCE LAST MEETING

Elementary and Intermediate Drives, Parking & Playground Improvements - August 2025





# CONSTRUCTION UPDATES SINCE LAST MEETING

Elementary and Intermediate Drives, Parking & Playground Improvements - August 2025



# CONSTRUCTION UPDATES SINCE LAST MEETING

## Athletics Complex – August 2025

- Started: April 2025
- Anticipated Completion – Baseball and Softball: April 2026
- Anticipated Completion – Football: September 2026





# 2021 BOND UPDATE

## New High School - August 2025





# 2021 BOND UPDATE

## New High School - August 2025





# Discussion
