

Minidoka County School District  
**Monthly Maintenance Report**  
October 11, 2017

Sept. 8th - 101 New Requests  
113 Work in Progress  
91 Complete  
10156 Closed Work Orders


Oct. 6th - 97 New Requests  
115 Work in Progress  
125 Complete  
10231 Closed Work Orders

## Maintenance Department Updates

### Current Projects:

#### DSC Roofing Project


- 1) Roofing project to replace three areas of sloped roofing is designed and ready for bidding. Bidding to take place late spring. Advertise for bid April 19 & 26. Bid opening was May 4<sup>th</sup>.
- 2) Replace and construct cat walk for servicing HVAC equipment on roof. Contracts being issued. Pre-construction meeting was held on July 7th. Work to begin on July 17<sup>th</sup>. Project under construction. Completion Mid- October.



Minidoka County School District  
**Monthly Maintenance Report**  
October 11, 2017

**Minico**

- 1) Irrigation Pump Project Relocation- Advanced Irrigation Solutions is designing the relocation of Minico's turbine pump. This is being relocated because MID is dropping the water level in the ditch. In design. Plans complete and under review. Specs reviewing making ready to bid.

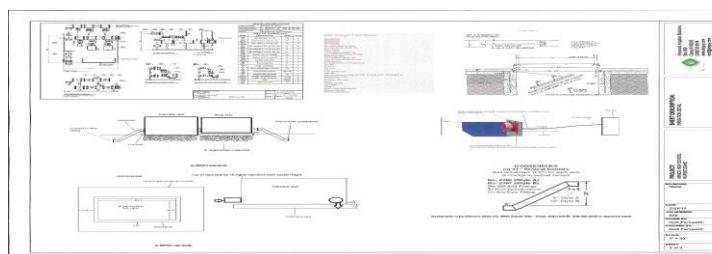

- 2) New Computer Lab – Finishing up.



Minidoka County School District  
**Monthly Maintenance Report**  
October 11, 2017

**Maintenance Building**

Before: Project taken a backseat to construction in schools. Project on hold until summer work is complete.



**Food Service Building**

Project on hold.



**Heyburn**

Flooring: Before



After - 100% of carpet installed in classrooms. Tiled floors to follow after school starts. It will be done after hours & weekends. A classroom or two at a time. Hallways to follow.

