

Minidoka County School District
Monthly Maintenance Report
January 11, 2018

Dec. 6th - 96 New Requests
135 Work in Progress
52 Complete
10498 Closed Work Orders


Jan. 11th – 101 New Requests
143 Work in Progress
46 Complete
10592 Closed Work Orders

Maintenance Department Updates

Current Projects:

Minico

- 1) Irrigation Pump Project Relocation- Advanced Irrigation Solutions is designing the relocation of Minico’s turbine pump. This is being relocated because MID is dropping the water level in the ditch. In design. Plans complete and under review. Specs reviewing making ready to bid. Priced out components, coordinated with MID for headgate construction. Start date will be January or February.



- 2) Old Food Service Building the construction class is remodeling.



- 3) Roofing project at Minico, East & West is underway. Bidding took place. Bid opening was Oct. 19. Reroofing to start soon. Started January 8, 2018.



Minidoka County School District
Monthly Maintenance Report
January 11, 2018

Maintenance Building

Before. Project taken a backseat to construction in schools. Project on hold until summer work is complete.



Food Service Building

Project on hold.



Heyburn

1) Flooring
Before

After



After - 100% of carpet installed in classrooms. Tiled floors to follow after school starts. It will be done after hours & weekends. A classroom or two at a time should be done around the 7th of November. Hallways are done. We have a few more items to finish up.

West

- 1) Modular - advertisement for bid is Nov. 1 & 8. Bid opening is to take place Dec 8. We declined the bids.
- 2) Marquee – took the old marquee down and got it ready for the new marquee.

Minidoka County School District
Monthly Maintenance Report
January 11, 2018


DSC

- 1) New locks on outside doors.


Paul

- 1) Sanded the walls for paint.

Before

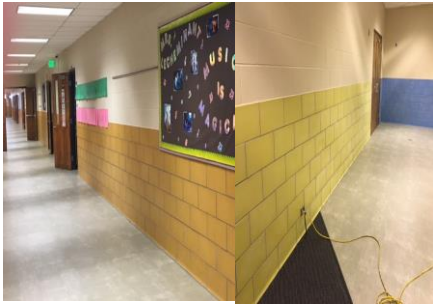

After

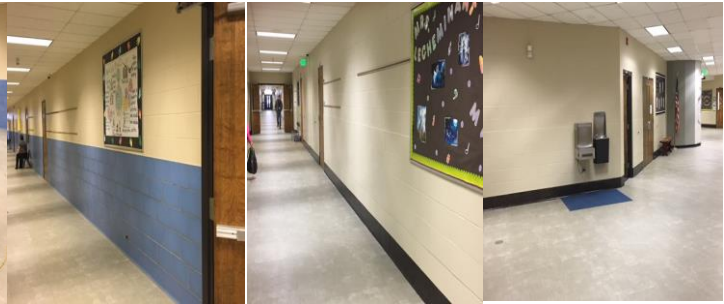

Acequia

- 1) Installed tv mounts.



- 2) New playground equipment has arrived with construction to begin soon.
