



**CENTENNIAL**

SCHOOL DISTRICT 12

CONNECTING. ACHIEVING. PREPARING.

# Summer Projects Update

**Board Meeting**

**August 18, 2025**

## **Approximately 30 Projects; 85% of Projects Complete**

- **Stadium Renovation (High School)**
- **Roofing Replacement (Blue Heron/High School West Gyms)**
- **Carpet Replacement Corridors (Centennial Elementary)**
- **Terrazzo Repair (High School)**
- **Parking Lot Sealing and Striping (Blue Heron/Middle/High)**
- **Chip Seal 2 Parking Lots (Middle School)**
- **Fire Panel Upgrades (Blue Heron and Middle School)**
- **Playground Equipment (Centennial Elementary)**
- **Playground Mulch (All Sites)**
- **Mechanical Repairs**
- **Teaching and Learning Office Remodel**
- **Painting**
- **Sink/Water Fountains Replacement**

Blue Heron & High School Replacement

Project Budget \$1.4M

Weekly Progress Update



Progress Summary  
(Total = 330 squares)

**Date:** 8-11-25

**Last Week:** 48 squares completed


**This Week:** Sheet Metal Fabrication.

**To Date:** 330 of 330 squares complete

**To Date:** 100% roofing complete

**Notes:** The roofing crew finished the last remaining sections of roof work. All ground equipment has been removed from the job site.

Completed Areas



Centennial School District #12

4707 North Road

Circle Pines, MN 55014


SHEET TITLE:

Roof Plan

SHEET NO.:

A1

Weekly Progress Update

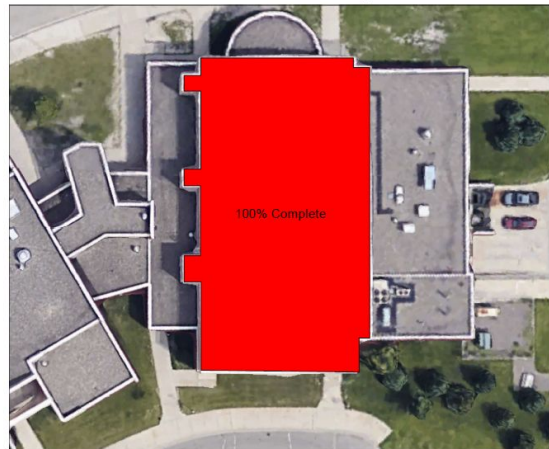

Progress Summary  
(Total = 110 squares)

**Date:** 7-21-25

**Last Week:** 100 squares completed

**This Week:** Gravel & tear down.

**To Date:** 110 of 110 squares complete

**To Date:** 100% roofing complete

**Notes:** The new roof system is 100% complete over the gymnasium. They need one more day to install the gravel surfacing. After complete they will be tearing down equipment and moving back to the High School.

Completed Areas



Centennial School District #12

4707 North Road

Circle Pines, MN 55014

SHEET TITLE:

Roof Plan

SHEET NO.:

A1

# High School Roof Replacement





# Blue Heron Roof Replacement



# Stadium Renovation

## Project Budget \$2.6M

- Turf
- Track
- Scoreboard
- Lighting
- Buried Electrical
- Asphalt Restoration
- Underground Raceway
- Fencing
- Wireless Access Control Boxes
- New Wiring
- Batting Cages (Repurposed Turf)





# Removal/Sub Cutting/Grade



# Grading/Preparation/Underground Utilities





# Track Sub Base



## Electrical/Lighting





# Turf Install





# Turf Install



## Turf Install/Fencing





# Finishing Touches





# Questions?



**CENTENNIAL**  
SCHOOL DISTRICT 12

CONNECTING. ACHIEVING. PREPARING.
