# Crosby ISD Construction Update



October 19, 2026

# Administration Building

**Completion:** Summer 2027

**Architect:** Stantec

**General Contractor:** TBD

**Current Status:**

- Recommendation of Millenium as selected Contractor

**Upcoming Milestones:**

- Construction Kick off Meeting October 30, 2026
- Site Mobilization early November.



# Red Barn

**Completion**: Summer 2027

**Architect:** Pfluger


**General Contractor:** TBD December 2026

**Current Status:**

- 95% Construction Documents
- Defined Scope to include Red Barn and White Barn
- Submitted for Permitting October 8,2026.

**Upcoming Milestones:**

- General Contractor Selection December 2026.

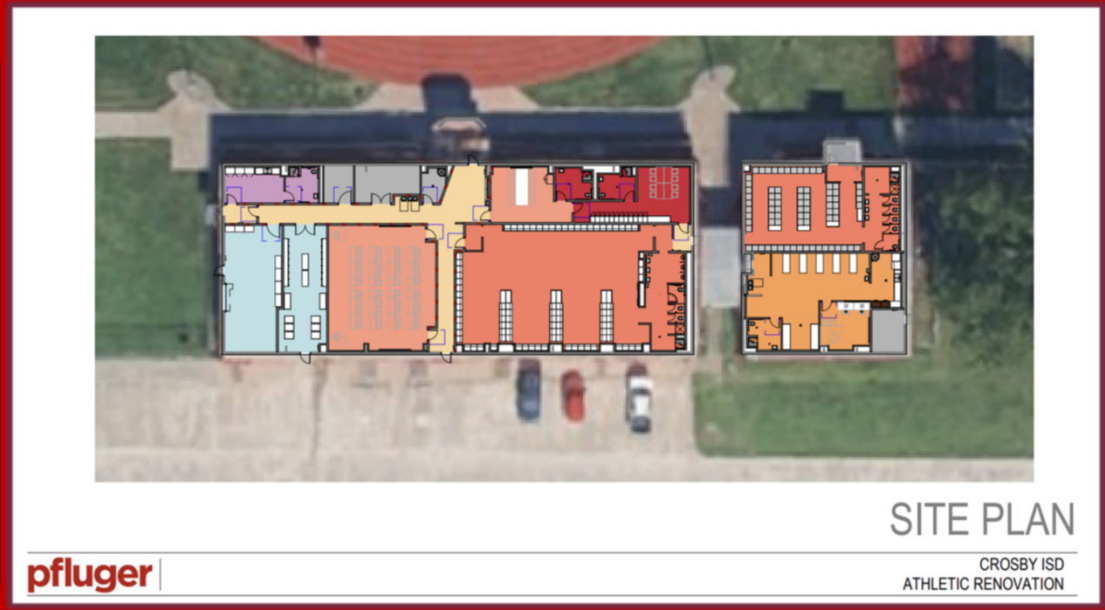

# Crosby Sixth Grade Campus

**Completion:** June 18, 2027

**Architect:** Stantec

**General Contractor:** Gamma

**Current Status :**

- 100% Complete on Detention Pond
- 100% Slab Pour

**Upcoming Milestones:**

- Steel Erection and Decking through October and Early November



# Crosby Sixth Grade Campus

