BOND PROJECT UPDATES
AS OF: NOVEMBER 16, 2026

BASEBALL AND SOFTBALL STADIUMS – FIELD LIGHTING UPGRADE

Contracts Awarded to:

Engineer:	Stridde, Callins & Associates, Inc.
Contractor:	Musco Sports Lighting, LLC



Project Timelines:

Board Approved Contracts/Purchases:	April 20, 2026
Contracts Awarded & Purchase Orders Issued:	April 21, 2026
Project Start Date:	September 30, 2026
Estimated Project Completion Date:	November 30, 2026

Project Updates:

The light installation is complete at both fields. The contractor is working on installing the controllers and Show Lights features in the coming weeks. The project will be substantially complete by November 30, 2026.

Project Photos:

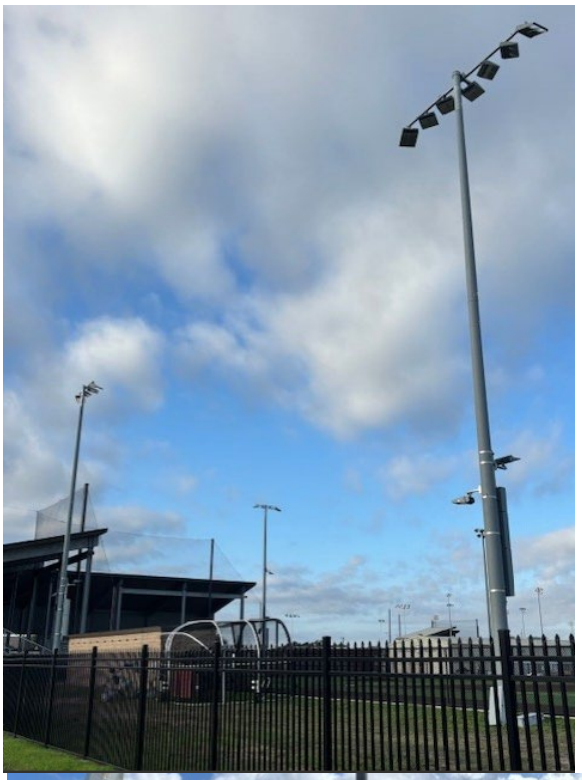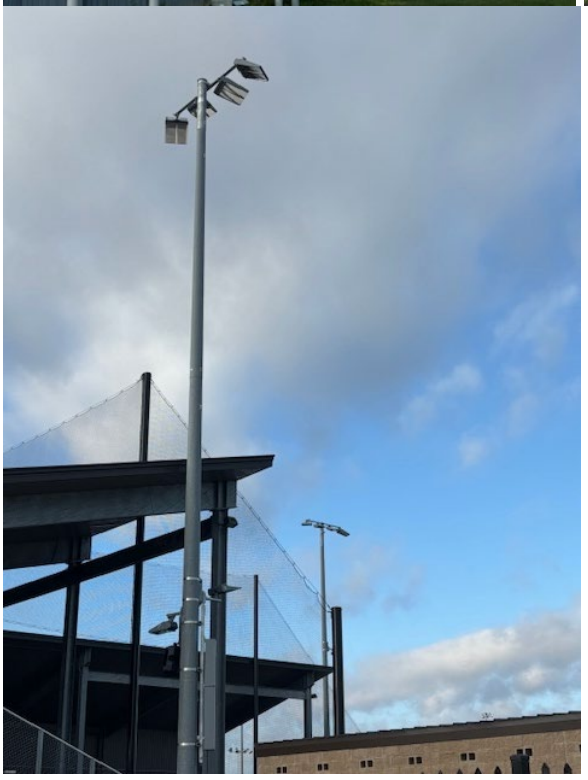
PHIL DANAHER STADIUM – STADIUM RENOVATION & PRESS BOX REPLACEMENT

Contracts Awarded to:

Architect:	Rawley McCoy & Associates
Contractor:	B.E. Beecroft Company

Project Timelines:

Board Approved Contracts/Purchases:	December 2, 2025
Contracts Awarded & Purchase Orders Issued:	December 5 2025
Project Start Date:	December 8, 2025
Estimated Project Completion Date:	August 31, 2026


Project Updates:


The project was substantially complete on August 31, 2026. Site work and final construction cleanup have begun. The contractor is finishing final punch list items in the coming weeks.

Project Photos:





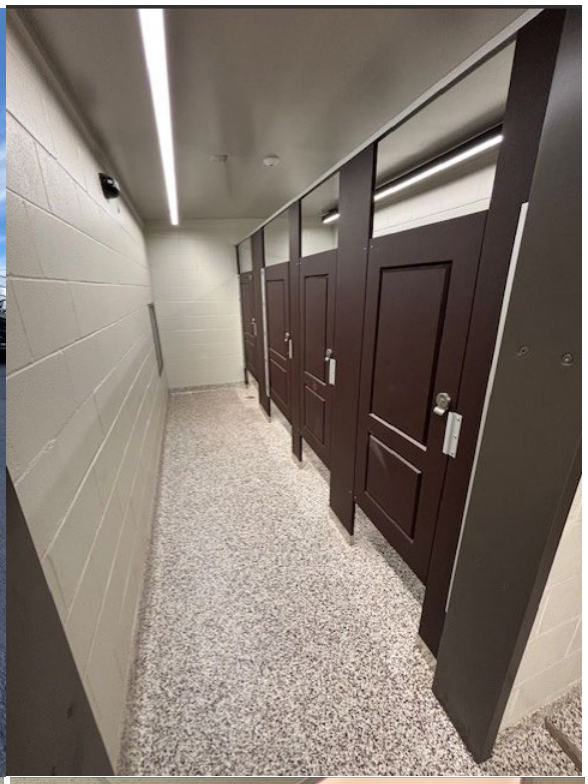

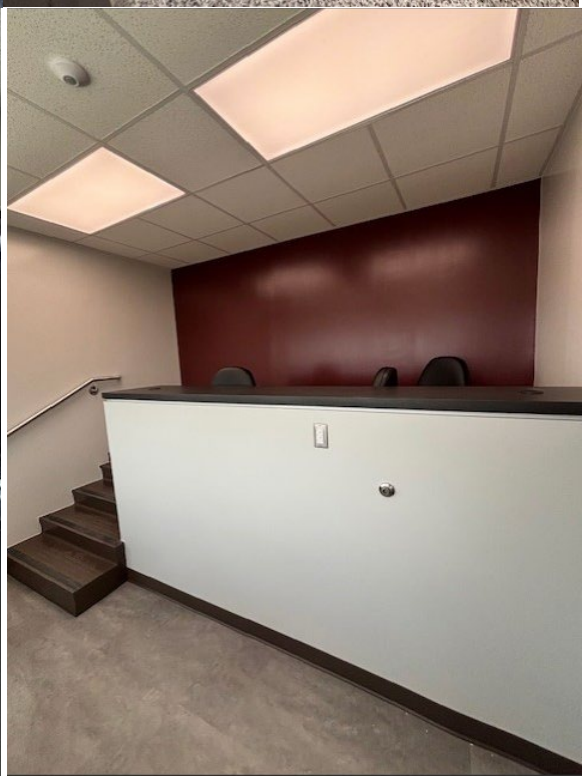



PHIL DANAHER STADIUM – SCORE BOARD REPLACEMENT

Contracts Awarded to:

Independent Design Representative:	Stridde, Callins & Associates, Inc. Wilkerson & Sanders, Inc.
Contractor:	Nevco Sports, LLC


Project Timelines:

Board Approved Contracts/Purchases:	July 14, 2025
Contracts Awarded & Purchase Orders Issued:	August 5, 2025
Estimated Project Start Date:	January 1, 2026
Estimated Project Completion Date:	August 31, 2026

Project Updates:
The project was substantially complete on August 31, 2026. The contractor is finishing final punch list items in the coming weeks.

Project Photos:



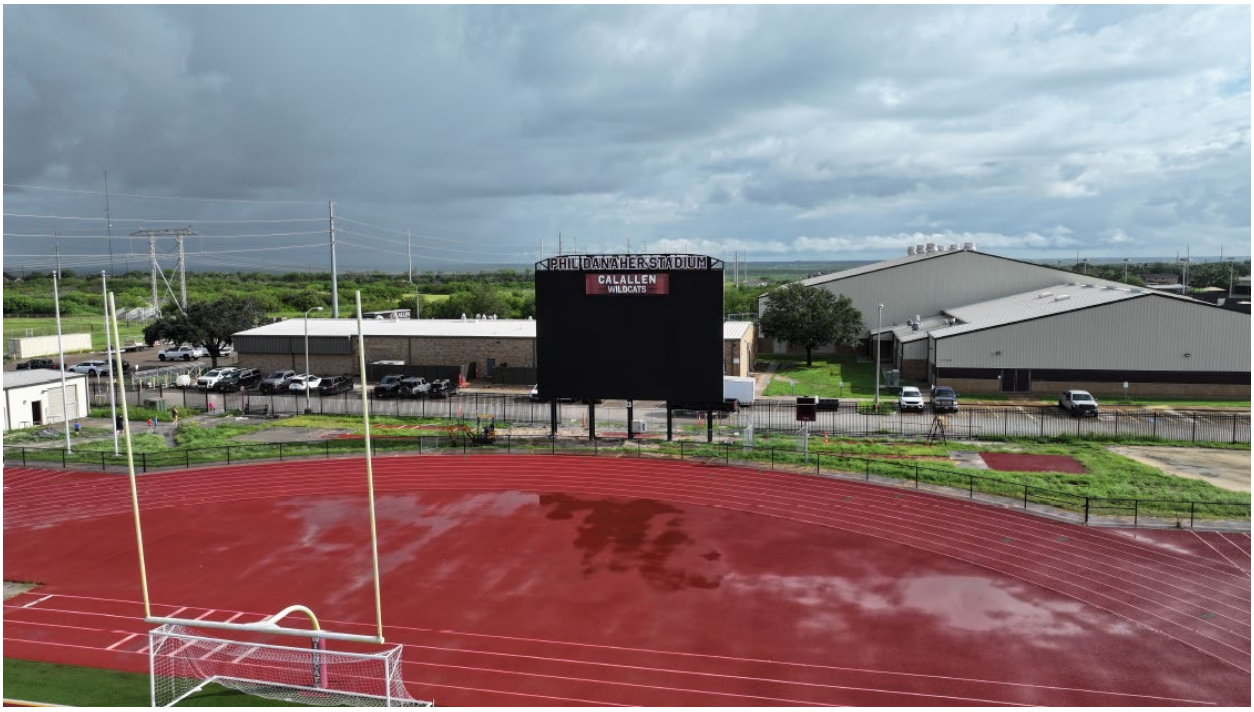

GENERAL PLANNING COSTS

All Bond 2024 Projects

Legal Services:
Walsh Gallegos
Estimated expenditures $20,000
Administration continues to work closely with legal counsel to negotiate and finalize contracts for the Bond 2024 program. Utilizing the assistance of legal counsel ensures that the Bond 2024 program is compliant with all applicable laws during every phase.

Architect Services:
Rawley McCoy and Associates, PLLC
Rawley McCoy and Associates' (RMA) contract was awarded at the May 13, 2024 Board Meeting. Future updates on RMA's progress can be found on the specific projects updates above.

Civil Engineering Services:
York Engineering
Estimated expenditures $40,000
Bond 2024 engineering contracts were awarded at the May 13, 2024 Board Meeting. Future updates on York Engineering's progress can be found on the specific projects updates above.

MEP Engineering Services:
Stridde, Callins & Associates, Inc.
Estimated expenditures $75,000
Bond 2024 engineering contracts were awarded at the May 13, 2024 Board Meeting. Future updates on York Engineering's progress can be found on the specific projects updates above.

Structural Engineering Services:
Wilkerson & Sanders, Inc
Estimated expenditures $25,000
Bond 2024 engineering contracts were awarded at the May 13, 2024 Board Meeting. Future updates on York Engineering's progress can be found on the specific projects updates above.

Geotechnical Engineering and Construction Material Testing Services:
Intertek PSI
Estimated expenditures $25,000
Bond 2024 contracts were awarded at the June 24, 2024 Board Meeting. Administration will begin scheduling these services as needed throughout project design and implementation.
