Crosby ISD Construction Update



November 16, 2026

Administration Building

Completion: Summer 2027

Architect: Stantec

General Contractor: Millennium Project Solutions

Current Status:

- Pre-construction Meeting
  November 10, 2026

Upcoming Milestones:

- Complete Site Mobilization and selective demoing this November.



Red Barn

Completion: Summer 2027

Architect: Pfluger


General Contractor: TBD December 2026

Current Status:

- Pre-proposal meeting and site walk November 10, 2026.
- Submitted for Permitting October 8, 2026 and awaiting comments.

Upcoming Milestones:

- General Contractor Selection December 2026.

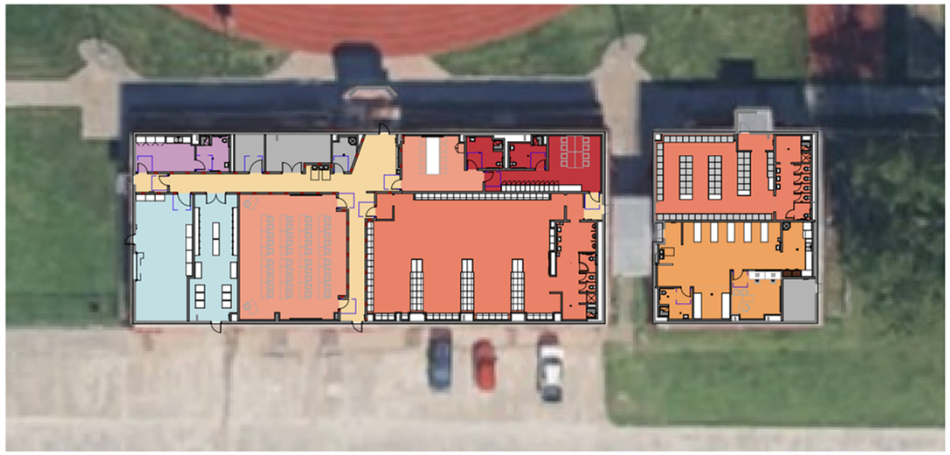

Crosby Sixth Grade Campus

Completion: June 18, 2027

Architect: Stantec

General Contractor: Gamma

Current Status :

- 80% Area B CMU Walls
- 40% Roof Steel Joist
- Starting to work on the Rough-In

Upcoming Milestones:

- Enclosing Exterior Walls By December



Crosby Sixth Grade Campus



