JOB: 21062 Lakeview HS Facility Upgrades
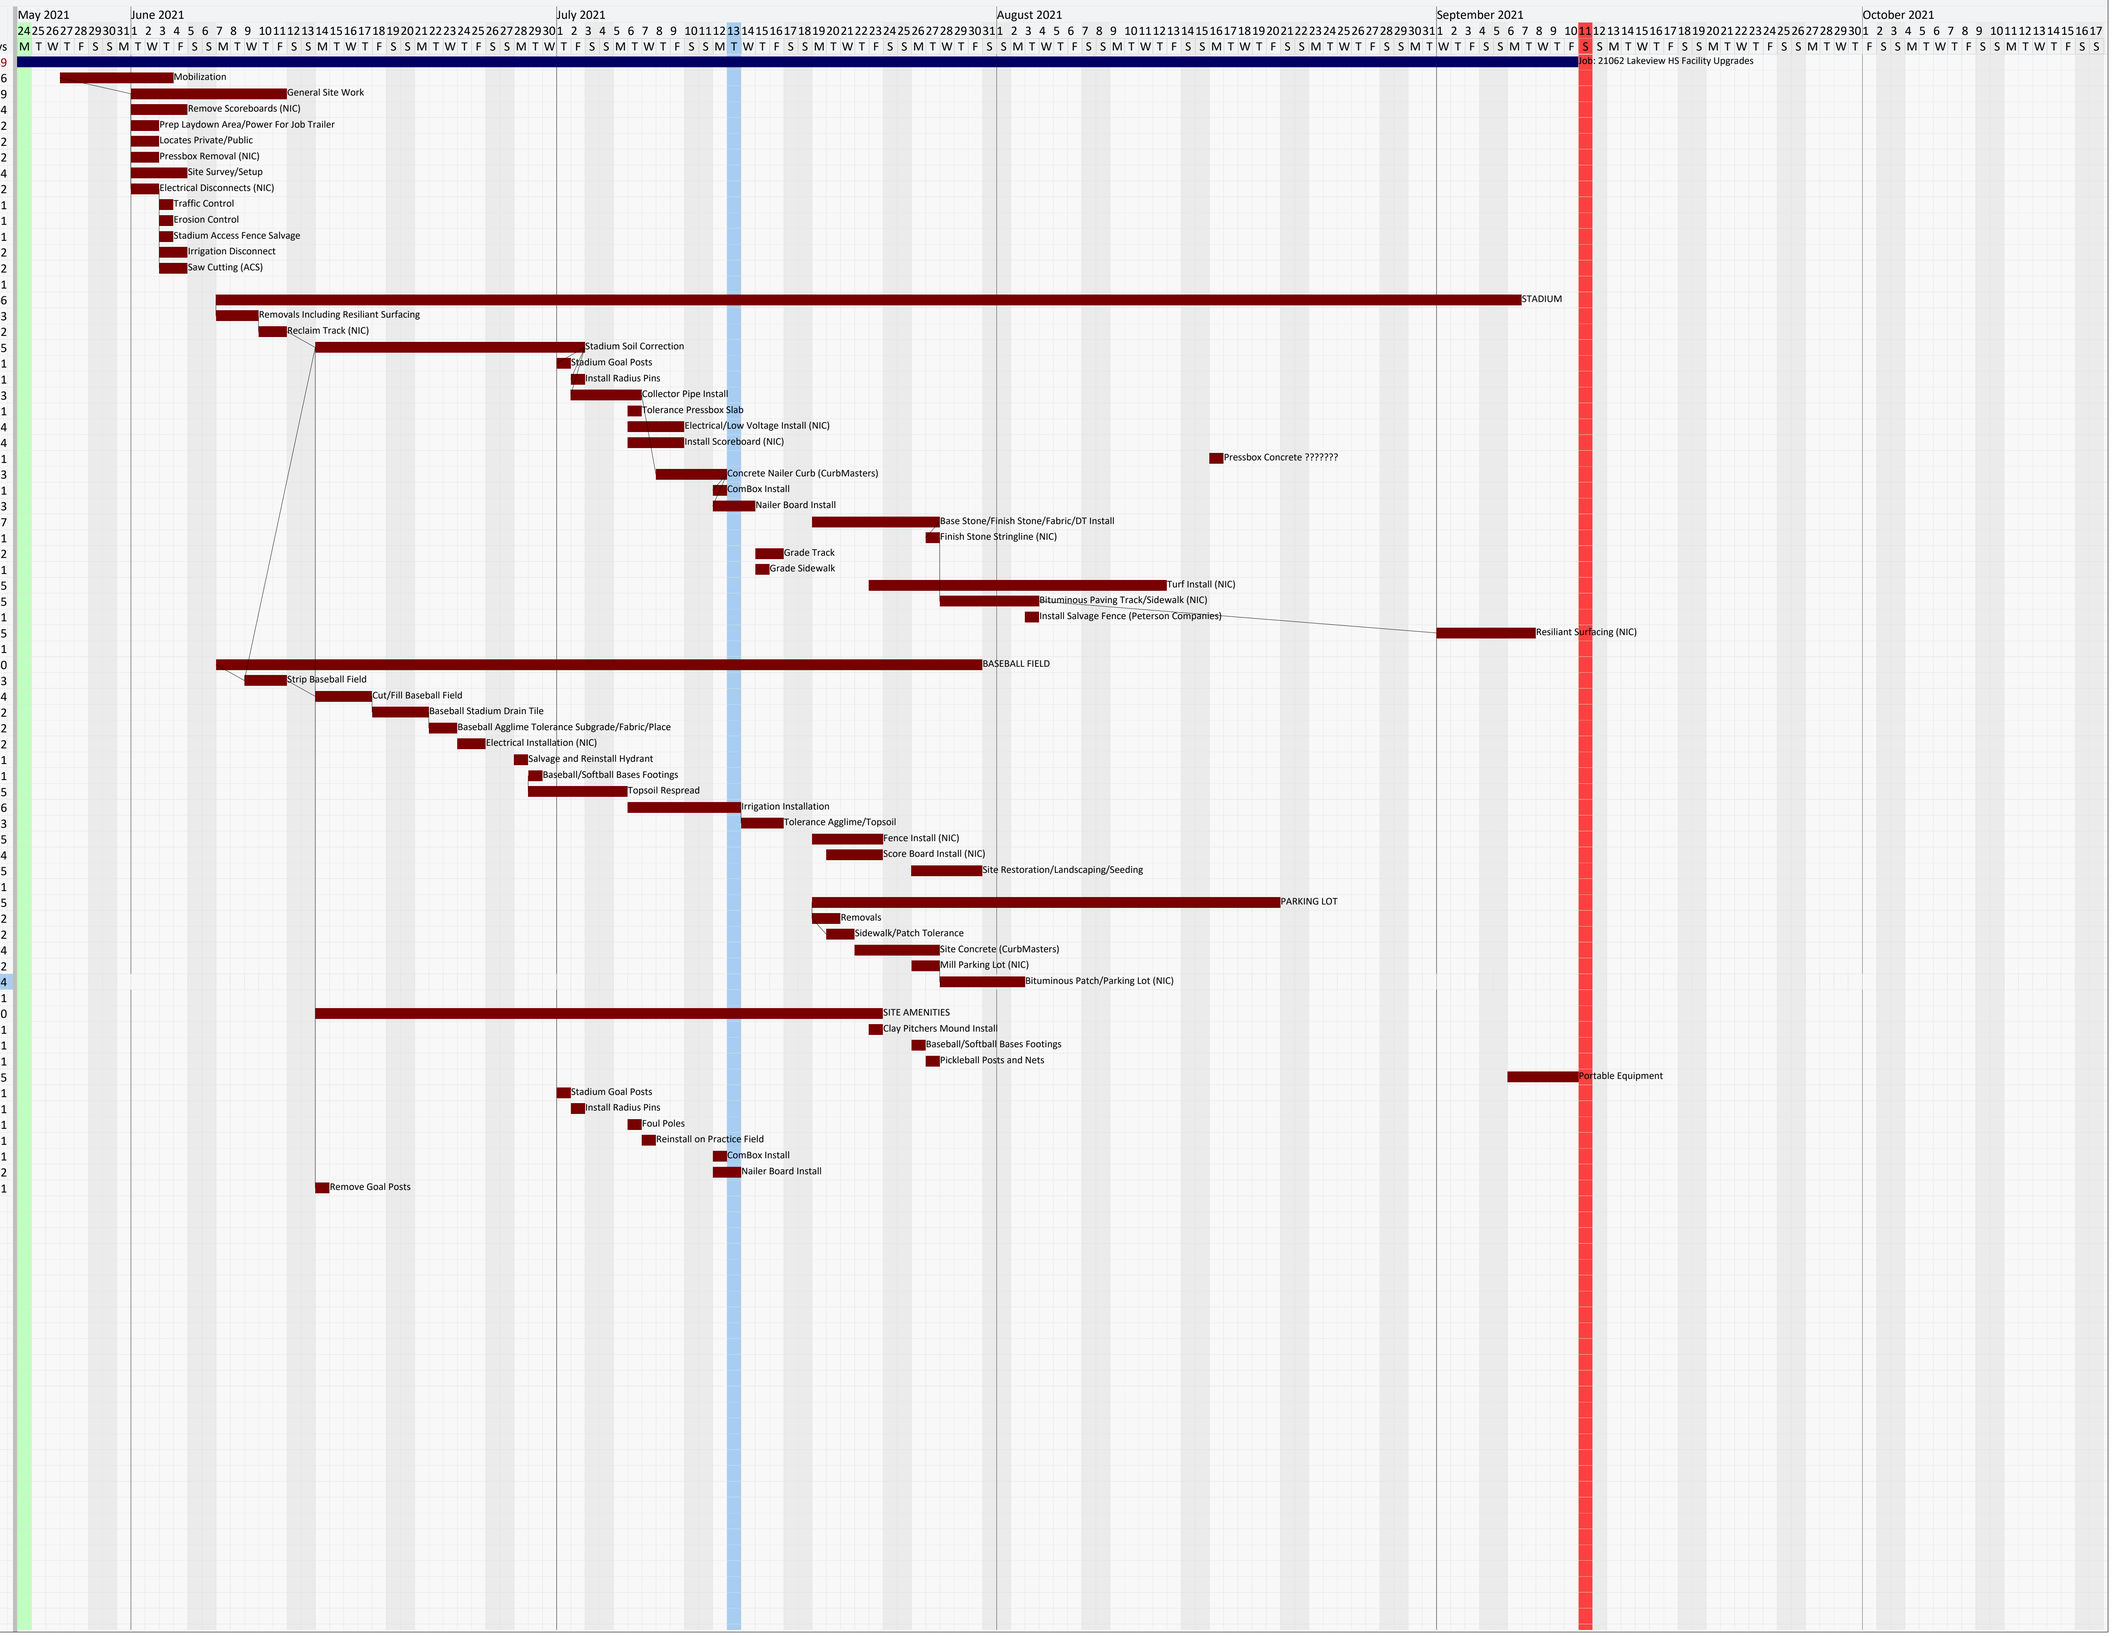
S	M	Start Date	Finish Date	Description	Days
		5/11	9/10	Lakeview HS Facility Upgrades	89
		5/27	6/3	Mobilization	6
		6/1	6/11	General Site Work	9
		6/1	6/4	Remove Scoreboards (NIC)	4
		6/1	6/2	Prep Laydown Area/Power For Job Trailer	2
		6/1	6/2	Locates Private/Public	2
		6/1	6/2	Pressbox Removal (NIC)	2
		6/1	6/4	Site Survey/Setup	4
		6/1	6/2	Electrical Disconnects (NIC)	2
		6/3	6/3	Traffic Control	1
		6/3	6/3	Erosion Control	1
		6/3	6/3	Stadium Access Fence Salvage	1
		6/3	6/4	Irrigation Disconnect	2
		6/3	6/4	Saw Cutting (ACS)	2
		5/11	5/11		1
		6/7	9/6	STADIUM	66
		6/7	6/9	Removals Including Resiliant Surfacing	3
		6/10	6/11	Reclaim Track (NIC)	2
		6/14	7/2	Stadium Soil Correction	15
		7/1	7/1	Stadium Goal Posts	1
		7/2	7/2	Install Radius Pins	1
		7/2	7/6	Collector Pipe Install	3
		7/6	7/6	Tolerance Pressbox Slab	1
		7/6	7/9	Electrical/Low Voltage Install (NIC)	4
		7/6	7/9	Install Scoreboard (NIC)	4
		8/16	8/16	Pressbox Concrete ???????	1
		7/8	7/12	Concrete Nailer Curb (CurbMasters)	3
		7/12	7/12	ComBox Install	1
		7/12	7/14	Nailer Board Install	3
		7/19	7/27	Base Stone/Finish Stone/Fabric/DT Install	7
		7/27	7/27	Finish Stone Stringline (NIC)	1
		7/15	7/16	Grade Track	2
		7/15	7/15	Grade Sidewalk	1
		7/23	8/12	Turf Install (NIC)	15
		7/28	8/3	Bituminous Paving Track/Sidewalk (NIC)	5
		8/3	8/3	Install Salvage Fence (Peterson Companies)	1
		9/1	9/7	Resiliant Surfacing (NIC)	5
		5/11	5/11		1
		6/7	7/30	BASEBALL FIELD	40
		6/9	6/11	Strip Baseball Field	3
		6/14	6/17	Cut/Fill Baseball Field	4
		6/18	6/21	Baseball Stadium Drain Tile	2
		6/22	6/23	Baseball Agglime Tolerance Subgrade/Fabric/Place	2
		6/24	6/25	Electrical Installation (NIC)	2
		6/28	6/28	Salvage and Reinstall Hydrant	1
		6/29	6/29	Baseball/Softball Bases Footings	1
		6/29	7/5	Topsoil Respread	5
		7/6	7/13	Irrigation Installation	6
		7/14	7/16	Tolerance Agglime/Topsoil	3
		7/19	7/23	Fence Install (NIC)	5
		7/20	7/23	Score Board Install (NIC)	4
		7/26	7/30	Site Restoration/Landscaping/Seeding	5
		5/11	5/11		1
		7/19	8/20	PARKING LOT	25
		7/19	7/20	Removals	2
		7/20	7/21	Sidewalk/Patch Tolerance	2
		7/22	7/27	Site Concrete (CurbMasters)	4
		7/26	7/27	Mill Parking Lot (NIC)	2
		7/28	8/2	Bituminous Patch/Parking Lot (NIC)	4
		5/11	5/11		1
		6/14	7/23	SITE AMENITIES	30
		7/23	7/23	Clay Pitchers Mound Install	1
		7/26	7/26	Baseball/Softball Bases Footings	1
		7/27	7/27	Pickleball Posts and Nets	1
		9/6	9/10	Portable Equipment	5
		7/1	7/1	Stadium Goal Posts	1
		7/2	7/2	Install Radius Pins	1
		7/6	7/6	Foul Poles	1
		7/7	7/7	Reinstall on Practice Field	1
		7/12	7/12	ComBox Install	1
		7/12	7/13	Nailer Board Install	2
		6/14	6/14	Remove Goal Posts	1
