William Walker Replacement

Prepared By: Megan Finch

ID	Task Mode	Task Name	Duration	Start	Finish
0		**WW Construction**	**174 days**	**Thu 12/20/18**	**Mon 8/26/19**
1		**Building**	**174 days**	**Thu 12/20/18**	**Mon 8/26/19**
2		Steel Erection	50 days	Thu 12/20/18	Fri 3/1/19
3		Slab on Metal Deck	35 days	Tue 1/22/19	Mon 3/11/19
4		Metal Stud Framing	94 days	Wed 1/23/19	Tue 6/4/19
5		MEP Rough-in	51 days	Wed 2/20/19	Wed 5/1/19
6		Roof Structure	39 days	Wed 1/23/19	Mon 3/18/19
7		Roofing	44 days	Wed 2/6/19	Mon 4/8/19
8		Exterior Finshes	85 days	Wed 1/30/19	Wed 5/29/19
9		Interior Finshes	52 days	Wed 4/24/19	Mon 7/8/19
10		MEP Trim	25 days	Wed 5/22/19	Wed 6/26/19
11		Final Building Completition	31 days	Thu 6/27/19	Fri 8/9/19
12		BSD Furnish Building	10 days	Mon 8/12/19	Fri 8/23/19
13		**Site**	**140 days**	**Mon 1/21/19**	**Tue 8/6/19**
14		Constructed Covered Play	70 days	Mon 1/21/19	Fri 4/26/19
15		Complete Storm System	25 days	Mon 1/21/19	Fri 2/22/19
16		Concrete at Entry and South	15 days	Mon 2/25/19	Fri 3/15/19
17		Complete Drop-Off Loops	55 days	Mon 3/18/19	Mon 6/3/19
18		Complete Play Area/Courtyard	45 days	Tue 6/4/19	Tue 8/6/19
19		Complete East Parking Lot	30 days	Mon 1/21/19	Fri 3/1/19
20		Lynnfield Lane Work	60 days	Mon 1/21/19	Fri 4/12/19
21		School Starts	1 day	Mon 8/26/19	Mon 8/26/19

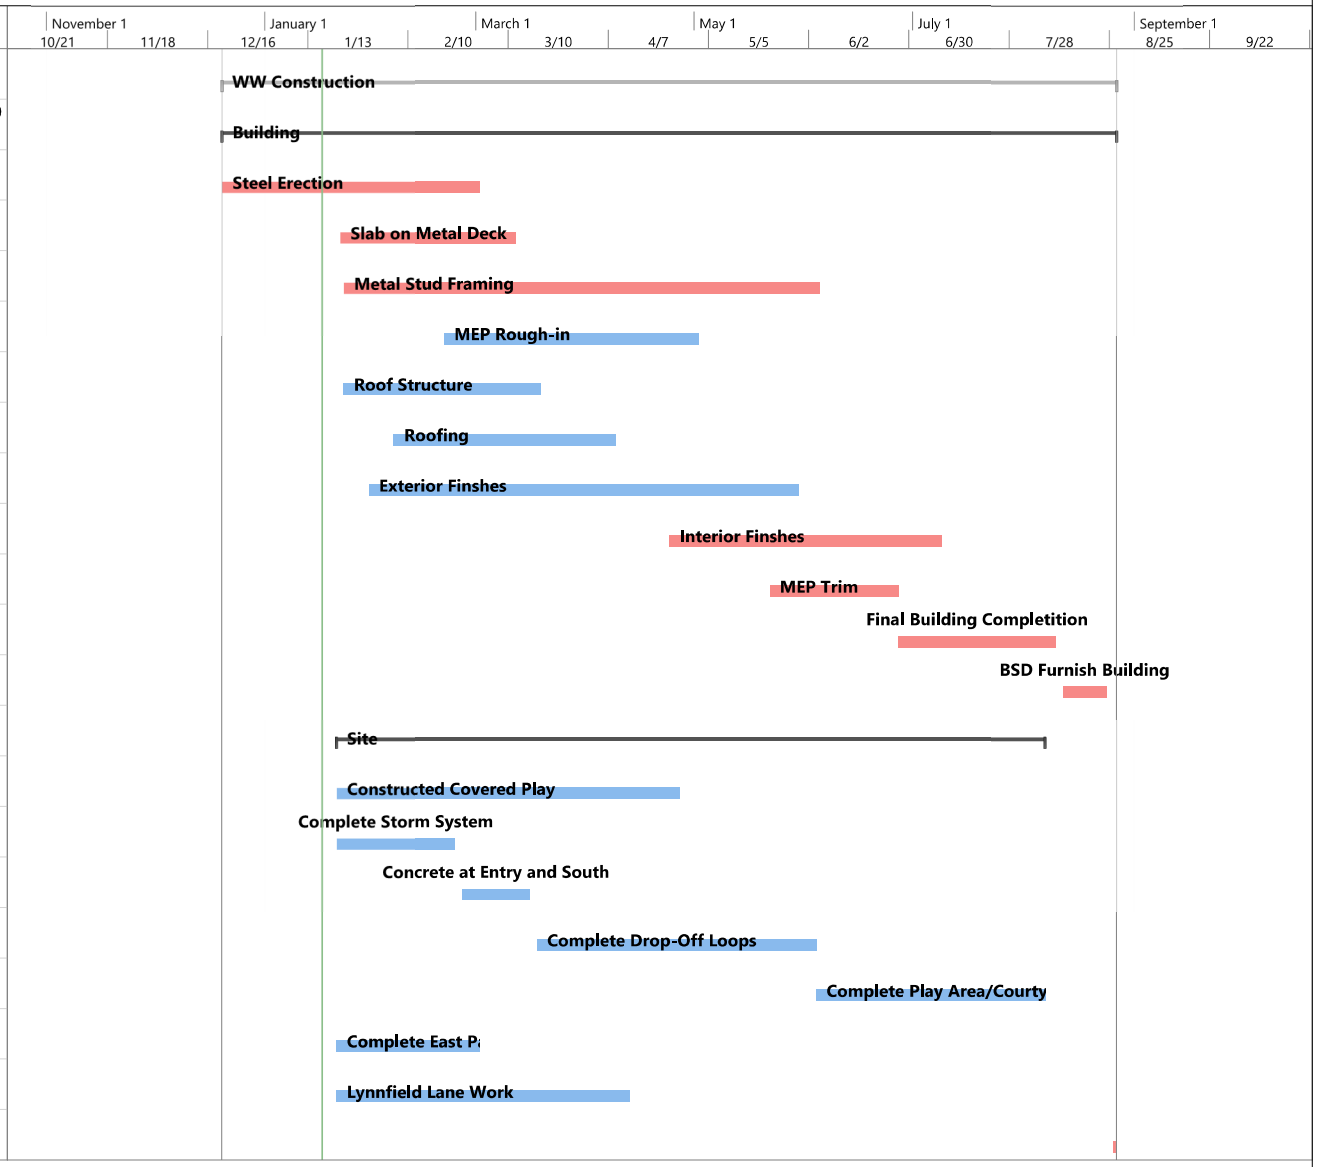

1/22/19
