



NOTICE is hereby given that the Collin County Community College District Board of Trustees will hold a meeting of the Campus Facilities and Construction Committee (Hardin, Gomel, and Saad) at 6:00 p.m. on Tuesday, October 20, 2020, in the President's Conference Room 407 at the Collin Higher Education Center, 3452 Spur 399, McKinney, Texas 75069.

Locations

Collin Higher Education Center
McKinney, Texas

Courtyard Center
Plano, Texas

Frisco Campus

McKinney Campus

Plano Campus

Public Safety Training Center
McKinney, Texas

Rockwall Center

Technical Campus
Allen, Texas

Wylie Campus

PUBLIC COMMENT

REVIEW AND DISCUSSION ITEMS

- | | |
|---|----|
| 1. Consideration of Approval Authorizing the District President to Contract with The Gordian Group to Provide a Customized Job Order Contract (JOC) Complete Solution for the District | 2 |
| 2. Consideration of Approval Authorizing the Construction Manager-at-Risk Contract with Skanska Building USA, Inc. ("Skanska") for the Construction of the Alumni Hall Fire Lane at the Frisco Campus | 7 |
| 3. AECOM Monthly Report for September 2020 | 10 |

*J. Robert Collins, Ph.D.
Chairman, Board of Trustees*

iCollin

www.collin.edu

Board of Trustees

J. Robert Collins, Ph.D.,
Chair

Andrew Hardin,
Vice Chair

Jim Orr,
Secretary

Raj Menon, Ph.D.,
Treasurer

Stacy Anne Arias

Stacey Donald, Ph.D.

Greg Gomel

Fred Moses

Jay Saad

District President

H. Neil Matkin, Ed.D.

3452 Spur 399

P.O. Box 8021

McKinney, Texas 75070

P | 972.758.3800

F | 972.758.3807

nmatkin@collin.edu

www.collin.edu

Collin County Community College District Board of Trustees

1. Campus Facilities and Construction Committee

October 20, 2020

Resource: Christopher G. Eyle
Vice President of Facilities & Construction

DISCUSSION ITEM: Consideration of Approval Authorizing the District President to Contract with The Gordian Group to Provide a Customized Job Order Contract (JOC) Complete Solution for the District

DISCUSSION: The District currently utilizes Gordian’s ezIQC JOC program, which is offered through the BuyBoard and Sourcewell Cooperative Purchasing Networks. Because we use Gordian’s ezIQC JOC program through purchasing cooperatives, the District pays additional fees (ranging from 1.25% for BuyBoard or 2.25% for Sourcewell) above a project’s cost.

A customized JOC for Collin College can realize numerous benefits. If a Gordian customized JOC Complete Solution is implemented, the District will save co-op fees, have a more accurately priced construction catalog, potentially more loyal and responsive contractors, as well as have the option of utilizing Gordian Construction Management for each project.

There is no cost to establish a customized JOC for Collin College. Gordian’s fees are added to a project’s total and only paid when a work order is issued.

Gordian provides a single point of responsibility for all of the products and services necessary for a JOC program. Gordian’s in-house staff will prepare, customize, support, input the contract documents, construction task catalogs, technical specifications, and the eGordian Information Management System.

With a Collin College customized JOC, Gordian will prepare a fully customized Gordian Construction Task Catalog, which is structured according to the College’s needs. The College can include the goods and services relevant to it at labor rates that are unique to our market. There is a bottom-line benefit to that customization in our book that cannot be achieved by sharing a book with other cooperative purchasing clients.

When using a cooperative’s JOC program, the College uses the cooperative’s awarded contractors. With a Collin College specific JOC, the College would have its own customized

program with a list of awarded contractors who are committed to Collin College and its needs. There is a bottom-line benefit in having contractors who do not share loyalty with the co-op or with other co-op clients. They are committed to Collin College and its goals, both short and long-term.

The table below outlines the differences between the existing ezIQC JOC and a customized JOC:

	ezIQC JOC	Customized Collin College JOC
Co-op Administrative Fees	1.25% (Buyboard), 2.25% (Sourcewell)	0%
Construction Catalog	Regional Pricing	Customized Local Pricing (more accurate)
Contractors Loyalty	Regional/Co-Op JOC clients	Collin College
Licensing, Software, Job Order Development Fees	5.25%	5.25%
Contractor Licensing Fee	1%	1%
Construction Management Option / Fee	N	Y / 6.01%

Gordian has been awarded a contract through Sourcewell’s Cooperative Purchasing Program, Contract No. 071415-GGI, which is available for use by the District and complies with the competitive procurement requirements outlined in Section 44.031 of the Texas Education Code, as permitted under Section 791.011 of the Texas Government Code.

A customized JOC provides the best value to the District for the projects that will be completed under this method and is an allowed project delivery method for construction-related goods and services under Government Code 2269.

Collin County Community College District Board of Trustees

2020-10-X

October 27, 2020

Resource: Christopher G. Eyle
Vice President of Facilities & Construction

AGENDA ITEM: Report Out of the Campus Facilities and Construction Committee and Consideration of Approval Authorizing the District President to Contract with The Gordian Group to Provide a Customized Job Order Contract (JOC) Complete Solution for the District

DISCUSSION: The District currently utilizes Gordian's ezJOC JOC program, which is offered through the BuyBoard and Sourcewell Cooperative Purchasing Networks. Because we use Gordian's ezJOC JOC program through purchasing cooperatives, the District pays additional fees (ranging from 1.25% for BuyBoard or 2.25% for Sourcewell) above a project's cost.

A customized JOC for Collin College can realize numerous benefits. If a Gordian customized JOC Complete Solution is implemented, the District will save Co-op fees, have a more accurately priced construction catalog, potentially more loyal and responsive contractors, as well as have the option of utilizing Gordian Construction Management for each project.

There is no cost to establish a customized JOC for Collin College. Gordian's fees are added to a project's total and only paid when a work order is issued.

Gordian provides a single point of responsibility for all of the products and services necessary for a JOC program. Gordian's in-house staff will prepare, customize, support, input the contract documents, construction task catalogs, technical specifications, and the eGordian Information Management System.

With a Collin College customized JOC, Gordian will prepare a fully customized Gordian Construction Task Catalog, which is structured according to the College's needs. The College can include the goods and services relevant to it at labor rates that are unique to our market. There is a bottom-line benefit to that customization in our book that cannot be achieved by sharing a book with other cooperative purchasing clients.

When using a cooperative’s JOC program, the College uses the cooperative’s awarded contractors. With a Collin College specific JOC, the College would have its own customized program with a list of awarded contractors who are committed to Collin College and its needs. There is a bottom-line benefit in having contractors who do not share loyalty with the co-op or with other co-op clients. They are committed to Collin College and its goals, both short and long-term.

The table below outlines the differences between the existing ezIQC JOC and a customized JOC:

	ezIQC JOC	Customized Collin College JOC
Co-op Administrative Fees	1.25% (Buyboard), 2.25% (Sourcewell)	0%
Construction Catalog	Regional Pricing	Customized Local Pricing (more accurate)
Contractors Loyalty	Regional/Co-Op JOC clients	Collin College
Licensing, Software, Job Order Development Fees	5.25%	5.25%
Contractor Licensing Fee	1%	1%
Construction Management Option / Fee	N	Y / 6.01%

Gordian has been awarded a contract through Sourcewell’s Cooperative Purchasing Program, Contract No. 071415-GGI, which is available for use by the District and complies with the competitive procurement requirements outlined in Section 44.031 of the Texas Education Code, as permitted under Section 791.011 of the Texas Government Code.

A customized JOC provides the best value to the District for the projects that will be completed under this method and is an allowed project delivery method for construction-related goods and services under Government Code 2269.

**DISTRICT PRESIDENT'S
RECOMMENDATION:**

The District President recommends approval of authorization to contract with The Gordian Group to provide a customized Job Order Contract (JOC) Complete Solution for the District.

SUGGESTED MOTION:

This item comes as a motion and second out of committee. A suggested motion would be, "Mr. Chairman, I make a motion that the Board of Trustees of Collin County Community College District approves the authorization of the District President to contract with The Gordian Group to provide a customized Job Order Contract (JOC) Complete Solution for the District."

DRAFT

Collin County Community College District Board of Trustees

2. Campus Facilities and Construction Committee

October 20, 2020

Resource: Christopher G. Eyle
Vice President of Facilities & Construction

DISCUSSION ITEM: Consideration of Approval Authorizing the Construction Manager-at-Risk Contract with Skanska Building USA, Inc. (“Skanska”) for the Construction of the Alumni Hall Fire Lane at the Frisco Campus

DISCUSSION: At the August 2020 Board meeting, the Board approved Skanska as the Construction Manager at Risk for the Phase 3 Renovations and Additions at the Frisco Campus and the Board authorized the District President to negotiate and enter into a Construction Manager-at-Risk contract with Skanska for this work at the Frisco Campus. A portion of this work is the renovation and addition of the kitchen and dining area at Alumni Hall. Before this work can begin, a new fire lane that allows fire truck access within a 150’ distance from any portion of Alumni Hall must be installed per current City code.

Skanska has been providing pre-construction services for the Phase 3 work as defined by the executed contract. Part of these services include providing an estimate of the fire lane work. Upon request of Collin Facilities and AECOM, Skanska has provided a Guaranteed Maximum Price proposal that is within the established project budget for the fire lane work. Upon approval of the Guaranteed Maximum price, the previously executed contract will be amended allowing for the issuance of a Notice to Proceed to commence the Construction Phase of the Contract.

The amount of the Guaranteed Maximum Price is \$1,258,671, which includes \$1,208,671 for Construction Costs and \$50,000 of Owner’s Contingency. The planned completion date is March 25, 2021.

Collin County Community College District Board of Trustees

2020-10-X

October 27, 2020

Resource: Christopher G. Eyle
Vice President of Facilities & Construction

AGENDA ITEM:

Report Out of the Campus Facilities and Construction Committee and Consideration of Approval Authorizing the Construction Manager-at-Risk Contract with Skanska Building USA, Inc. ("Skanska") for the Construction of the Alumni Hall Fire Lane at the Frisco Campus

DISCUSSION:

At the August 2020 Board meeting, the Board approved Skanska as the Construction Manager at Risk for the Phase 3 Renovations and Additions at the Frisco Campus and the Board authorized the District President to negotiate and enter into a Construction Manager-at-Risk contract with Skanska for this work at the Frisco Campus. A portion of this work is the renovation and addition of the kitchen and dining area at Alumni Hall. Before this work can begin, a new fire lane that allows fire truck access within a 150' distance from any portion of Alumni Hall must be installed per current City code.

Skanska has been providing pre-construction services for the Phase 3 work as defined by the executed contract. Part of these services include providing an estimate of the fire lane work. Upon request of Collin Facilities and AECOM, Skanska has provided a Guaranteed Maximum Price proposal that is within the established project budget for the fire lane work. Upon approval of the Guaranteed Maximum price, the previously executed contract will be amended allowing for the issuance of a Notice to Proceed to commence the Construction Phase of the Contract.

The amount of the Guaranteed Maximum Price is \$1,258,671, which includes \$1,208,671 for Construction Costs and \$50,000 of Owner's Contingency. The planned completion date is March 25, 2021.

DISTRICT PRESIDENT'S RECOMMENDATION:

The District President recommends approval of the Guaranteed Maximum Price in the amount of \$1,258,671 for the construction of the new fire lane at the Frisco Campus.

SUGGESTED MOTION:

This item comes as a motion and second out of committee. A suggested motion would be, “Mr. Chairman, I make a motion that the Board of Trustees of Collin County Community College District authorizes the District President or designee to execute pre-approved contract forms and all other documents to approve Skanska Building USA, Inc.’s Guaranteed Maximum Price in the amount of \$1,258,671 for the construction of the new fire lane at the Frisco Campus.”

DRAFT

Collin County Community College District Board of Trustees

3. Campus Facilities and Construction Committee

October 20, 2020

Resource: Adrian Grimes
AECOM Project Manager

DISCUSSION ITEM: AECOM Monthly Report for September 2020

DISCUSSION: AECOM Project Manager Adrian Grimes will review items on the Collin College 2017 Capital Improvement Program Monthly Report for September 2020.



Collin College

2017 Capital Improvement Program
Monthly Report
September 2020

Collin County Community College District

Project Reference: 60541060
Project Number: 60541060

October 07, 2020

Quality information

Prepared by




Nuria Cortes
Program Controls Manager

Checked by



Deputy Program Director

Approved By



Adrian Grimes
Program Director

Revision History

Revision	Revision date	Details	Authorized	Name	Position
First Publication	October 7, 2020	September '20 Report	Yes	Adrian Grimes	Program Director

Distribution List

# Hard Copies	PDF Required	Association / Company Name
	1	Dr. Neil Matkin / Collin College
	1	Chris Eyle / Collin College

Prepared for:

Collin County Community College District
3452 Spur 399
Suite 327
McKinney, TX 75069

Prepared by:

Nuria Cortes
Program Controls Manager
E: ncortes.aecom@collin.edu

AECOM
13355 Noel Road
4th Floor
Dallas TX, 75240
aecom.com

Copyright © 2020 by AECOM

All rights reserved. No part of this copyrighted work may be reproduced, distributed, or transmitted in any form or by any means without the prior written permission of AECOM.

Table of Contents

1.	Introduction.....	5
2.	Executive Summary	5
3.	Scope.....	6
3.1	Phase 1	6
3.2	Phase 2	6
3.3	Phase 3	7
4.	Community	7
4.1	Project Teams	7
4.1.1	Phase 1	7
4.1.2	Phase 2	8
4.1.3	Phase 3	9
4.2	Current Personnel Estimate.....	9
4.3	Community Outreach.....	10
5.	Schedule	10
5.1	Program.....	10
5.2	Phase 1	11
5.3	Phase 2	12
5.4	Phase 3	13
6.	Budget.....	14
6.1	Program Summary	14
6.2	Phase 1	14
6.3	Phase 2	15
6.4	Phase 3	16
6.5	Phase A	17
6.6	Additional Program Budgets	18
7.	Completed Items.....	18
7.1	General Program.....	18
7.2	Procurement	18
7.3	Design	18
7.4	Pre-Construction	18
7.5	Construction.....	19
7.6	Acceptance and Close-Out.....	19
8.	Pending Items.....	19
8.1	General Program.....	19
8.2	Procurement	19
8.3	Design	19
8.4	Pre-Construction	19
8.5	Construction.....	19
8.6	Acceptance and Close-Out.....	19
	Appendix A – Construction Progress Photos	20

1. Introduction

On May 6, 2017, voters approved Collin College's \$600 million bond proposal to facilitate a long-range plan to accommodate the projected population growth in Collin County over the next two decades. The program consists of 4 new campuses and 2 new facilities.

On May 16, 2017, in a special session, the Board of Trustees granted the District President authority to enter and negotiate into contract with AECOM Technical Services, Inc. (AECOM) to provide Program Management Services to the Collin College 2017 Capital Improvement Program. On May 25, 2017, Collin College issued a Notice to Proceed to AECOM. As part of these services, AECOM will deliver a monthly report to provide status and progress of key aspects of the Program.

2. Executive Summary

The Program is progressing as planned with no major issues to report at this time.

Completed and Pending Items

- Technical Campus – Punchlist is 95% complete. Test & Balance and Commissioning services is nearing completion. McCarthy is finishing up O&M's and Warranties, in preparation of turnover to the College.
- Wylie Campus – Final punch list items are completed at the Library. At the Campus Commons, waiting on the delivery of the auto-operator stand. At the Student Center, waiting of the delivery of 2 auto-operator stands. Kitchen exhaust fan will be replaced and ductwork will be re-routed.
- Page Southerland Page, Inc. was issued a PO for Design Services for the Frisco Campus Additions and Renovations on September 30th

Items of close attention

- Punch list items at the Technical and Wylie Campus

Budget Summary

- \$505,766,016 of the \$600,000,000 has been committed to-date in the form of contracts with various vendors. This represents 84.29% of the overall program budget committed.
- \$442,494,114 of the \$505,766,016 committed amount has been expended to-date. This represents 87.49% of the commitments to date and 73.75% of the program budget.

3. Scope

3.1 Phase 1

- Wylie Campus
 - Construction of a campus on a new approximately 97-acre site
 - The campus includes:
 - Campus Commons
 - Library
 - Student Center/Conference Center
 - Central Utility Plant
- Technical Campus
 - Construction of a Technical Campus on a new 32-acre site in Allen, Texas
 - The campus includes:
 - 450 space underground parking garage
 - Academic Building (includes space for dual credit students)
 - 3 Trade Bar Buildings to support CTE programs
 - Programs planned for inclusion include:
 - Advanced Manufacturing, Automotive, Construction, and Health Science

3.2 Phase 2

- Celina Campus
 - Construction of a campus on a new approximately 75-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Farmersville Campus
 - Construction of a campus on a new approximately 76-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Frisco Campus
 - Construction of a new IT Center building on the existing campus

3.3 Phase 3

- Additions and Renovations at Frisco Campus
 - Alumni Hall Renovations and Additions
 - Lawler Hall Renovations
 - Heritage Hall Upgrades
 - Founders Hall Renovations
 - Wayfinding
- Additional Frisco Campus Projects
 - Construction of a new fire lane, parking lot, and loop road on the existing campus
 - Trane Upgrades
- Additions and Renovations at McKinney Campus
 - Construction of a new Welcome Center on the existing campus
 - New Entry Drive and Parking
 - Pistol Range Demo
 - Classroom Building and Dining Renovations
 - Dental Hygiene Renovations
 - Wayfinding
- Additional McKinney Campus Projects
 - Trane Upgrades
- Additional Plano Campus Projects
 - Trane Upgrades
 - Wayfinding
- Additional Courtyard Center Projects
 - Trane Upgrades
- Additional CHEC Projects
 - Trane Upgrades

4. Community

4.1 Project Teams

4.1.1 Phase 1

- Wylie Campus
 - Program Manager: AECOM Technical Services, Inc. (under contract)
 - A/E: Page Southerland Page, Inc. (under contract)
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.

- Cost Consulting: Vermeulens
- Construction Manager-at-Risk: Skanska USA Building, Inc. (under contract)
- Commissioning Agent: Bath Group, Inc. (under contract)
- Technical Campus
 - Program Manager: AECOM Technical Services, Inc. (under contract)
 - A/E: Perkins+Will, Inc. (under contract)
 - Associate Architect: Hoefer Wysocki Architecture
 - MEP: Purdy McGuire
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - Cost Consulting: Vermeulens
 - Construction Manager-at-Risk: McCarthy Building Companies, Inc. (under contract)
 - Commissioning Agent: Farnsworth (under contract)


4.1.2 Phase 2

- Celina Campus
 - Program Manager: AECOM (under contract)
 - A/E: Beck Architecture, LLC (under contract)
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction (under contract)
- Farmersville Campus
 - Program Manager: AECOM (under contract)
 - A/E: Beck Architecture, LLC (under contract)
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction (under contract)
- IT Center
 - Program Manager: AECOM (under contract)
 - A/E: Beck Architecture, LLC (under contract)
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: ME Engineers
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JE Dunn Construction (under contract)

4.1.3 Phase 3

- Welcome Center at the McKinney Campus
 - Program Manager: AECOM Technical Service, Inc. (under contract)
 - A/E: PBK (under contract)
 - Construction Manager-at-Risk: Skanska USA Building, Inc. (under contract)
- Fire Lane and Loop Road/Parking at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc. (under contract)
 - Civil Engineer: RLK Engineering (under contract)
 - Construction Manager-at-Risk: JE Dunn Construction (under contract)
- Additional Projects at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc. (under contract)
 - A/E: Page Southerland Page, Inc. (contract pending)
 - Construction Manager-at-Risk: Skanska USA Building, Inc. (contract pending)
- Additional Projects at McKinney Campus
 - Program Manager: AECOM Technical Service, Inc. (under contract)
 - A/E: PBK (under contract)
 - Construction Manager-at-Risk: Skanska USA Building, Inc. (under contract)
- Trane Upgrades at 5 Existing Campuses
 - Program Manager: AECOM Technical Service, Inc (under contract)
 - Design – Builder: Trane Companies, Inc. (under contract)

4.2 Current Personnel Estimate

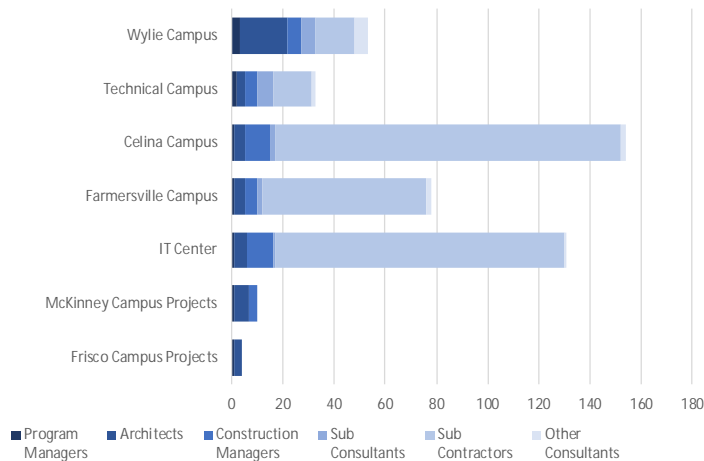

It is estimated that the Program Managers, Architects, Construction Managers, Sub-Consultants, and Sub-Contractors, under contract with Collin College for the 2017 Capital Improvement Program, have 463 employees contributing to the program’s progress.

5.2 Phase 1

Wylie Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	👍	May 16, 2017	✔️
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	👍	May 23, 2017	✔️
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	👍	May 23, 2017	✔️
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	👍	August 22, 2017	✔️
Architect Mobilized	September 12, 2017	September 29, 2017	👎	September 28, 2017	✔️
GMP Construction Documents Submittal	June 26, 2018	June 26, 2018	👍	June 26, 2018	✔️
BOT Approval of GMP	August 28, 2018	August 28, 2018	👍	August 28, 2018	✔️
Contractor Mobilized	September 10, 2018	September 12, 2018	👎	September 12, 2018	✔️
Foundations Complete	May 18, 2019	April 30, 2019	👍	April 23, 2019	✔️
Structures Complete	June 28, 2019	June 28, 2019	👍	May 23, 2019	✔️
Dry-In of Buildings Complete	October 26, 2019	October 26, 2019	👍	October 29, 2019	✔️
Permanent Power Complete	September 17, 2019	September 17, 2019	👍	September 21, 2019	✔️
Interior Finish-Out Complete	May 1, 2020	June 10, 2020	👎	July 1, 2020	✔️
Substantial Completion	June 25, 2020	June 25, 2020	👍	June 30, 2020	✔️
Final Completion	August 23, 2020	November 15, 2020	👎	-	
Student Occupancy	August 2020	August 2020	👍	August 1, 2020	✔️

Technical Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	👍	May 16, 2017	✔️
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	👍	May 23, 2017	✔️
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	👍	May 23, 2017	✔️
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	👍	August 22, 2017	✔️
Architect Mobilized	September 12, 2017	September 29, 2017	👎	September 28, 2017	✔️
GMP Construction Documents Submittal	April 16, 2018	April 16, 2018	👍	April 19, 2018	✔️
BOT Approval of GMP	June 26, 2018	June 26, 2018	👍	June 26, 2018	✔️
Contractor Mobilized	July 6, 2018	July 20, 2018	👎	July 26, 2018	✔️
Foundations Complete	September 23, 2019	September 23, 2019	👍	July 29, 2019	✔️
Structures Complete	November 18, 2019	November 18, 2019	👍	November 13, 2019	✔️
Roofing of Buildings Complete	December 20, 2019	December 20, 2019	👍	December 20, 2019	✔️
Permanent Power Complete	December 15, 2019	January 10, 2020	👎	January 15, 2020	✔️
Building A Punchlist Generated	June 5, 2020	June 12, 2020	👎	June 12, 2020	✔️
Building B Punchlist Generated	June 12, 2020	June 19, 2020	👎	June 19, 2020	✔️
Building C Punchlist Generated	June 30, 2020	July 6, 2020	👎	July 9, 2020	✔️
Building D Punchlist Generated	July 6, 2020	July 20, 2020	👎	July 15, 2020	✔️
Substantial Completion	July 6, 2020	August 10, 2020	👎	August 10, 2020	✔️
Final Completion	September 4, 2020	November 15, 2020	👎	-	
Student Occupancy	August 2020	August 2020	👍	August 8, 2020	✔️

5.3 Phase 2

Celina Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	👤	February 14, 2018	✔️
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	👤	March 27, 2018	✔️
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	👤	March 27, 2018	✔️
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	👤	June 26, 2018	✔️
BOT Approval of Recommended CM Firm	August 2018	August 2018	👤	August 28, 2018	✔️
Architect Mobilized	July 24, 2018	July 24, 2018	👤	July 31, 2018	✔️
Schematic Design Submittal	January 8, 2019	January 15, 2019	👤	January 16, 2019	✔️
Design Development Submittal	April 30, 2019	April 30, 2019	👤	April 26, 2019	✔️
Construction Document Submittal	September 20, 2019	September 20, 2019	👤	September 3, 2019	✔️
Contractor Mobilized	December 2019	December 2019	👤	November 25, 2019	✔️
Foundations Complete	April 9, 2020	April 14, 2020	👤	April 21, 2020	✔️
Structures Complete	July 7, 2020	July 7, 2020	👤	June 9, 2020	✔️
Roofing of Buildings Complete	December 2, 2020	December 2, 2020	👤	-	
Permanent Power Complete	October 7, 2020	October 7, 2020	👤	May 28, 2020	✔️
Interior Finish-Out Complete	May 18, 2021	May 18, 2021	👤	-	
Substantial Completion	July 15, 2021	June 30, 2021	👤	-	
Final Completion	August 12, 2021	August 30, 2021	👤	-	
Student Occupancy	August 2021	August 2021	👤	-	

Farmersville Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	👤	February 14, 2018	✔️
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	👤	March 27, 2018	✔️
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	👤	March 27, 2018	✔️
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	👤	June 26, 2018	✔️
BOT Approval of Recommended CM Firm	August 2018	August 2018	👤	August 28, 2018	✔️
Architect Mobilized	July 24, 2018	July 24, 2018	👤	July 31, 2018	✔️
Schematic Design Submittal	December 20, 2018	December 18, 2018	👤	December 18, 2018	✔️
Design Development Submittal	April 2, 2019	April 19, 2019	👤	April 26, 2019	✔️
Construction Document Submittal	July 25, 2019	August 9, 2019	👤	August 9, 2019	✔️
Contractor Mobilized	November 2019	November 2019	👤	October 21, 2019	✔️
Foundations Complete	March 5, 2020	March 13, 2020	👤	April 2, 2020	✔️
Structures Complete	April 13, 2020	April 13, 2020	👤	April 30, 2020	✔️
Roofing of Buildings Complete	June 29, 2020	June 29, 2020	👤	June 30, 2020	✔️
Permanent Power Complete	June 30, 2020	July 7, 2020	👤	May 4, 2020	✔️
Interior Finish-Out Complete	November 30, 2020	November 30, 2020	👤	-	
Substantial Completion	January 5, 2021	January 5, 2021	👤	-	
Final Completion	February 2, 2021	February 2, 2021	👤	-	
Student Occupancy	August 2021	August 2021	👤	-	

IT Center

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	May 24, 2019	May 24, 2019	↑	May 24, 2019	✓
Design Development Submittal	August 23, 2019	August 23, 2019	↑	August 23, 2019	✓
Construction Document Submittal	December 9, 2019	December 9, 2019	↑	December 9, 2019	✓
Contractor Mobilized	December 2019	January 6, 2020	↓	January 20, 2020	✓
Construction Start for Loop Road/Parking	June 1, 2020	July 13, 2020	↓	July 27, 2020	✓
Foundations Complete	June 22, 2020	June 22, 2020	↑	May 2, 2020	✓
Structures Complete	August 14, 2020	August 14, 2020	↑	July 14, 2020	✓
Phase 1 Construction Complete for Loop Road/Parking	August 15, 2020	August 15, 2020	↑	August 22, 2020	✓
Phase 2 Construction Complete for Loop Road/Parking	October 31, 2020	October 31, 2020	↑		
Roofing of Buildings Complete	November 3, 2020	November 3, 2020	↑	-	
Permanent Power Complete	January 4, 2021	January 4, 2021	↑	-	
Interior Finish-Out Complete	May 13, 2021	May 13, 2021	↑	-	
Substantial Completion	June 30, 2021	July 7, 2021	👉	-	
Final Completion	August 26, 2021	August 26, 2021	↑	-	
Student Occupancy	August 2021	August 2021	↑	-	

* Phase 3 (Loop Road, Fire Lane, and Parking Lot) at Frisco Campus is included in this schedule

5.4 Phase 3

McKinney Campus (Welcome Center and Renovations)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of A/E Procurement Method	October 22, 2019	October 22, 2019	↑	October 22, 2019	✓
BOT Approval of Construction Delivery Method	February 2020	February 2020	↑	October 22, 2019	✓
BOT Approval of Recommended A/E Firm	March 24, 2020	March 24, 2020	↑	April 28, 2020	✓
BOT Approval of Recommended CM Firm	March 24, 2020	March 24, 2020	↑	April 28, 2020	✓
Architect NTP	April 14, 2020	April 14, 2020	↑	April 8, 2020	✓
Schematic Design Submittal	August 1, 2020	August 1, 2020	↑	August 1, 2020	✓
50% Construction Document Submittal	September 5, 2020	September 25, 2020	↓	September 25, 2020	✓
Student Occupancy	January 2022	January 2022	↑	-	

Frisco Campus (Addition and Renovations)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of Recommended AE Firm	June 23, 2020	June 23, 2020	↑	June 23, 2020	✓
BOT Approval of Recommended CM Firm	August 25, 2020	August 25, 2020	↑	August 25, 2020	✓

6. Budget

6.1 Program Summary

Program Wide Budget Summary

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$47,226,570	\$43,090,280	\$41,841,207	\$36,196,681	97%	87%
Investigation, Testing & Verification	\$8,185,410	\$6,922,870	\$5,329,184	\$3,604,637	77%	68%
Construction, Equipment & Furnishings	\$486,561,069	\$501,672,320	\$458,465,002	\$402,572,128	91%	88%
Misc.	\$394,411	\$388,256	\$130,623	\$120,667	34%	92%
Contingency	\$61,621,273	\$22,168,937	\$0	\$0	0%	0%
Total Program Budget	\$600,000,000	\$600,000,000	\$505,766,016	\$442,494,114		
% of Total Program Budget Committed	84.29%					
% of Total Commitments Expended	87.49%					
% of Total Program Budget Expended	73.75%					

6.2 Phase 1

Wylie Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$15,051,440	\$13,514,928	\$13,511,929	\$13,151,014	100%	97%
Investigation, Testing & Verification	\$2,679,247	\$2,084,678	\$1,780,126	\$1,539,947	85%	87%
Construction, Equipment & Furnishings	\$133,174,284	\$150,296,082	\$150,290,694	\$146,667,219	100%	98%
Misc.	\$126,082	\$175,999	\$60,878	\$60,878	35%	100%
Contingency	\$6,571,649	\$13,102	\$0	\$0	0%	0%
Total Project Budget	\$157,602,702	\$166,084,789	\$165,643,627	\$161,419,058		
% of Total Project Budget Committed	99.73%					
% of Total Commitments Expended	97.45%					
% of Total Project Budget Expended	97.19%					

Technical Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$14,713,206	\$13,792,895	\$13,740,617	\$13,360,533	100%	97%
Investigation, Testing & Verification	\$2,619,039	\$1,694,355	\$1,633,265	\$1,154,405	96%	71%
* Construction, Equipment & Furnishings	\$130,181,602	\$161,425,103	\$160,972,168	\$152,686,796	100%	95%
Misc.	\$123,249	\$38,857	\$38,163	\$28,207	98%	74%
Contingency	\$6,423,972	\$171,597	\$0	\$0	0%	0%
Allen ISD Reimbursement	-	(\$12,000,000)	(\$12,000,000)	-		
Allen EDC Grant	-	(\$400,000)	(\$400,000)	-		
Total Project Budget	\$154,061,068	\$164,722,807	\$163,984,213	\$167,229,941		
% of Total Project Budget Committed	99.55%					
% of Total Commitments Expended	101.98%					
% of Total Project Budget Expended	101.52%					

* Actual Budget from bond funds is \$149,025,103 (\$161,425,103 less \$12,000,000 Allen ISD Reimbursement and \$400,000 Allen EDC Grant)

6.3 Phase 2

Celina Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,078,807	\$3,993,544	\$3,961,185	\$2,993,464	99%	76%
Investigation, Testing & Verification	\$936,908	\$936,908	\$585,520	\$260,582	62%	45%
Construction, Equipment & Furnishings	\$46,569,862	\$48,572,753	\$43,546,617	\$25,815,414	90%	59%
Misc.	\$44,090	\$62,092	\$19,124	\$19,124	31%	100%
Contingency	\$2,482,596	\$1,546,966	\$0	\$0	0%	0%
Total Project Budget	\$55,112,263	\$55,112,263	\$48,112,446	\$29,088,583		
% of Total Project Budget Committed	87.30%					
% of Total Commitments Expended	60.46%					
% of Total Project Budget Expended	52.78%					

Farmersville Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,539,404	\$2,185,319	\$2,171,319	\$1,754,455	99%	81%
Investigation, Testing & Verification	\$468,453	\$540,867	\$444,545	\$199,067	82%	45%
Construction, Equipment & Furnishings	\$23,284,932	\$25,219,613	\$23,312,679	\$14,257,127	92%	61%
Misc.	\$22,045	\$26,716	\$5,911	\$5,911	22%	100%
Contingency	\$1,241,298	\$533,618	\$0	\$0	0%	0%
Total Project Budget	\$27,556,132	\$28,506,132	\$25,934,454	\$16,216,560		
% of Total Project Budget Committed	90.98%					
% of Total Commitments Expended	62.53%					
% of Total Project Budget Expended	56.89%					

IT Center

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,472,853	\$4,858,074	\$4,823,265	\$3,334,457	99%	69%
Investigation, Testing & Verification	\$1,009,600	\$1,193,900	\$856,813	\$450,636	72%	53%
Construction, Equipment & Furnishings	\$50,183,042	\$45,473,400	\$39,837,291	\$13,804,622	88%	35%
Misc.	\$47,510	\$53,157	\$5,647	\$5,647	11%	100%
Contingency	\$2,675,210	\$7,411,603	\$0	\$0	0%	0%
Total Project Budget	\$59,388,215	\$58,990,133	\$45,523,016	\$17,595,362		
% of Total Project Budget Committed	77.17%					
% of Total Commitments Expended	38.65%					
% of Total Project Budget Expended	29.83%					

* Project Budget contains funds for Phase 3 (Loop Road and Parking Lot) at Frisco Campus

6.4 Phase 3

McKinney Campus (Welcome Center and Renovations)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$4,370,860	\$4,375,520	\$3,262,892	\$1,251,260	75%	38%
Investigation, Testing & Verification	\$472,163	\$472,163	\$28,915	\$0	6%	0%
Construction, Equipment & Furnishings	\$30,179,816	\$30,179,816	\$0	\$0	0%	0%
Misc.	\$31,435	\$31,435	\$901	\$901	3%	100%
Contingency	\$2,833,454	\$11,470,661	\$0	\$0	0%	0%
Total Project Budget	\$37,887,728	\$46,529,595	\$3,292,708	\$1,252,161		
% of Total Project Budget Committed	7.08%					
% of Total Commitments Expended	38.03%					
% of Total Project Budget Expended	2.69%					

Frisco Campus (Addition and Renovations)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,883,468	\$2,883,468	\$1,746,468	\$60,000	61%	3%
Investigation, Testing & Verification	\$347,015	\$347,015	\$0	\$0	0%	0%
Construction, Equipment & Furnishings	\$16,724,000	\$16,724,000	\$0	\$0	0%	0%
Misc.	\$70,820	\$70,820	\$0	\$0	0%	0%
Contingency	\$1,094,995	\$1,094,995	\$0	\$0	0%	0%
Total Project Budget	\$21,120,298	\$21,120,298	\$1,746,468	\$60,000		
% of Total Project Budget Committed	8.27%					
% of Total Commitments Expended	3.44%					
% of Total Project Budget Expended	0.28%					

Plano Campus (Additional Projects)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Total Project Budget	\$0	\$2,177,541	\$0	\$0		
% of Total Project Budget Committed	0.00%					
% of Total Commitments Expended	0.00%					
% of Total Project Budget Expended	0.00%					

6.5 Phase A

Public Safety Training Center

Budget Group	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Construction Costs	\$31,068,022	\$31,068,022	\$31,068,022	100%	100%
Total Project Budget	\$31,068,022	\$31,068,022	\$31,068,022		

* This project was not managed by AECOM. However, it is included in the report to make a complete report of Bond costs.

Trane Energy PACT

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Frisco Campus	\$9,725,336	\$9,725,336	\$9,725,336	\$7,777,253	100%	80%
Plano Campus	\$6,797,834	\$6,797,834	\$6,797,834	\$5,560,157	100%	82%
McKinney Campus	\$4,044,983	\$4,044,983	\$4,044,983	\$3,705,430	100%	92%
Courtyard Center	\$548,720	\$548,720	\$548,720	\$536,634	100%	98%
Collin Higher Education Center	\$720,659	\$720,659	\$720,659	\$693,453	100%	96%
Total Program Budget	\$21,837,531	\$21,837,531	\$21,837,531	\$18,272,927		
% of Total Project Budget Committed	100.00%					
% of Total Commitments Expended	83.68%					
% of Total Project Budget Expended	83.68%					

6.6 Additional Program Budgets

Program Level

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Building Fund Reimbursement	\$51,150,000	\$0	\$0	\$0	0%	0%
Program Wide Traffic Study	\$0	\$370,000	\$370,000	\$351,500	100%	95%
Program Contingency	\$39,393,094	\$1,021,390	\$0	\$0	0%	0%
Trane PACT Program Management		\$99,500	\$99,500	\$60,000	100%	60%
District Wide Air Cleaning		\$2,259,999	\$2,259,999	\$3,150	100%	0%
District Wide Commissioning		\$100,000	\$19,850	\$17,500	20%	88%
Total Project Budget	\$90,543,094	\$3,850,889	\$370,000	\$351,500		

* Building Fund Reimbursements for Wylie Campus land, Technical Campus land, and Public Safety Training Center construction costs were completed in August '18. Budgets, Commitments and Expenditures for these costs are reflected in each project.

** Program Contingency Original Budget is the result of the balance from the original Phase 3 & 4 projects less the funding for the Frisco Campus Parking Garage, McKinney Campus Welcome Center & Trane Energy PACT projects.

* Additional Phase 3 projects to be funded from Program Contingency

7. Completed Items

7.1 General Program

- [AECOM issued the Monthly Program Report for August '20 to Collin College on September 8th](#)
- [AECOM conducted coordination meetings with the Executive Committee on September 14th and 21st](#)
- [Ribbon Cutting Ceremony was held on September 11th and Open House was held on September 12th for the Technical Campus](#)
- [Ribbon Cutting Ceremony was held on September 25th and Open House was held on September 26th for the Wylie Campus](#)

7.2 Procurement

- [Page Southerland Page, Inc. was issued a PO for Design Services for the Frisco Campus Additions and Renovations on September 30th](#)

7.3 Design

- [AECOM, PBK, and Skanska USA Building, Inc. met for design review meetings for the McKinney Campus Welcome Center on September 2nd, 9th, 16th, 23rd, and 30th](#)
- [Collin College, AECOM, Page Southerland Page, Inc., and Skanska USA Building, Inc. met to discuss Scope of Work for the Frisco Campus Additions and Renovations on September 16th](#)
- [PBK submitted 50% Construction Documents on September 25th for the McKinney Campus Welcome Center.](#)

7.4 Pre-Construction

- No Pre-Construction Items have been completed at this time

7.5 Construction

- Collin College, AECOM, Beck Architecture, LLC, and JT Vaughn Construction conducted Weekly OAC meetings on September 2nd, 9th, 16th, 23rd, and 30th for the Celina Campus
- Collin College, AECOM, Beck Architecture, LLC, and JT Vaughn Construction conducted Weekly OAC meetings on September 3rd, 10th, 17th, and 24th for the Farmersville Campus
- Collin College, AECOM, Beck Architecture, LLC, and JE Dunn Construction conducted an OAC meeting on September 1st, 8th, 15th, 22nd, and 29th for the IT Center at the Frisco Campus

See Appendix A for Construction Progress Photos

7.6 Acceptance and Close-Out

- No Acceptance and Close-Out Phase Items have been completed at this time

8. Pending Items

8.1 General Program

- No General Program items are pending at this time

8.2 Procurement

- Contract pending for Skanska USA Building, Inc. for the Frisco Campus Additions and Renovations, including fire lane

8.3 Design

- Changes as requested by the College SME's have been approved and PBK is working on the Construction Documents for McKinney Campus Welcome Center
- GMP #1 documents, which will include Civil/Site, Dental and Kitchen reno, are scheduled to be issued late October for the McKinney Campus Renovations

8.4 Pre-Construction

- Coordination with the City of Frisco on the permitting/zoning requirements for the work on the Frisco Campus

8.5 Construction

- Final FF&E deliveries, IT installations, and punch list at the Technical Campus
- Final FF&E deliveries, IT installations, and punch list at the Wylie Campus



See Appendix A for Construction Progress Photos

8.6 Acceptance and Close-Out


- Wylie and Technical Campuses achieved Substantial Completion and were accepted by the College in order to start final installation of FF&E and IT equipment in preparation for the Fall 2020 semester. Project close-out activities have begun and are on-going on both projects.

Appendix A – Construction Progress Photos

Technical Campus – Ribbon Cutting Ceremony and Open House

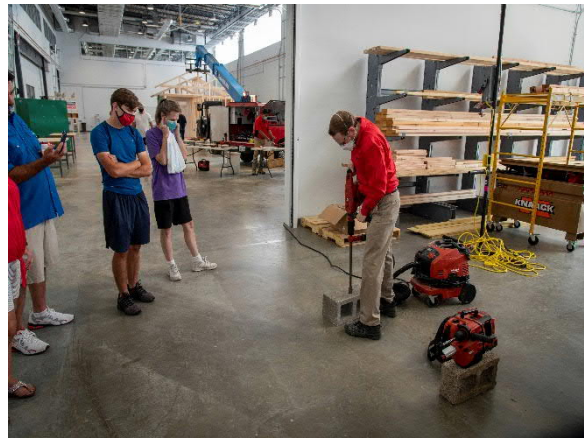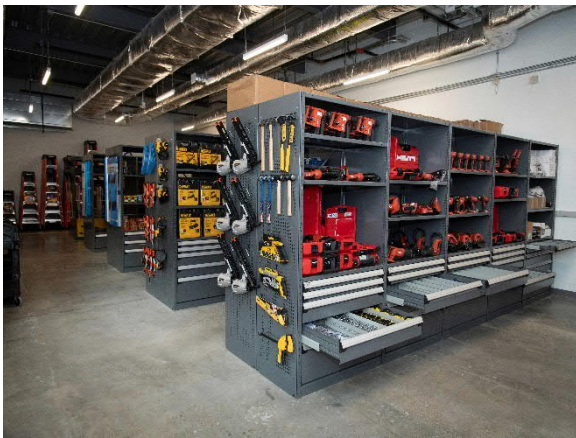


Wylie Campus – Ribbon Cutting Ceremony and Open House

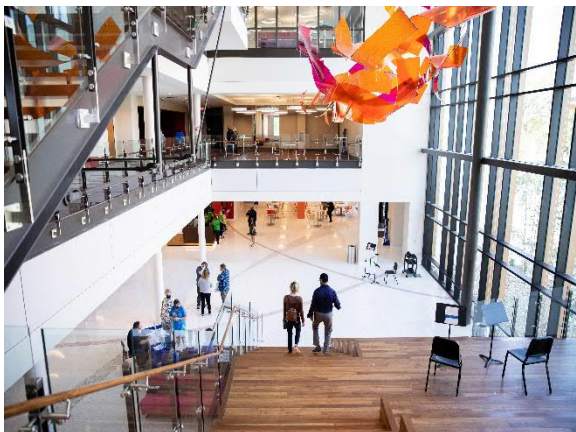

Celina Campus



September '20 Aerial

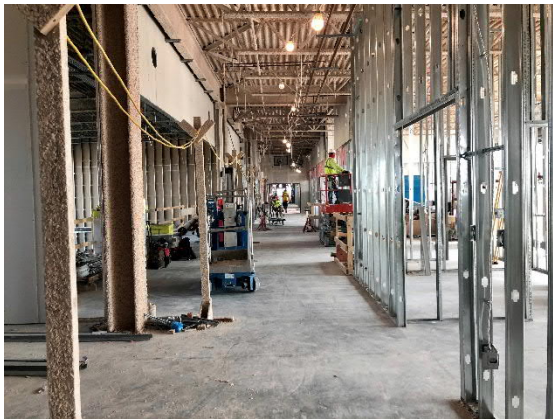

Classroom Space on Level 2 of North Building



NW View of Campus

Farmersville Campus



September '20 Aerial



Commons Area at Main Entry




A&P Lab Space


IT Center at Frisco Campus



September '20 Aerial

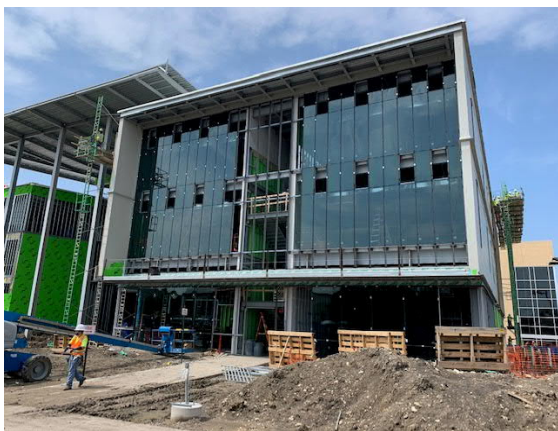

Curtain Wall Install Progress on South Side of Building

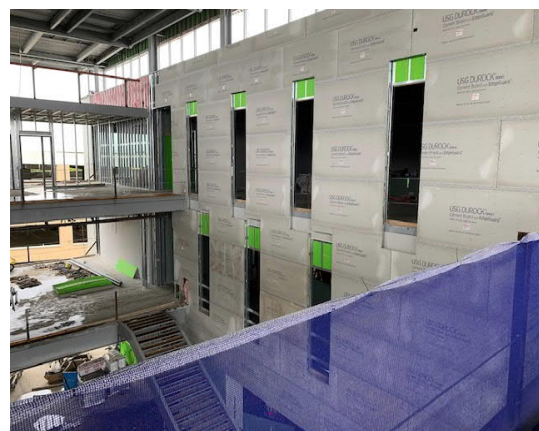

Installation of Atrium Finishes
