



NOTICE is hereby given that the Collin County Community College District Board of Trustees will hold a meeting of the Campus Facilities and Construction Committee (Saad, Moses, and Donald) at 5:00 p.m. on Tuesday, August 16, 2022, in the President's Conference Room 407 at the Collin Higher Education Center, 3452 Spur 399, McKinney, Texas 75069.

Locations

Celina Campus

Collin Higher
Education Center
McKinney, Texas

Courtyard Center
Plano, Texas

Farmersville Campus

Frisco Campus

McKinney Campus

Plano Campus

Public Safety
Training Center
McKinney, Texas

Rockwall Center

Technical Campus
Allen, Texas

Wylie Campus

PUBLIC COMMENT

REVIEW AND DISCUSSION ITEMS

1. Consideration of Approval of Change Order #1 for the Construction Contract with Infinity Contractors at the Plano Campus
2. Consideration of Approval for the District President to Execute a Contract for the Construction of Wind and Rain Abatement and Installation of 15 Welding Booths and Associated Infrastructure at the Technical Campus
3. AECOM Monthly Reports for June and July 2022

*Andrew P. Hardin
Chair, Board of Trustees*

iCollin

www.collin.edu

Board of Trustees

Andrew Hardin, *Chair*

Jay Saad, *Vice Chair*

Jim Orr, *Secretary*

Raj Menon, Ph.D., *Treasurer*

Stacy Anne Arias

J. Robert Collins, Ph.D.

Stacey Donald, Ph.D.

Greg Gomel

Fred Moses

District President

H. Neil Matkin, Ed.D.

3452 Spur 399

P.O. Box 8021

McKinney, Texas 75070

P | 972.758.3800

F | 972.758.3807

nmatkin@collin.edu

www.collin.edu

Collin County Community College District Board of Trustees

1. Campus Facilities and Construction Committee

August 16, 2022

Resource: Christopher G. Eyle
Vice President of Facilities & Construction

DISCUSSION ITEM: Consideration of Approval of Change Order #1 for the Construction Contract with Infinity Contractors at the Plano Campus

DISCUSSION: The construction contract issued to Infinity Contractors for \$6,957,000 had an original scope to replace 16 legacy air handler units (installed in the 1980s) with new units and associated hardware to upgrade the systems to MERV-13 Filters, which would increase filtration level of air and improve HVAC system reliability for a portion of the Plano Campus.

After this contract was issued to Infinity Contractors, further evaluation and design has been completed by RWB Consulting Engineers. It is recommended to replace an additional 13 air handling units, associated piping and connections, and add an additional boiler. This additional scope will increase reliability of the HVAC system for the Plano Campus as well as add much needed heating capacity and redundancy.

The District Staff recommends a change order in the amount of \$6,873,000 to be added to Infinity Contractors' existing contract (\$6,957,000), plus \$500,000 of owner's contingency for a total project amount of \$14,330,000. Funding for the change order is budgeted and available in CARES funds.

Collin County Community College District Board of Trustees

2022-08-2-X

August 23, 2022

Resource: Christopher G. Eyle
Vice President of Facilities & Construction

AGENDA ITEM: Report Out of the Campus Facilities and Construction Committee and Consideration of Approval of Change Order #1 for the Construction Contract with Infinity Contractors at the Plano Campus

DISCUSSION: The construction contract issued to Infinity Contractors for \$6,957,000 had an original scope to replace 16 legacy air handler units (installed in the 1980s) with new units and associated hardware to upgrade the systems to MERV-13 Filters, which would increase filtration level of air and improve HVAC system reliability for a portion of the Plano Campus.

After this contract was issued to Infinity Contractors, further evaluation and design has been completed by RWB Consulting Engineers. It is recommended to replace an additional 13 air handling units, associated piping and connections, and add an additional boiler. This additional scope will increase reliability of the HVAC system for the Plano Campus as well as add much needed heating capacity and redundancy.

The District Staff recommends a change order in the amount of \$6,873,000 to be added to Infinity Contractors' existing contract (\$6,957,000), plus \$500,000 of owner's contingency for a total project amount of \$14,330,000. Funding for the change order is budgeted and available in CARES funds.

DISTRICT PRESIDENT'S RECOMMENDATION: The District President recommends approval of Change Order #1 resulting in a revised contract amount of \$13,830,000 and \$500,000 for contingency for the replacement of legacy air handlers and associated infrastructure at the Plano Campus.

SUGGESTED MOTION: This item comes as a motion and second out of committee. A suggested motion would be, "Mr. Chairman, I make a motion that the Board of Trustees of Collin County Community College District authorizes the District President to execute Infinity Contractors' Change Order #1 resulting in a revised contract amount of \$13,830,000 and \$500,000 for contingency for the replacement of legacy air handlers and associated infrastructure at the Plano Campus."

Collin County Community College District Board of Trustees

2. Campus Facilities and Construction Committee

August 16, 2022

Resource: Christopher G. Eyle
Vice President of Facilities & Construction

DISCUSSION ITEM: Consideration of Approval for the District President to Execute a Contract for the Construction of Wind and Rain Abatement and Installation of 15 Welding Booths and Associated Infrastructure at the Technical Campus

DISCUSSION: The construction of the wind and rain abatement and the installation of 15 welding booths and associated infrastructure was approved at the April 2022 Board of Trustees meeting. In order to save costs in mobilization and ensure coordination, the College bid both efforts in one project.

Formal solicitations were issued and evaluated to determine the contractor. XXX responses were received and subsequently reviewed by the project management staff. The bid submitted by XXXX was the most responsive to the solicitation requirements and is recommended as the District's best value. The estimated cost for this project is \$XXXXXX, which includes a bid amount of \$XXXXXX and \$XXXXXX of owner's contingency. \$XXXXXX is budgeted and available in bond funds for the wind and rain abatement, and \$XXXXXX is budgeted and available in CARES funds for the installation of 15 welding booths and associated infrastructure.

Collin County Community College District Board of Trustees

2022-08-2-X

August 23, 2022

Resource: Christopher G. Eyle
Vice President of Facilities & Construction

AGENDA ITEM: Report Out of the Campus Facilities and Construction Committee and Consideration of Approval for the District President to Execute a Contract for the Construction of Wind and Rain Abatement and Installation of 15 Welding Booths and Associated Infrastructure at the Technical Campus

DISCUSSION: The construction of the wind and rain abatement and the installation of 15 welding booths and associated infrastructure was approved at the April 2022 Board of Trustees Meeting. In order to save costs in mobilization and ensure coordination, the College bid both efforts in one project.

Formal solicitations were issued and evaluated to determine the contractor. XXX responses were received and subsequently reviewed by the project management staff. The bid submitted by XXXX, was the most responsive to the solicitation requirements and is recommended as the District's best value. The estimated cost for this project is \$XXXXX, which includes a bid amount of \$XXXXX and \$XXXXX of owner's contingency. \$XXXXX is budgeted and available in bond funds for the wind and rain abatement, and \$XXXXX is budgeted and available in CARES funds for the installation of 15 welding booths and associated infrastructure.

DISTRICT PRESIDENT'S RECOMMENDATION: The District President recommends approval of XXXX's bid of \$XXXXX and \$XXXXX of owner's contingency, for a total of \$XXXXX for the construction of wind and rain abatement and installation of 15 welding booths and associated infrastructure at the Technical Campus.

SUGGESTED MOTION: This item comes as a motion and second out of committee. A suggested motion would be, "Mr. Chairman, I make a motion that the Board of Trustees of Collin County Community College District approves XXXX's bid in the amount of \$XXXXX and \$XXXXX of owners contingency, for the construction of wind and rain abatement and installation of 15 welding booths and associated infrastructure at the Technical Campus."

Collin County Community College District Board of Trustees

3. Campus Facilities and Construction Committee

August 16, 2022

Resource: Adrian Grimes
AECOM Project Manager

DISCUSSION ITEM: AECOM Monthly Reports for June and July 2022

DISCUSSION: AECOM Project Manager Adrian Grimes will review items on the Collin College 2017 Capital Improvement Program Monthly Reports for June and July 2022.



Collin College

2017 Capital Improvement Program
Monthly Report
June 2022

Collin County Community College District

Project Reference: 60541060
Project Number: 60541060

July 7, 2022

Quality Information

Prepared by



Nuria Cortes
Program Controls Manager

Reviewed by



Jeff Hagerich
Deputy Program Director

Approved By



Adrian Grimes
Program Director

Revision History

Revision	Revision date	Details	Authorized	Name	Position
First Publication	July 07, 2022	June '22 Report	Yes	Adrian Grimes	Program Director

Distribution List

# Hard Copies	PDF Required	Association / Company Name
1		Dr. Neil Matkin / Collin College
1		Chris Eyle / Collin College

Prepared for:

Collin County Community College District
3452 Spur 399
Suite 327
McKinney, TX 75069

Prepared by:

Nuria Cortes
Program Controls Manager
E: ncortes.aecom@collin.edu

AECOM
13355 Noel Road
4th Floor
Dallas TX, 75240
aecom.com

Copyright © 2020 by AECOM

All rights reserved. No part of this copyrighted work may be reproduced, distributed, or transmitted in any form or by any means without the prior written permission of AECOM.

Table of Contents

- 1. Introduction5
- 2. Executive Summary5
- 3. Scope.....6
 - 3.1 Phase 16
 - 3.2 Phase 26
 - 3.3 Phase 37
- 4. Community.....7
 - 4.1 Project Teams7
 - 4.1.1 Phase 17
 - 4.1.2 Phase 28
 - 4.1.3 Phase 39
 - 4.2 Current Personnel Estimate10
 - 4.3 Community Outreach.....10
- 5. Schedule.....11
 - 5.1 Program11
 - 5.2 Phase 111
 - 5.3 Phase 212
 - 5.4 Phase 314
- 6. Budget16
 - 6.1 Program Summary.....16
 - 6.2 Phase 116
 - 6.3 Phase 217
 - 6.4 Phase 318
 - 6.5 Phase A19
 - 6.6 Additional Program Budgets20
- 7. Completed Items.....20
 - 7.1 General Program20
 - 7.2 Procurement.....20
 - 7.3 Design20
 - 7.4 Pre-Construction.....20
 - 7.5 Construction20
 - 7.6 Acceptance and Close-Out.....20
- 8. Pending Items.....21
 - 8.1 General Program21
 - 8.2 Procurement.....21
 - 8.3 Design21
 - 8.4 Pre-Construction.....21
 - 8.5 Construction21
 - 8.6 Acceptance and Close-Out.....21
- Appendix A – Construction Progress Photos.....22

1. Introduction

On May 6, 2017, voters approved Collin College's \$600 million bond proposal to facilitate a long-range plan to accommodate the projected population growth in Collin County over the next two decades. The program consists of 4 new campuses and 2 new facilities.

On May 16, 2017, in a special session, the Board of Trustees granted the District President authority to enter and negotiate into contract with AECOM Technical Services, Inc. (AECOM) to provide Program Management Services to the Collin College 2017 Capital Improvement Program. On May 25, 2017, Collin College issued a Notice to Proceed to AECOM. As part of these services, AECOM will deliver a monthly report to provide status and progress of key aspects of the Program.

2. Executive Summary

The Program is progressing as planned with no major issues to report at this time.

Completed and Pending Items

- [Celina Campus – Financial close-out is ongoing.](#)
- [Farmersville Campus – Financial close-out is ongoing. Drywall repairs are completed in the building.](#)
- [IT Center - Financial close-out is ongoing.](#)
- [Frisco Campus \(Addition and Renovations\) – At Alumni Hall, working on final punch list items. Certificate of Occupancy for new kitchen/dining area was obtained on June 10th. Monument sign instal work is ongoing.](#)
- [McKinney Campus – Welcome Center – Grand staircase terrazzo install is complete. Glass handrails have been installed on the bridge and grand staircase. Interior paint, install of wood panels, carpet, and signage, is on-going. Landscape and hardscape installation is on-going. Fire lane West of the Welcome Center has been poured, as well as the colored concrete and sidewalks.](#)
- [Plano Campus \(Wayfinding\) – Electrical and foundation work for the signs is underway. Installation of directional wayfinding signs has begun.](#)

Items of close attention

- [No items of close attention at this time.](#)

Budget Summary

- [\\$586,781,003 of the \\$614,025,181 has been committed to-date in the form of contracts with various vendors. This represents 95.56% of the overall program budget committed.](#)
- [\\$567,781,450 of the \\$586,781,003 committed amount has been expended to-date. This represents 96.76% of the commitments to date and 92.47% of the program budget.](#)

3. Scope

3.1 Phase 1

- Wylie Campus
 - Construction of a campus on a new approximately 97-acre site
 - The campus includes:
 - Campus Commons
 - Library
 - Student Center/Conference Center
 - Central Utility Plant
- Technical Campus
 - Construction of a Technical Campus on a new 32-acre site in Allen, Texas
 - The campus includes:
 - 450 space underground parking garage
 - Academic Building (includes space for dual credit students)
 - 3 Trade Bar Buildings to support CTE programs

3.2 Phase 2

- Celina Campus
 - Construction of a campus on a new approximately 75-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Farmersville Campus
 - Construction of a campus on a new approximately 76-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Frisco Campus
 - Construction of a new IT Center building on the existing campus

3.3 Phase 3

- Additions and Renovations at Frisco Campus
 - Alumni Hall Renovations and Additions
 - Lawler Hall Renovations
 - Heritage Hall Upgrades
 - Founders Hall Renovations
 - Wayfinding
- Additional Frisco Campus Projects
 - Construction of a new fire lane, parking lot, and loop road on the existing campus
 - Trane Upgrades
- Additions and Renovations at McKinney Campus
 - Construction of a new Welcome Center on the existing campus
 - New Entry Drive and Parking
 - Pistol Range Demo
 - Kitchen and Dining Renovations in Main Building
 - Dental Hygiene Renovations
 - Wayfinding
- Additional McKinney Campus Projects
 - Trane Upgrades
- Additional Plano Campus Projects
 - Trane Upgrades
 - Wayfinding
- Additional Courtyard Center Projects
 - Trane Upgrades
- Additional CHEC Projects
 - Trane Upgrades

4. Community

4.1 Project Teams

4.1.1 Phase 1

- Wylie Campus
 - Program Manager: AECOM Technical Services, Inc.
 - A/E: Page Southerland Page, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.

- Cost Consulting: Vermeulens
- Construction Manager-at-Risk: Skanska USA Building, Inc.
- Commissioning Agent: Bath Group, Inc.
- Technical Campus
 - Program Manager: AECOM Technical Services, Inc.
 - A/E: Perkins+Will, Inc.
 - Associate Architect: Hoefer Wysocki Architecture
 - MEP: Purdy McGuire
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - Cost Consulting: Vermeulens
 - Construction Manager-at-Risk: McCarthy Building Companies, Inc.
 - Commissioning Agent: Farnsworth


4.1.2 Phase 2

- Celina Campus
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction
- Farmersville Campus
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction
- IT Center
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: ME Engineers
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JE Dunn Construction

4.1.3 Phase 3

- Welcome Center at the McKinney Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: PBK
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
 - Commissioning Agent: Bath Group, Inc.
- Loop Road/Parking at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JE Dunn Construction
- Fire Lane at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Additional Projects at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: Page Southerland Page, Inc.
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Additional Projects at McKinney Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: PBK
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Trane Upgrades at 5 Existing Campuses
 - Program Manager: AECOM Technical Service, Inc
 - Design – Builder: Trane Companies, Inc.
- Additional Projects at Plano Campus (Wayfinding)
 - Program Manager: AECOM Technical Service, Inc
 - A/E: IN2 Architects
 - General Contractor: SCC Signs and Lighting

4.2 Current Personnel Estimate

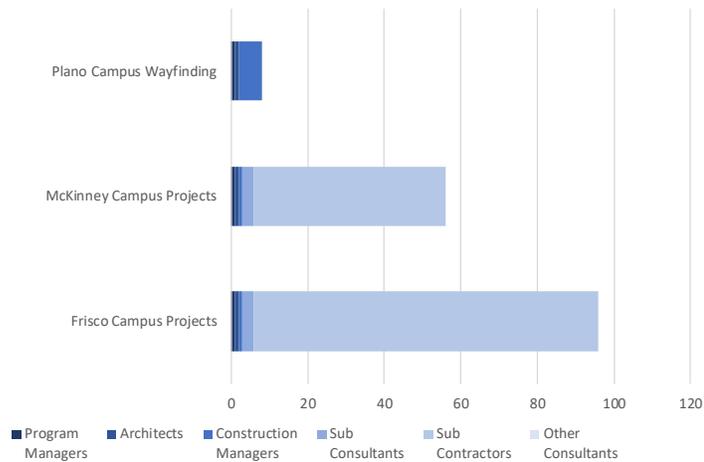


It is estimated that the Program Managers, Architects, Construction Managers, Sub-Consultants, and Sub-Contractors, under contract with Collin College for the 2017 Capital Improvement Program, have 160 employees contributing to the program's progress.

4.3 Community Outreach

- Collin College 2017 Capital Improvement Program Website
 - <https://CollinCollege2017CIP.com>
 - Includes the following features:
 - Program Overview
 - Project Scopes
 - Project Schedules
 - Project Budgets
 - Progress Photos/Renderings
 - Live On-Site Camera Feeds

5. Schedule

5.1 Program

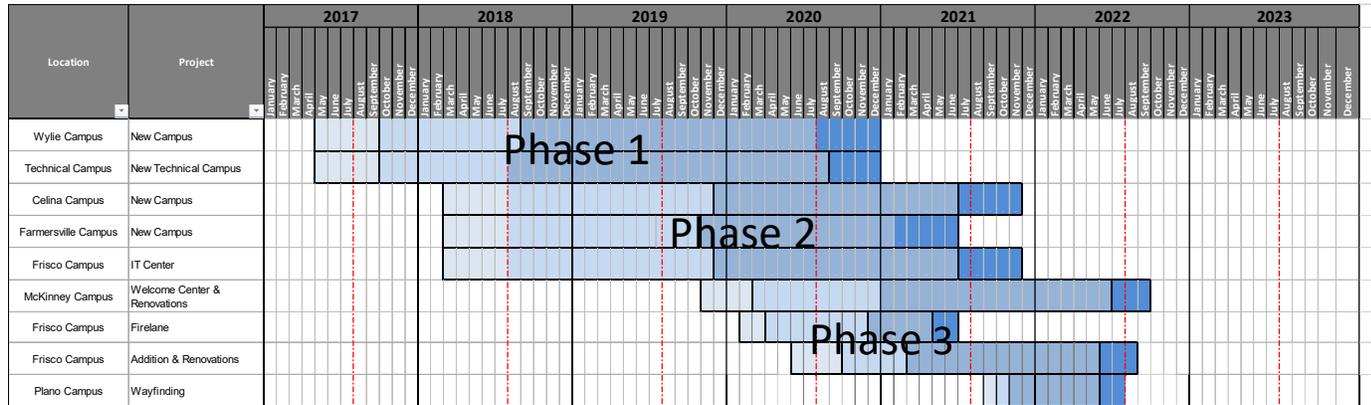

- Planning & Team Selection
- Programming & Design
- Construction
- Final Completion & Close-Out

We Are Here

5.2 Phase 1

Wylie Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	👆	May 16, 2017	✅
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	👆	May 23, 2017	✅
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	👆	May 23, 2017	✅
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	👆	August 22, 2017	✅
Architect Mobilized	September 12, 2017	September 29, 2017	👇	September 28, 2017	✅
GMP Construction Documents Submittal	June 26, 2018	June 26, 2018	👆	June 26, 2018	✅
BOT Approval of GMP	August 28, 2018	August 28, 2018	👆	August 28, 2018	✅
Contractor Mobilized	September 10, 2018	September 12, 2018	👉	September 12, 2018	✅
Foundations Complete	May 18, 2019	April 30, 2019	👆	April 23, 2019	✅
Structures Complete	June 28, 2019	June 28, 2019	👆	May 23, 2019	✅
Dry-In of Buildings Complete	October 26, 2019	October 26, 2019	👆	October 29, 2019	✅
Permanent Power Complete	September 17, 2019	September 17, 2019	👆	September 21, 2019	✅
Interior Finish-Out Complete	May 1, 2020	June 10, 2020	👇	July 1, 2020	✅
Substantial Completion	June 25, 2020	June 25, 2020	👆	June 30, 2020	✅
Final Completion	August 23, 2020	November 2021	👇	November 2021	✅
Student Occupancy	August 2020	August 2020	👆	August 1, 2020	✅

Technical Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	↑	May 16, 2017	✓
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	↑	August 22, 2017	✓
Architect Mobilized	September 12, 2017	September 29, 2017	↓	September 28, 2017	✓
GMP Construction Documents Submittal	April 16, 2018	April 16, 2018	↑	April 19, 2018	✓
BOT Approval of GMP	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
Contractor Mobilized	July 6, 2018	July 20, 2018	👉	July 26, 2018	✓
Foundations Complete	September 23, 2019	September 23, 2019	↑	July 29, 2019	✓
Structures Complete	November 18, 2019	November 18, 2019	↑	November 13, 2019	✓
Roofing of Buildings Complete	December 20, 2019	December 20, 2019	↑	December 20, 2019	✓
Permanent Power Complete	December 15, 2019	January 10, 2020	↓	January 15, 2020	✓
Building A Punchlist Generated	June 5, 2020	June 12, 2020	👉	June 12, 2020	✓
Building B Punchlist Generated	June 12, 2020	June 19, 2020	👉	June 19, 2020	✓
Building C Punchlist Generated	June 30, 2020	July 6, 2020	👉	July 9, 2020	✓
Building D Punchlist Generated	July 6, 2020	July 20, 2020	👉	July 15, 2020	✓
Substantial Completion	July 6, 2020	August 10, 2020	↓	August 10, 2020	✓
Final Completion	September 4, 2020	November 2021	↓	November 2021	✓
Student Occupancy	August 2020	August 2020	↑	August 8, 2020	✓

5.3 Phase 2

Celina Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	January 8, 2019	January 15, 2019	👉	January 16, 2019	✓
Design Development Submittal	April 30, 2019	April 30, 2019	↑	April 26, 2019	✓
Construction Document Submittal	September 20, 2019	September 20, 2019	↑	September 3, 2019	✓
Contractor Mobilized	December 2019	December 2019	↑	November 25, 2019	✓
Foundations Complete	April 9, 2020	April 14, 2020	👉	April 21, 2020	✓
Structures Complete	July 7, 2020	July 7, 2020	↑	June 9, 2020	✓
Roofing of Buildings Complete	December 2, 2020	December 2, 2020	↑	November 13, 2020	✓
Permanent Power Complete	October 7, 2020	October 7, 2020	↑	May 28, 2020	✓
Interior Finish-Out Complete	May 18, 2021	May 18, 2021	↑	May 28, 2021	✓
Substantial Completion	July 15, 2021	June 30, 2021	↑	June 30, 2021	✓
Final Completion	August 12, 2021	August 2022	↓	-	
Student Occupancy	August 2021	August 2021	↑	August 23, 2021	✓

Farmersville Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	December 20, 2018	December 18, 2018	↑	December 18, 2018	✓
Design Development Submittal	April 2, 2019	April 19, 2019	↓	April 26, 2019	✓
Construction Document Submittal	July 25, 2019	August 9, 2019	↓	August 9, 2019	✓
Contractor Mobilized	November 2019	November 2019	↑	October 21, 2019	✓
Foundations Complete	March 5, 2020	March 13, 2020	👉	April 2, 2020	✓
Structures Complete	April 13, 2020	April 13, 2020	↑	April 30, 2020	✓
Roofing of Buildings Complete	June 29, 2020	June 29, 2020	↑	June 30, 2020	✓
Permanent Power Complete	June 30, 2020	July 7, 2020	👉	May 4, 2020	✓
Interior Finish-Out Complete	November 30, 2020	November 30, 2020	↑	December 11, 2020	✓
Substantial Completion	January 5, 2021	January 5, 2021	↑	December 21, 2020	✓
Final Completion	February 2, 2021	August 2022	↓	-	
Student Occupancy	August 2021	March 2021	↑	March 12, 2021	✓

IT Center

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	May 24, 2019	May 24, 2019	↑	May 24, 2019	✓
Design Development Submittal	August 23, 2019	August 23, 2019	↑	August 23, 2019	✓
Construction Document Submittal	December 9, 2019	December 9, 2019	↑	December 9, 2019	✓
Contractor Mobilized	December 2019	January 6, 2020	↓	January 20, 2020	✓
Construction Start for Loop Road/Parking	June 1, 2020	July 13, 2020	↓	July 27, 2020	✓
Foundations Complete	June 22, 2020	June 22, 2020	↑	May 2, 2020	✓
Structures Complete	August 14, 2020	August 14, 2020	↑	July 14, 2020	✓
Phase 1 Construction Complete for Loop Road/Parking	August 15, 2020	August 15, 2020	↑	August 22, 2020	✓
Phase 2 Construction Complete for Loop Road/Parking	October 31, 2020	March 15, 2021	↓	March 15, 2021	✓
Roofing of Buildings Complete	November 3, 2020	November 23, 2020	↓	October 23, 2020	✓
Permanent Power Complete	January 4, 2021	January 4, 2021	↑	January 29, 2021	✓
Interior Finish-Out Complete	May 13, 2021	June 30, 2021	↓	June 30, 2021	✓
Substantial Completion	June 30, 2021	July 7, 2021	👉	July 8, 2021	✓
Final Completion	August 26, 2021	August 2022	↓	-	
Student Occupancy	August 2021	August 2021	↑	August 23, 2021	✓

* Phase 3 (Loop Road and Parking Lot) at Frisco Campus is included in this schedule

5.4 Phase 3

McKinney Campus (Welcome Center and Renovations)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of A/E Procurement Method	October 22, 2019	October 22, 2019	↑	October 22, 2019	✓
BOT Approval of Construction Delivery Method	February 2020	February 2020	↑	October 22, 2019	✓
BOT Approval of Recommended A/E Firm	March 24, 2020	March 24, 2020	↑	April 28, 2020	✓
BOT Approval of Recommended CM Firm	March 24, 2020	March 24, 2020	↑	April 28, 2020	✓
Architect NTP	April 14, 2020	April 14, 2020	↑	April 8, 2020	✓
Schematic Design Submittal	August 1, 2020	August 1, 2020	↑	August 1, 2020	✓
Site Construction Document Submittal	October 2, 2020	October 2, 2020	↑	October 2, 2020	✓
Welcome Center Construction Document Submittal	November 20, 2020	November 20, 2020	↑	October 30, 2020	✓
GMP #1 * Board Approval	December 8, 2020	December 8, 2020	↑	December 8, 2021	✓
GMP #2 ** Board Approval	January 26, 2021	February 23, 2021	↓	January 26, 2021	✓
GMP #1 * Construction Start	January 18, 2021	January 18, 2021	↑	January 28, 2021	✓
GMP #2 ** Construction Start	March 1, 2021	March 1, 2021	↑	March 15, 2021	✓
Site - Phase 1	September 3, 2021	September 3, 2021	↑	August 30, 2021	✓
Site - Phase 2	January 7, 2022	March 11, 2022	↓	March 24, 2022	✓
Site - Core Utilities	January 4, 2022	April 30, 2022	↓	April 30, 2022	✓
Welcome Center Substantial Completion	June 29, 2022	July 22, 2022	↓	-	
Welcome Center Final Completion	July 31, 2022	July 31, 2022	↑	-	
Kitchen Renovation Substantial Completion	December 27, 2021	March 4, 2022	↓	March 31, 2022	✓
Dental Offices Substantial Completion	October 25, 2021	March 24, 2022	↓	March 31, 2022	✓
Dental Lab Substantial Completion	October 5, 2021	January 10, 2022	↓	December 28, 2021	✓
Staff Occupancy	July 2022	August 2022	↓	-	

* GMP #1 Site, Civil, and Demolition for Renovation Work

** GMP #2 Construction of New Welcome Center and Renovation

Frisco Campus (Addition and Renovations)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of Recommended AE Firm	June 23, 2020	June 23, 2020	↑	June 23, 2020	✓
BOT Approval of Recommended CM Firm	August 25, 2020	August 25, 2020	↑	August 25, 2020	✓
Schematic Design Submittal	December 14, 2020	December 14, 2020	↑	December 14, 2020	✓
Construction Document Submittal	March 26, 2021	March 26, 2021	↑	March 26, 2021	✓
GMP #1 * Board Approval	October 27, 2020	October 27, 2020	↑	October 27, 2020	✓
GMP #1 * Construction Start	December 15, 2020	December 15, 2020	↑	December 2, 2020	✓
GMP #2 ** Board Approval	March 2021	April 2021	↓	April 25, 2021	✓
GMP #2 ** Construction Start	April 2021	June 2021	↓	June 7, 2021	✓
Fire Lane Completion	March 2021	October 2021	↓	October 15, 2021	✓
Alumni Hall Start	July 2021	July 2021	↑	July 21, 2021	✓
Alumni Hall Foundations Complete	September 2021	September 2021	↑	September 2021	✓
Alumni Hall Structure Complete	October 2021	November 2021	↓	November 15, 2021	✓
Alumni Hall Roof Complete	November 2021	December 2021	↓	December 30, 2021	✓
Alumni Hall Interior Finish-out	April 2022	April 19, 2022	↓	April 19, 2022	✓
Alumni Hall Substantial Completion	April 2022	April 19, 2022	↓	April 19, 2022	✓
Alumni Hall Final Completion	June 2022	June 2022	↑	June 10, 2022	✓
Heritage Hall Renovations Start	June 21, 2021	June 21, 2021	↑	June 21, 2021	✓
Heritage Hall Substantial Completion	January 2022	January 2022	↑	January 14, 2022	✓
Founders Hall Renovations Start	July 2021	July 15, 2021	👉	July 15, 2021	✓
Founders Hall Substantial Completion	January 2022	January 2022	↑	January 14, 2022	✓
Lawler Hall Building Entrance Start	July 2021	July 15, 2021	👉	July 26, 2021	✓
Lawler Hall Building Entrance Substantial Completion	December 2021	March 16, 2022	↓	March 16, 2022	✓

* GMP #1 Fire Lane

** GMP #2 Alumni Hall Remaining Work, Renovations and Foundation Work

Plano Campus (Wayfinding)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of Recommended Signage Firm	October 26, 2021	October 26, 2021	↑	October 26, 2021	✓
Demo for Wayfinding Signs	March 21, 2022	March 21, 2022	↑	March 21, 2022	✓
Install of Electrical Wiring	May 8, 2022	July 22, 2022	↓	-	
Install of Wayfinding Foundations	April 25, 2022	July 21, 2022	↓	-	
Install of Wayfinding Signs	May 27, 2022	August 18, 2022	↓	-	

6. Budget

6.1 Program Summary

Program Wide Budget Summary

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$50,110,038	\$45,568,512	\$45,450,563	\$45,078,254	100%	99%
Investigation, Testing & Verification	\$8,532,425	\$5,669,732	\$5,257,743	\$4,974,970	93%	95%
Construction, Equipment & Furnishings	\$503,285,069	\$540,675,736	\$535,849,156	\$517,520,086	99%	97%
Misc.	\$465,231	\$257,904	\$223,541	\$208,139	87%	93%
Contingency	\$37,607,237	\$21,853,297	\$0	\$0	0%	0%
Total Program Budget	\$600,000,000	\$614,025,181	\$586,781,003	\$567,781,450		
% of Total Program Budget Committed	95.56%					
% of Total Commitments Expended	96.76%					
% of Total Program Budget Expended	92.47%					

6.2 Phase 1

Wylie Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$15,051,440	\$13,595,304	\$13,595,304	\$13,595,304	100%	100%
Investigation, Testing & Verification	\$2,679,247	\$1,587,529	\$1,587,529	\$1,587,529	100%	100%
Construction, Equipment & Furnishings	\$133,174,284	\$149,385,809	\$149,385,809	\$149,385,809	100%	100%
Misc.	\$126,082	\$61,361	\$61,361	\$61,361	100%	100%
Contingency	\$6,571,649	\$0	\$0	\$0	0%	0%
Total Project Budget	\$157,602,702	\$164,630,003	\$164,630,003	\$164,630,003		
% of Total Project Budget Committed	100.00%					
% of Total Commitments Expended	100.00%					
% of Total Project Budget Expended	100.00%					

Technical Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$14,713,206	\$13,730,909	\$13,730,909	\$13,730,909	100%	100%
Investigation, Testing & Verification	\$2,619,039	\$1,297,502	\$1,297,502	\$1,297,502	100%	100%
* Construction, Equipment & Furnishings	\$130,181,602	\$161,435,093	\$161,435,093	\$161,435,093	100%	100%
Misc.	\$123,249	\$38,501	\$38,501	\$38,501	100%	100%
Contingency	\$6,423,972	\$0	\$0	\$0	0%	0%
Total Project Budget	\$154,061,068	\$176,502,005	\$176,502,005	\$176,502,005		
Allen ISD Reimbursement	-	(\$12,000,000)	(\$12,000,000)	-		
Allen EDC Grant	-	(\$400,000)	(\$400,000)	-		
% of Total Project Budget Committed	100.00%					
% of Total Commitments Expended	100.00%					
% of Total Project Budget Expended	100.00%					

* Actual Budget from bond funds is \$149,035,093 (\$161,435,093 less \$12,000,000 Allen ISD Reimbursement and \$400,000 Allen EDC Grant)

6.3 Phase 2**Celina Campus**

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,078,807	\$3,996,375	\$3,996,375	\$3,996,375	100%	100%
Investigation, Testing & Verification	\$936,908	\$533,109	\$533,109	\$533,109	100%	100%
Construction, Equipment & Furnishings	\$46,569,862	\$47,979,970	\$44,863,007	\$44,785,845	94%	100%
Misc.	\$44,090	\$21,260	\$21,260	\$21,260	100%	100%
Contingency	\$2,482,596	\$4,206,729	\$0	\$0	0%	0%
Total Project Budget	\$55,112,263	\$56,737,444	\$49,413,752	\$49,336,590		
% of Total Project Budget Committed	87.09%					
% of Total Commitments Expended	99.84%					
% of Total Project Budget Expended	86.96%					

Farmersville Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,539,404	\$2,188,394	\$2,188,394	\$2,188,289	100%	100%
Investigation, Testing & Verification	\$468,453	\$352,478	\$352,478	\$352,478	100%	100%
Construction, Equipment & Furnishings	\$23,284,932	\$25,523,160	\$25,410,679	\$21,773,893	100%	86%
Misc.	\$22,045	\$6,107	\$6,107	\$6,107	100%	100%
Contingency	\$1,241,298	\$435,993	\$0	\$0	0%	0%
Total Project Budget	\$27,556,132	\$28,506,132	\$27,957,658	\$24,320,767		
% of Total Project Budget Committed	98.08%					
% of Total Commitments Expended	86.99%					
% of Total Project Budget Expended	85.32%					

IT Center

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,472,853	\$4,873,547	\$4,873,547	\$4,846,569	100%	99%
Investigation, Testing & Verification	\$1,009,600	\$842,333	\$842,333	\$821,562	100%	98%
Construction, Equipment & Furnishings	\$50,183,042	\$46,025,015	\$45,385,296	\$40,919,157	99%	90%
Misc.	\$47,510	\$10,487	\$10,487	\$10,487	100%	100%
Contingency	\$2,675,210	\$5,218,011	\$0	\$0	0%	0%
Total Project Budget	\$59,388,215	\$56,969,393	\$51,111,663	\$46,597,775		
% of Total Project Budget Committed	89.72%					
% of Total Commitments Expended	91.17%					
% of Total Project Budget Expended	81.79%					

* Project Budget contains funds for Phase 3 (Loop Road and Parking Lot) at Frisco Campus

6.4 Phase 3**McKinney Campus (Welcome Center and Renovations)**

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$4,370,860	\$4,512,820	\$4,486,018	\$4,338,980	99%	97%
Investigation, Testing & Verification	\$472,163	\$553,973	\$353,788	\$188,234	64%	53%
Construction, Equipment & Furnishings	\$30,179,816	\$38,994,104	\$38,186,454	\$31,495,319	98%	82%
Misc.	\$31,435	\$32,476	\$11,367	\$2,845	35%	25%
Contingency	\$2,833,454	\$2,886,222	\$0	\$0	0%	0%
Total Project Budget	\$37,887,728	\$46,979,595	\$43,037,627	\$36,025,379		
% of Total Project Budget Committed	91.61%					
% of Total Commitments Expended	83.71%					
% of Total Project Budget Expended	76.68%					

Frisco Campus (Addition and Renovations)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,883,468	\$2,097,152	\$2,006,005	\$1,876,828	96%	94%
Investigation, Testing & Verification	\$347,015	\$460,793	\$248,989	\$170,932	54%	69%
Construction, Equipment & Furnishings	\$16,724,000	\$16,962,367	\$16,831,958	\$14,161,385	99%	84%
Misc.	\$70,820	\$78,211	\$64,957	\$58,077	83%	89%
Contingency	\$1,094,995	\$3,342,515	\$0	\$0	0%	0%
Total Project Budget	\$21,120,298	\$22,941,038	\$19,151,910	\$16,267,222		
% of Total Project Budget Committed	83.48%					
% of Total Commitments Expended	84.94%					
% of Total Project Budget Expended	70.91%					

Plano Campus (Additional Projects)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$0	\$123,011	\$123,011	\$54,000	100%	44%
Investigation, Testing & Verification	\$0	\$24,515	\$24,515	\$6,125	100%	25%
Construction, Equipment & Furnishings	\$0	\$789,665	\$789,665	\$71,502	100%	9%
Misc.	\$0	\$0	\$0	\$0	0%	0%
Contingency	\$0	\$1,240,350	\$0	\$0	0%	0%
Total Project Budget	\$0	\$2,177,541	\$937,191	\$131,627		
% of Total Project Budget Committed		43.04%				
% of Total Commitments Expended		14.04%				
% of Total Project Budget Expended		6.04%				

6.5 Phase A**Public Safety Training Center**

Budget Group	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
PSTC Construction	\$31,068,022	\$31,068,022	\$31,068,022	100%	100%
PSTC Parking Addition	\$675,000	\$655,641	\$586,529	97%	89%
Total Project Budget	\$31,743,022	\$31,723,663	\$31,654,551		

* This project was not managed by AECOM. However, it is included in the report to make a complete report of Bond costs.

Trane Energy PACT

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Frisco Campus	\$9,725,336	\$9,725,336	\$9,725,336	\$9,725,336	100%	100%
Plano Campus	\$6,797,834	\$6,797,834	\$6,797,834	\$6,797,834	100%	100%
McKinney Campus	\$4,044,983	\$4,044,983	\$4,044,983	\$4,044,983	100%	100%
Courtyard Center	\$548,720	\$548,720	\$548,720	\$548,720	100%	100%
Collin Higher Education Center	\$720,659	\$720,659	\$720,659	\$720,659	100%	100%
Total Program Budget	\$21,837,531	\$21,837,531	\$21,837,531	\$21,837,531		
% of Total Project Budget Committed		100.00%				
% of Total Commitments Expended		100.00%				
% of Total Project Budget Expended		100.00%				

6.6 Additional Program Budgets

Program Level

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Building Fund Reimbursement	\$51,150,000	\$0	\$0	\$0	0%	0%
Program Wide Traffic Study	\$0	\$351,500	\$351,500	\$351,500	100%	100%
Program Contingency	\$39,393,094	\$4,523,477	\$0	\$0	0%	0%
Trane PACT Program Management		\$99,500	\$99,500	\$99,500	100%	100%
Bond Fees		\$9,500	\$9,500	\$9,500	100%	100%
District Wide Commissioning		\$17,500	\$17,500	\$17,500	100%	100%
Total Project Budget	\$90,543,094	\$5,001,477	\$478,000	\$478,000		

* Building Fund Reimbursements for Wylie Campus land, Technical Campus land, and Public Safety Training Center construction costs were completed in August '18. Budgets, Commitments and Expenditures for these costs are reflected in each project.

** Program Contingency Original Budget is the result of the balance from the original Phase 3 & 4 projects less the funding for the Frisco Campus Parking Garage, McKinney Campus Welcome Center & Trane Energy PACT projects.

* Additional Phase 3 projects to be funded from Program Contingency

7. Completed Items

7.1 General Program

- [AECOM issued the Monthly Program Report for May '22 to Collin College on June 7th](#)

7.2 Procurement

- No Procurement Items have been completed at this time

7.3 Design

- No Design Items have been completed at this time

7.4 Pre-Construction

- No Pre-Construction Items have been completed at this time

7.5 Construction

- [Collin College, AECOM, Page Southerland Page, Inc., and Skanska USA Building, Inc. conducted Weekly OAC meetings on June 1st and 15th for the Frisco Campus Addition and Renovations](#)
- [Collin College, AECOM, PBK, and Skanska USA Building, Inc. conducted Weekly OAC meetings on June 7th, 14th, 21st, and 28th for the McKinney Campus Addition and Renovations](#)
- [Obtained Final Certificate of Occupancy for the Alumni Hall Renovations/Additions at Frisco Campus](#)

[See Appendix A for Construction Progress Photos](#)

7.6 Acceptance and Close-Out

- No Acceptance and Close-Out items are pending at this time

8. Pending Items

8.1 General Program

- No General Program items are pending at this time

8.2 Procurement

- No Procurement items are pending at this time

8.3 Design

- No Design items are pending at this time

8.4 Pre-Construction

- No Pre-Construction items are pending at this time

8.5 Construction

- [Obtain Final Certificate of Occupancy for McKinney Campus Welcome Center](#)
[See Appendix A for Construction Progress Photos](#)

8.6 Acceptance and Close-Out

- [Final close-out activities are nearing completion for the Phase 2 projects](#)

Appendix A – Construction Progress Photos

Welcome Center, Parking Lot, and Renovations at McKinney Campus



Sidewalks and Colored Concrete Poured




Atrium Bridge, North View




Corridor Outside of Vet Lounge on 2nd Floor



Multi-Purpose Room

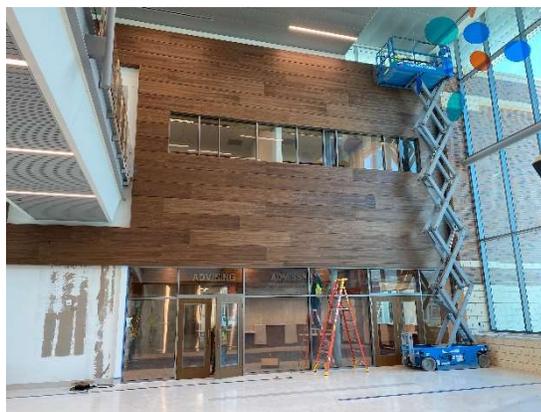

Entry to Transaction Area

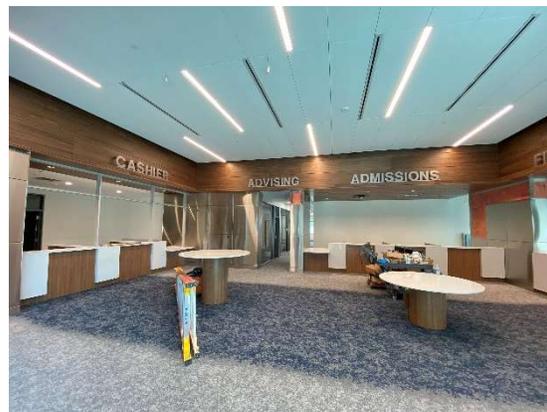

Transaction Area

Wayfinding at Plano Campus



Steel Tube for Directional Wayfinding Sign



Tube and Foundation for Wayfinding Signage

Collin College

2017 Capital Improvement Program
Monthly Report
July 2022

Collin County Community College District

Project Reference: 60541060
Project Number: 60541060

August 8, 2022


Quality Information

Prepared by



Nuria Cortes
Program Controls Manager

Reviewed by



Jeff Hagerich
Deputy Program Director

Approved By



Adrian Grimes
Program Director

Revision History

Revision	Revision date	Details	Authorized	Name	Position
First Publication	August 08, 2022	July '22 Report	Yes	Adrian Grimes	Program Director

Distribution List

# Hard Copies	PDF Required	Association / Company Name
	1	Dr. Neil Matkin / Collin College
	1	Chris Eyle / Collin College

Prepared for:

Collin County Community College District
3452 Spur 399
Suite 327
McKinney, TX 75069

Prepared by:

Nuria Cortes
Program Controls Manager
E: ncortes.aecom@collin.edu

AECOM
13355 Noel Road
4th Floor
Dallas TX, 75240
aecom.com

Copyright © 2020 by AECOM

All rights reserved. No part of this copyrighted work may be reproduced, distributed, or transmitted in any form or by any means without the prior written permission of AECOM.

Table of Contents

- 1. Introduction5
- 2. Executive Summary5
- 3. Scope.....6
 - 3.1 Phase 16
 - 3.2 Phase 26
 - 3.3 Phase 37
- 4. Community.....7
 - 4.1 Project Teams7
 - 4.1.1 Phase 17
 - 4.1.2 Phase 28
 - 4.1.3 Phase 39
 - 4.2 Current Personnel Estimate10
 - 4.3 Community Outreach.....10
- 5. Schedule.....11
 - 5.1 Program11
 - 5.2 Phase 111
 - 5.3 Phase 212
 - 5.4 Phase 314
- 6. Budget16
 - 6.1 Program Summary.....16
 - 6.2 Phase 116
 - 6.3 Phase 217
 - 6.4 Phase 318
 - 6.5 Phase A19
 - 6.6 Additional Program Budgets20
- 7. Completed Items.....20
 - 7.1 General Program20
 - 7.2 Procurement.....20
 - 7.3 Design20
 - 7.4 Pre-Construction.....21
 - 7.5 Construction21
 - 7.6 Acceptance and Close-Out.....21
- 8. Pending Items.....21
 - 8.1 General Program21
 - 8.2 Procurement.....21
 - 8.3 Design21
 - 8.4 Pre-Construction.....21
 - 8.5 Construction21
 - 8.6 Acceptance and Close-Out.....21
- Appendix A – Construction Progress Photos.....22

1. Introduction

On May 6, 2017, voters approved Collin College's \$600 million bond proposal to facilitate a long-range plan to accommodate the projected population growth in Collin County over the next two decades. The program consists of 4 new campuses and 2 new facilities.

On May 16, 2017, in a special session, the Board of Trustees granted the District President authority to enter and negotiate into contract with AECOM Technical Services, Inc. (AECOM) to provide Program Management Services to the Collin College 2017 Capital Improvement Program. On May 25, 2017, Collin College issued a Notice to Proceed to AECOM. As part of these services, AECOM will deliver a monthly report to provide status and progress of key aspects of the Program.

2. Executive Summary

The Program is progressing as planned with no major issues to report at this time.

Completed and Pending Items

- [Celina Campus – Financial close-out is ongoing.](#)
- [Farmersville Campus – Financial close-out is ongoing.](#)
- [IT Center - Financial close-out is ongoing.](#)
- [Frisco Campus \(Addition and Renovations\) – Vehicular, pedestrian and Building ID signs have been installed. Monument sign wall and brick installation is complete. Both boilers at Culinary Art have been replaced. ADA modifications began with handicapped parking spaces at Founders Hall and Heritage Hall, where concrete was demoed.](#)
- [McKinney Campus – Welcome Center –Landscape and hardscape installation is 98% complete. All concrete work is complete. Currently completing punchlist and performing final inspections of the building.](#)
- [Plano Campus \(Wayfinding\) – 97% of vehicular, pedestrian, and Building ID signs are installed. Three monument signs foundations and walls were formed and poured.](#)

Items of close attention

- [No items of close attention at this time.](#)

Budget Summary

- [\\$586,825,800 of the \\$614,025,181 has been committed to-date in the form of contracts with various vendors. This represents 95.57% of the overall program budget committed.](#)
- [\\$569,738,769 of the \\$586,825,800 committed amount has been expended to-date. This represents 97.09% of the commitments to date and 92.79% of the program budget.](#)

3. Scope

3.1 Phase 1

- Wylie Campus
 - Construction of a campus on a new approximately 97-acre site
 - The campus includes:
 - Campus Commons
 - Library
 - Student Center/Conference Center
 - Central Utility Plant
- Technical Campus
 - Construction of a Technical Campus on a new 32-acre site in Allen, Texas
 - The campus includes:
 - 450 space underground parking garage
 - Academic Building (includes space for dual credit students)
 - 3 Trade Bar Buildings to support CTE programs

3.2 Phase 2

- Celina Campus
 - Construction of a campus on a new approximately 75-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Farmersville Campus
 - Construction of a campus on a new approximately 76-acre site
 - The campus includes:
 - Student Union / Workforce / Instructional Building
- Frisco Campus
 - Construction of a new IT Center building on the existing campus

3.3 Phase 3

- Additions and Renovations at Frisco Campus
 - Alumni Hall Renovations and Additions
 - Lawler Hall Renovations
 - Heritage Hall Upgrades
 - Founders Hall Renovations
 - Wayfinding
- Additional Frisco Campus Projects
 - Construction of a new fire lane, parking lot, and loop road on the existing campus
 - Trane Upgrades
- Additions and Renovations at McKinney Campus
 - Construction of a new Welcome Center on the existing campus
 - New Entry Drive and Parking
 - Pistol Range Demo
 - Kitchen and Dining Renovations in Main Building
 - Dental Hygiene Renovations
 - Wayfinding
- Additional McKinney Campus Projects
 - Trane Upgrades
- Additional Plano Campus Projects
 - Trane Upgrades
 - Wayfinding
- Additional Courtyard Center Projects
 - Trane Upgrades
- Additional CHEC Projects
 - Trane Upgrades

4. Community

4.1 Project Teams

4.1.1 Phase 1

- Wylie Campus
 - Program Manager: AECOM Technical Services, Inc.
 - A/E: Page Southerland Page, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.

- Cost Consulting: Vermeulens
- Construction Manager-at-Risk: Skanska USA Building, Inc.
- Commissioning Agent: Bath Group, Inc.
- Technical Campus
 - Program Manager: AECOM Technical Services, Inc.
 - A/E: Perkins+Will, Inc.
 - Associate Architect: Hoefer Wysocki Architecture
 - MEP: Purdy McGuire
 - Civil Engineer: Pacheco Koch Consulting Engineers, Inc.
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - Cost Consulting: Vermeulens
 - Construction Manager-at-Risk: McCarthy Building Companies, Inc.
 - Commissioning Agent: Farnsworth


4.1.2 Phase 2

- Celina Campus
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction
- Farmersville Campus
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: Reed, Wells, Benson & Co.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JT Vaughn Construction
- IT Center
 - Program Manager: AECOM
 - A/E: Beck Architecture, LLC
 - Structural Engineer: L.A. Fuess Partners, Inc.
 - MEP: ME Engineers
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JE Dunn Construction

4.1.3 Phase 3

- Welcome Center at the McKinney Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: PBK
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
 - Commissioning Agent: Bath Group, Inc.
- Loop Road/Parking at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: JE Dunn Construction
- Fire Lane at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - Civil Engineer: RLK Engineering
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Additional Projects at Frisco Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: Page Southerland Page, Inc.
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Additional Projects at McKinney Campus
 - Program Manager: AECOM Technical Service, Inc.
 - A/E: PBK
 - Construction Manager-at-Risk: Skanska USA Building, Inc.
- Trane Upgrades at 5 Existing Campuses
 - Program Manager: AECOM Technical Service, Inc
 - Design – Builder: Trane Companies, Inc.
- Additional Projects at Plano Campus (Wayfinding)
 - Program Manager: AECOM Technical Service, Inc
 - A/E: IN2 Architects
 - General Contractor: SCC Signs and Lighting
- New Monument Signs
 - Program Manager: AECOM Technical Service, Inc
 - A/E: PBK
 - General Contractor: Skanska USA Building, Inc.

4.2 Current Personnel Estimate

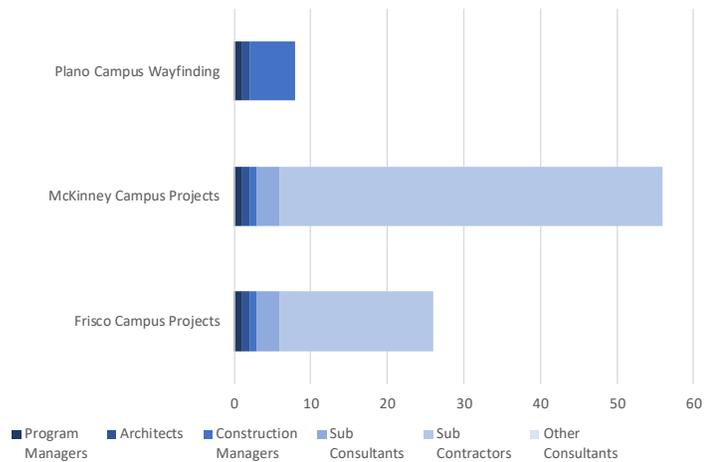


It is estimated that the Program Managers, Architects, Construction Managers, Sub-Consultants, and Sub-Contractors, under contract with Collin College for the 2017 Capital Improvement Program, have 90 employees contributing to the program's progress.

4.3 Community Outreach

- Collin College 2017 Capital Improvement Program Website
 - <https://CollinCollege2017CIP.com>
 - Includes the following features:
 - Program Overview
 - Project Scopes
 - Project Schedules
 - Project Budgets
 - Progress Photos/Renderings
 - Live On-Site Camera Feeds

5. Schedule

5.1 Program

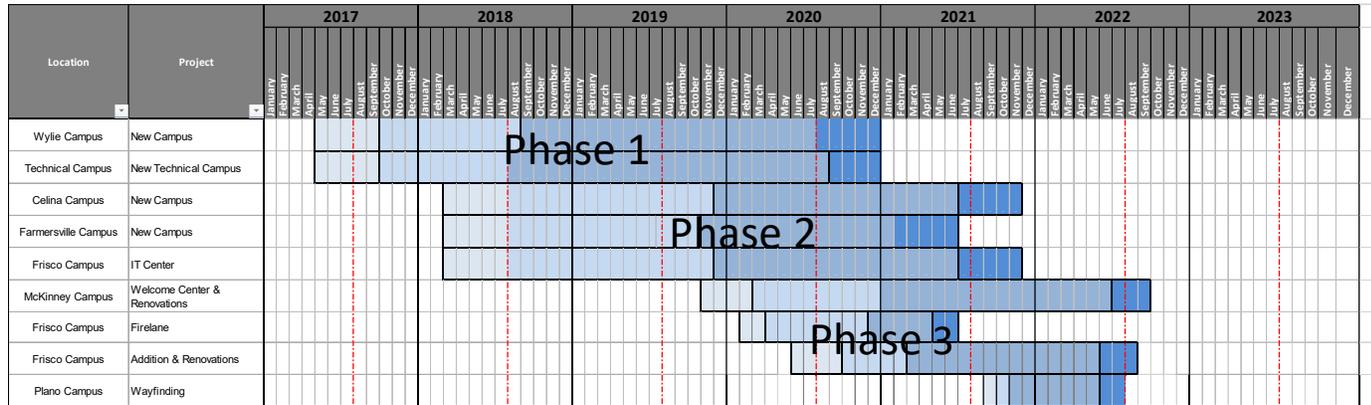

- Planning & Team Selection
- Programming & Design
- Construction
- Final Completion & Close-Out

We Are Here

5.2 Phase 1

Wylie Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	👆	May 16, 2017	✅
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	👆	May 23, 2017	✅
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	👆	May 23, 2017	✅
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	👆	August 22, 2017	✅
Architect Mobilized	September 12, 2017	September 29, 2017	👇	September 28, 2017	✅
GMP Construction Documents Submittal	June 26, 2018	June 26, 2018	👆	June 26, 2018	✅
BOT Approval of GMP	August 28, 2018	August 28, 2018	👆	August 28, 2018	✅
Contractor Mobilized	September 10, 2018	September 12, 2018	👉	September 12, 2018	✅
Foundations Complete	May 18, 2019	April 30, 2019	👆	April 23, 2019	✅
Structures Complete	June 28, 2019	June 28, 2019	👆	May 23, 2019	✅
Dry-In of Buildings Complete	October 26, 2019	October 26, 2019	👆	October 29, 2019	✅
Permanent Power Complete	September 17, 2019	September 17, 2019	👆	September 21, 2019	✅
Interior Finish-Out Complete	May 1, 2020	June 10, 2020	👇	July 1, 2020	✅
Substantial Completion	June 25, 2020	June 25, 2020	👆	June 30, 2020	✅
Final Completion	August 23, 2020	November 2021	👇	November 2021	✅
Student Occupancy	August 2020	August 2020	👆	August 1, 2020	✅

Technical Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	May 16, 2017	May 16, 2017	↑	May 16, 2017	✓
BOT Approval of A/E Procurement Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Construction Delivery Method	May 23, 2017	May 23, 2017	↑	May 23, 2017	✓
BOT Approval of Recommended Firms	August 22, 2017	August 22, 2017	↑	August 22, 2017	✓
Architect Mobilized	September 12, 2017	September 29, 2017	↓	September 28, 2017	✓
GMP Construction Documents Submittal	April 16, 2018	April 16, 2018	↑	April 19, 2018	✓
BOT Approval of GMP	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
Contractor Mobilized	July 6, 2018	July 20, 2018	👉	July 26, 2018	✓
Foundations Complete	September 23, 2019	September 23, 2019	↑	July 29, 2019	✓
Structures Complete	November 18, 2019	November 18, 2019	↑	November 13, 2019	✓
Roofing of Buildings Complete	December 20, 2019	December 20, 2019	↑	December 20, 2019	✓
Permanent Power Complete	December 15, 2019	January 10, 2020	↓	January 15, 2020	✓
Building A Punchlist Generated	June 5, 2020	June 12, 2020	👉	June 12, 2020	✓
Building B Punchlist Generated	June 12, 2020	June 19, 2020	👉	June 19, 2020	✓
Building C Punchlist Generated	June 30, 2020	July 6, 2020	👉	July 9, 2020	✓
Building D Punchlist Generated	July 6, 2020	July 20, 2020	👉	July 15, 2020	✓
Substantial Completion	July 6, 2020	August 10, 2020	↓	August 10, 2020	✓
Final Completion	September 4, 2020	November 2021	↓	November 2021	✓
Student Occupancy	August 2020	August 2020	↑	August 8, 2020	✓

5.3 Phase 2

Celina Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	January 8, 2019	January 15, 2019	👉	January 16, 2019	✓
Design Development Submittal	April 30, 2019	April 30, 2019	↑	April 26, 2019	✓
Construction Document Submittal	September 20, 2019	September 20, 2019	↑	September 3, 2019	✓
Contractor Mobilized	December 2019	December 2019	↑	November 25, 2019	✓
Foundations Complete	April 9, 2020	April 14, 2020	👉	April 21, 2020	✓
Structures Complete	July 7, 2020	July 7, 2020	↑	June 9, 2020	✓
Roofing of Buildings Complete	December 2, 2020	December 2, 2020	↑	November 13, 2020	✓
Permanent Power Complete	October 7, 2020	October 7, 2020	↑	May 28, 2020	✓
Interior Finish-Out Complete	May 18, 2021	May 18, 2021	↑	May 28, 2021	✓
Substantial Completion	July 15, 2021	June 30, 2021	↑	June 30, 2021	✓
Final Completion	August 12, 2021	August 2022	↓	-	
Student Occupancy	August 2021	August 2021	↑	August 23, 2021	✓

Farmersville Campus

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	December 20, 2018	December 18, 2018	↑	December 18, 2018	✓
Design Development Submittal	April 2, 2019	April 19, 2019	↓	April 26, 2019	✓
Construction Document Submittal	July 25, 2019	August 9, 2019	↓	August 9, 2019	✓
Contractor Mobilized	November 2019	November 2019	↑	October 21, 2019	✓
Foundations Complete	March 5, 2020	March 13, 2020	👉	April 2, 2020	✓
Structures Complete	April 13, 2020	April 13, 2020	↑	April 30, 2020	✓
Roofing of Buildings Complete	June 29, 2020	June 29, 2020	↑	June 30, 2020	✓
Permanent Power Complete	June 30, 2020	July 7, 2020	👉	May 4, 2020	✓
Interior Finish-Out Complete	November 30, 2020	November 30, 2020	↑	December 11, 2020	✓
Substantial Completion	January 5, 2021	January 5, 2021	↑	December 21, 2020	✓
Final Completion	February 2, 2021	August 2022	↓	-	
Student Occupancy	August 2021	March 2021	↑	March 12, 2021	✓

IT Center

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	September 25, 2018	February 14, 2018	↑	February 14, 2018	✓
BOT Approval of A/E Procurement Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Construction Delivery Method	September 25, 2018	March 27, 2018	↑	March 27, 2018	✓
BOT Approval of Recommended A/E Firm	June 26, 2018	June 26, 2018	↑	June 26, 2018	✓
BOT Approval of Recommended CM Firm	August 2018	August 2018	↑	August 28, 2018	✓
Architect Mobilized	July 24, 2018	July 24, 2018	↑	July 31, 2018	✓
Schematic Design Submittal	May 24, 2019	May 24, 2019	↑	May 24, 2019	✓
Design Development Submittal	August 23, 2019	August 23, 2019	↑	August 23, 2019	✓
Construction Document Submittal	December 9, 2019	December 9, 2019	↑	December 9, 2019	✓
Contractor Mobilized	December 2019	January 6, 2020	↓	January 20, 2020	✓
Construction Start for Loop Road/Parking	June 1, 2020	July 13, 2020	↓	July 27, 2020	✓
Foundations Complete	June 22, 2020	June 22, 2020	↑	May 2, 2020	✓
Structures Complete	August 14, 2020	August 14, 2020	↑	July 14, 2020	✓
Phase 1 Construction Complete for Loop Road/Parking	August 15, 2020	August 15, 2020	↑	August 22, 2020	✓
Phase 2 Construction Complete for Loop Road/Parking	October 31, 2020	March 15, 2021	↓	March 15, 2021	✓
Roofing of Buildings Complete	November 3, 2020	November 23, 2020	↓	October 23, 2020	✓
Permanent Power Complete	January 4, 2021	January 4, 2021	↑	January 29, 2021	✓
Interior Finish-Out Complete	May 13, 2021	June 30, 2021	↓	June 30, 2021	✓
Substantial Completion	June 30, 2021	July 7, 2021	👉	July 8, 2021	✓
Final Completion	August 26, 2021	August 2022	↓	-	
Student Occupancy	August 2021	August 2021	↑	August 23, 2021	✓

* Phase 3 (Loop Road and Parking Lot) at Frisco Campus is included in this schedule

5.4 Phase 3

McKinney Campus (Welcome Center and Renovations)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of A/E Procurement Method	October 22, 2019	October 22, 2019	↑	October 22, 2019	✓
BOT Approval of Construction Delivery Method	February 2020	February 2020	↑	October 22, 2019	✓
BOT Approval of Recommended A/E Firm	March 24, 2020	March 24, 2020	↑	April 28, 2020	✓
BOT Approval of Recommended CM Firm	March 24, 2020	March 24, 2020	↑	April 28, 2020	✓
Architect NTP	April 14, 2020	April 14, 2020	↑	April 8, 2020	✓
Schematic Design Submittal	August 1, 2020	August 1, 2020	↑	August 1, 2020	✓
Site Construction Document Submittal	October 2, 2020	October 2, 2020	↑	October 2, 2020	✓
Welcome Center Construction Document Submittal	November 20, 2020	November 20, 2020	↑	October 30, 2020	✓
GMP #1 * Board Approval	December 8, 2020	December 8, 2020	↑	December 8, 2021	✓
GMP #2 ** Board Approval	January 26, 2021	February 23, 2021	↓	January 26, 2021	✓
GMP #1 * Construction Start	January 18, 2021	January 18, 2021	↑	January 28, 2021	✓
GMP #2 ** Construction Start	March 1, 2021	March 1, 2021	↑	March 15, 2021	✓
Site - Phase 1	September 3, 2021	September 3, 2021	↑	August 30, 2021	✓
Site - Phase 2	January 7, 2022	March 11, 2022	↓	March 24, 2022	✓
Site - Core Utilities	January 4, 2022	April 30, 2022	↓	April 30, 2022	✓
Welcome Center Substantial Completion	June 29, 2022	August 12, 2022	↓	-	
Welcome Center Final Completion	July 31, 2022	August 31, 2022	↓	-	
Kitchen Renovation Substantial Completion	December 27, 2021	March 4, 2022	↓	March 31, 2022	✓
Dental Offices Substantial Completion	October 25, 2021	March 24, 2022	↓	March 31, 2022	✓
Dental Lab Substantial Completion	October 5, 2021	January 10, 2022	↓	December 28, 2021	✓
Staff Occupancy	July 2022	August 2022	↓	-	

* GMP #1 Site, Civil, and Demolition for Renovation Work

** GMP #2 Construction of New Welcome Center and Renovation

Frisco Campus (Addition and Renovations)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of Recommended AE Firm	June 23, 2020	June 23, 2020	↑	June 23, 2020	✓
BOT Approval of Recommended CM Firm	August 25, 2020	August 25, 2020	↑	August 25, 2020	✓
Schematic Design Submittal	December 14, 2020	December 14, 2020	↑	December 14, 2020	✓
Construction Document Submittal	March 26, 2021	March 26, 2021	↑	March 26, 2021	✓
GMP #1 * Board Approval	October 27, 2020	October 27, 2020	↑	October 27, 2020	✓
GMP #1 * Construction Start	December 15, 2020	December 15, 2020	↑	December 2, 2020	✓
GMP #2 ** Board Approval	March 2021	April 2021	↓	April 25, 2021	✓
GMP #2 ** Construction Start	April 2021	June 2021	↓	June 7, 2021	✓
Fire Lane Completion	March 2021	October 2021	↓	October 15, 2021	✓
Alumni Hall Start	July 2021	July 2021	↑	July 21, 2021	✓
Alumni Hall Foundations Complete	September 2021	September 2021	↑	September 2021	✓
Alumni Hall Structure Complete	October 2021	November 2021	↓	November 15, 2021	✓
Alumni Hall Roof Complete	November 2021	December 2021	↓	December 30, 2021	✓
Alumni Hall Interior Finish-out	April 2022	April 19, 2022	↓	April 19, 2022	✓
Alumni Hall Substantial Completion	April 2022	April 19, 2022	↓	April 19, 2022	✓
Alumni Hall Final Completion	June 2022	June 2022	↑	June 10, 2022	✓
Heritage Hall Renovations Start	June 21, 2021	June 21, 2021	↑	June 21, 2021	✓
Heritage Hall Substantial Completion	January 2022	January 2022	↑	January 14, 2022	✓
Founders Hall Renovations Start	July 2021	July 15, 2021	👉	July 15, 2021	✓
Founders Hall Substantial Completion	January 2022	January 2022	↑	January 14, 2022	✓
Lawler Hall Building Entrance Start	July 2021	July 15, 2021	👉	July 26, 2021	✓
Lawler Hall Building Entrance Substantial Completion	December 2021	March 16, 2022	↓	March 16, 2022	✓

* GMP #1 Fire Lane

** GMP #2 Alumni Hall Remaining Work, Renovations and Foundation Work

Plano Campus (Wayfinding)

Activity	Baseline Finish	Planned Finish		Actual Finish	
BOT Approval of Program Manager	August 27, 2019	August 27, 2019	↑	August 27, 2019	✓
BOT Approval of Recommended Signage Firm	October 26, 2021	October 26, 2021	↑	October 26, 2021	✓
Demo for Wayfinding Signs	March 21, 2022	March 21, 2022	↑	March 21, 2022	✓
Install of Electrical Wiring	May 8, 2022	August 10, 2022	↓	-	
Install of Wayfinding Foundations	April 25, 2022	August 11, 2022	↓	-	
Install of Wayfinding Signs	May 27, 2022	August 18, 2022	↓	-	

6. Budget

6.1 Program Summary

Program Wide Budget Summary

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$50,141,038	\$45,599,512	\$45,450,563	\$45,179,732	100%	99%
Investigation, Testing & Verification	\$8,546,425	\$5,683,732	\$5,257,743	\$4,999,787	93%	95%
Construction, Equipment & Furnishings	\$503,393,069	\$540,786,736	\$535,893,953	\$519,351,110	99%	97%
Misc.	\$465,231	\$254,904	\$223,541	\$208,139	88%	93%
Contingency	\$37,807,237	\$21,700,297	\$0	\$0	0%	0%
Total Program Budget	\$600,000,000	\$614,025,181	\$586,825,800	\$569,738,769		
% of Total Program Budget Committed	95.57%					
% of Total Commitments Expended	97.09%					
% of Total Program Budget Expended	92.79%					

6.2 Phase 1

Wylie Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$15,051,440	\$13,595,304	\$13,595,304	\$13,595,304	100%	100%
Investigation, Testing & Verification	\$2,679,247	\$1,587,529	\$1,587,529	\$1,587,529	100%	100%
Construction, Equipment & Furnishings	\$133,174,284	\$149,385,809	\$149,385,809	\$149,385,809	100%	100%
Misc.	\$126,082	\$61,361	\$61,361	\$61,361	100%	100%
Contingency	\$6,571,649	\$0	\$0	\$0	0%	0%
Total Project Budget	\$157,602,702	\$164,630,003	\$164,630,003	\$164,630,003		
% of Total Project Budget Committed	100.00%					
% of Total Commitments Expended	100.00%					
% of Total Project Budget Expended	100.00%					

Technical Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$14,713,206	\$13,730,909	\$13,730,909	\$13,730,909	100%	100%
Investigation, Testing & Verification	\$2,619,039	\$1,297,502	\$1,297,502	\$1,297,502	100%	100%
* Construction, Equipment & Furnishings	\$130,181,602	\$161,435,093	\$161,435,093	\$161,435,093	100%	100%
Misc.	\$123,249	\$38,501	\$38,501	\$38,501	100%	100%
Contingency	\$6,423,972	\$0	\$0	\$0	0%	0%
Total Project Budget	\$154,061,068	\$176,502,005	\$176,502,005	\$176,502,005		
Allen ISD Reimbursement	-	(\$12,000,000)	(\$12,000,000)	-		
Allen EDC Grant	-	(\$400,000)	(\$400,000)	-		
% of Total Project Budget Committed	100.00%					
% of Total Commitments Expended	100.00%					
% of Total Project Budget Expended	100.00%					

* Actual Budget from bond funds is \$149,035,093 (\$161,435,093 less \$12,000,000 Allen ISD Reimbursement and \$400,000 Allen EDC Grant)

6.3 Phase 2**Celina Campus**

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,078,807	\$3,996,375	\$3,996,375	\$3,996,375	100%	100%
Investigation, Testing & Verification	\$936,908	\$533,109	\$533,109	\$533,109	100%	100%
Construction, Equipment & Furnishings	\$46,569,862	\$47,979,970	\$44,863,007	\$44,785,845	94%	100%
Misc.	\$44,090	\$21,260	\$21,260	\$21,260	100%	100%
Contingency	\$2,482,596	\$4,206,729	\$0	\$0	0%	0%
Total Project Budget	\$55,112,263	\$56,737,444	\$49,413,752	\$49,336,590		
% of Total Project Budget Committed	87.09%					
% of Total Commitments Expended	99.84%					
% of Total Project Budget Expended	86.96%					

Farmersville Campus

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,539,404	\$2,188,394	\$2,188,394	\$2,188,289	100%	100%
Investigation, Testing & Verification	\$468,453	\$352,478	\$352,478	\$352,478	100%	100%
Construction, Equipment & Furnishings	\$23,284,932	\$25,523,160	\$25,410,679	\$21,773,893	100%	86%
Misc.	\$22,045	\$6,107	\$6,107	\$6,107	100%	100%
Contingency	\$1,241,298	\$435,993	\$0	\$0	0%	0%
Total Project Budget	\$27,556,132	\$28,506,132	\$27,957,658	\$24,320,767		
% of Total Project Budget Committed	98.08%					
% of Total Commitments Expended	86.99%					
% of Total Project Budget Expended	85.32%					

IT Center

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$5,472,853	\$4,873,547	\$4,873,547	\$4,870,887	100%	100%
Investigation, Testing & Verification	\$1,009,600	\$842,333	\$842,333	\$821,562	100%	98%
Construction, Equipment & Furnishings	\$50,183,042	\$46,025,015	\$45,385,296	\$40,919,157	99%	90%
Misc.	\$47,510	\$10,487	\$10,487	\$10,487	100%	100%
Contingency	\$2,675,210	\$5,218,011	\$0	\$0	0%	0%
Total Project Budget	\$59,388,215	\$56,969,393	\$51,111,663	\$46,622,092		
% of Total Project Budget Committed	89.72%					
% of Total Commitments Expended	91.22%					
% of Total Project Budget Expended	81.84%					

* Project Budget contains funds for Phase 3 (Loop Road and Parking Lot) at Frisco Campus

6.4 Phase 3**McKinney Campus (Welcome Center and Renovations)**

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$4,370,860	\$4,512,820	\$4,486,018	\$4,359,980	99%	97%
Investigation, Testing & Verification	\$472,163	\$553,973	\$353,788	\$188,234	64%	53%
Construction, Equipment & Furnishings	\$30,179,816	\$38,997,104	\$38,228,185	\$32,531,151	98%	85%
Misc.	\$31,435	\$29,476	\$11,367	\$2,845	39%	25%
Contingency	\$2,833,454	\$2,886,222	\$0	\$0	0%	0%
Total Project Budget	\$37,887,728	\$46,979,595	\$43,079,358	\$37,082,211		
% of Total Project Budget Committed	91.70%					
% of Total Commitments Expended	86.08%					
% of Total Project Budget Expended	78.93%					

Frisco Campus (Addition and Renovations)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$2,883,468	\$2,097,152	\$2,006,005	\$1,910,988	96%	95%
Investigation, Testing & Verification	\$347,015	\$460,793	\$248,989	\$195,748	54%	79%
Construction, Equipment & Furnishings	\$16,724,000	\$16,962,367	\$16,835,024	\$14,579,314	99%	87%
Misc.	\$70,820	\$78,211	\$64,957	\$58,077	83%	89%
Contingency	\$1,094,995	\$3,342,515	\$0	\$0	0%	0%
Total Project Budget	\$21,120,298	\$22,941,038	\$19,154,976	\$16,744,128		
% of Total Project Budget Committed	83.50%					
% of Total Commitments Expended	87.41%					
% of Total Project Budget Expended	72.99%					

Plano Campus (Additional Projects)

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$0	\$123,011	\$123,011	\$76,000	100%	62%
Investigation, Testing & Verification	\$0	\$24,515	\$24,515	\$6,125	100%	25%
Construction, Equipment & Furnishings	\$0	\$789,665	\$789,665	\$448,766	100%	57%
Misc.	\$0	\$0	\$0	\$0	0%	0%
Contingency	\$0	\$1,240,350	\$0	\$0	0%	0%
Total Project Budget	\$0	\$2,177,541	\$937,191	\$530,891		
% of Total Project Budget Committed		43.04%				
% of Total Commitments Expended		56.65%				
% of Total Project Budget Expended		24.38%				

New Monument Signs

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Management, Design, & Pre-Construction	\$31,000	\$31,000	\$0	\$0	0%	0%
Investigation, Testing & Verification	\$14,000	\$14,000	\$0	\$0	0%	0%
Construction, Equipment & Furnishings	\$108,000	\$108,000	\$0	\$0	0%	0%
Misc.	\$0	\$0	\$0	\$0	0%	0%
Contingency	\$200,000	\$47,000	\$0	\$0	0%	0%
Total Project Budget	\$353,000	\$200,000	\$0	\$0		
% of Total Project Budget Committed		0.00%				
% of Total Commitments Expended		0.00%				
% of Total Project Budget Expended		0.00%				

6.5 Phase A**Public Safety Training Center**

Budget Group	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
PSTC Construction	\$31,068,022	\$31,068,022	\$31,068,022	100%	100%
PSTC Parking Addition	\$675,000	\$655,641	\$586,529	97%	89%
Total Project Budget	\$31,743,022	\$31,723,663	\$31,654,551		

* This project was not managed by AECOM. However, it is included in the report to make a complete report of Bond costs.

Trane Energy PACT

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	& of Budget Committed	% of Commitment Expended
Frisco Campus	\$9,725,336	\$9,725,336	\$9,725,336	\$9,725,336	100%	100%
Plano Campus	\$6,797,834	\$6,797,834	\$6,797,834	\$6,797,834	100%	100%
McKinney Campus	\$4,044,983	\$4,044,983	\$4,044,983	\$4,044,983	100%	100%
Courtyard Center	\$548,720	\$548,720	\$548,720	\$548,720	100%	100%
Collin Higher Education Center	\$720,659	\$720,659	\$720,659	\$720,659	100%	100%
Total Program Budget	\$21,837,531	\$21,837,531	\$21,837,531	\$21,837,531		

% of Total Project Budget Committed **100.00%**

% of Total Commitments Expended **100.00%**

% of Total Project Budget Expended **100.00%**

6.6 Additional Program Budgets**Program Level**

Budget Group	Original Budget	Current Budget	Commitments	Expenditures	% of Budget Committed	% of Commitment Expended
Building Fund Reimbursement	\$51,150,000	\$0	\$0	\$0	0%	0%
Program Wide Traffic Study	\$0	\$351,500	\$351,500	\$351,500	100%	100%
Program Contingency	\$39,393,094	\$4,323,477	\$0	\$0	0%	0%
Trane PACT Program Management		\$99,500	\$99,500	\$99,500	100%	100%
Bond Fees		\$9,500	\$9,500	\$9,500	100%	100%
District Wide Commissioning		\$17,500	\$17,500	\$17,500	100%	100%
Total Project Budget	\$90,543,094	\$4,801,477	\$478,000	\$478,000		

* Building Fund Reimbursements for Wylie Campus land, Technical Campus land, and Public Safety Training Center construction costs were completed in August '18. Budgets, Commitments and Expenditures for these costs are reflected in each project.

** Program Contingency Original Budget is the result of the balance from the original Phase 3 & 4 projects less the funding for the Frisco Campus Parking Garage, McKinney Campus Welcome Center & Trane Energy PACT projects.

* Additional Phase 3 projects to be funded from Program Contingency

7. Completed Items**7.1 General Program**

- [AECOM issued the Monthly Program Report for June '22 to Collin College on July 7th](#)

7.2 Procurement

- No Procurement Items have been completed at this time

7.3 Design

- No Design Items have been completed at this time

7.4 Pre-Construction

- No Pre-Construction Items have been completed at this time

7.5 Construction

- Collin College, AECOM, Page Southerland Page, Inc., and Skanska USA Building, Inc. conducted Weekly OAC meetings on July 13th for the Frisco Campus Addition and Renovations
- Collin College, AECOM, PBK, and Skanska USA Building, Inc. conducted Weekly OAC meetings on July 5th, 12th, 19th, and 26th for the McKinney Campus Addition and Renovations
- AECOM held an electrical discussion meeting with Collin College Facilities on July 12th for the Frisco Campus

See Appendix A for Construction Progress Photos

7.6 Acceptance and Close-Out

- No Acceptance and Close-Out items are pending at this time

8. Pending Items

8.1 General Program

- No General Program items are pending at this time

8.2 Procurement

- No Procurement items are pending at this time

8.3 Design

- No Design items are pending at this time

8.4 Pre-Construction

- No Pre-Construction items are pending at this time

8.5 Construction

- Obtain Final Certificate of Occupancy for McKinney Campus Welcome Center
- ADA renovations for Friso Campus

See Appendix A for Construction Progress Photos

8.6 Acceptance and Close-Out

- Final close-out activities are nearing completion for the Phase 2 projects

Appendix A – Construction Progress Photos

Welcome Center at McKinney Campus



Entry Landscaping



Selfie Wall



Veteran's Lounge



Testing Center



First Floor of Atrium



Transaction Area

Wayfinding at Plano Campus



Building ID Signs



Drilling Piers at Spring Creek Sign
